

Lower Duwamish Waterway Group

Port of Seattle / City of Seattle / King County / The Boeing Company

REMEDIAL DESIGN WORK PLAN FOR THE LOWER DUWAMISH WATERWAY MIDDLE REACH

FINAL

For submittal to

The U.S. Environmental Protection Agency

Region 10

Seattle, WA

December 2, 2022

Prepared by



1201 3rd Ave. • Suite 2600
Seattle, Washington • 981019

in association
with



200 First Avenue West • Suite 500
Seattle, Washington • 98119

TABLE OF CONTENTS

1	Introduction	1
1.1	Remedial Design Work Plan Objectives	1
1.2	Remedial Design Work Plan Overview.....	2
1.3	Site Description.....	2
1.4	Selected Remedy Summary.....	3
1.5	General Approach to Contracting, Construction, Operation, Maintenance, and Monitoring for the Middle Reach	4
1.5.1	Contracting	5
1.5.2	Construction	5
1.5.3	Maintenance and Monitoring, and Institutional Controls	5
1.6	Remedial Design Project Management.....	7
1.6.1	Agency Oversight and Stakeholder Process	7
1.6.2	Respondent Team Organization, Responsibilities, and Authorities.....	7
1.6.3	Communications.....	8
2	Existing Information Review	10
2.1	Physical Conditions.....	12
2.1.1	Geology and Hydrogeology.....	12
2.1.2	Geomorphology.....	13
2.1.3	Bathymetry.....	14
2.1.4	Hydrodynamics and Sediment Transport	15
2.1.5	Stratigraphy and Geotechnical Characteristics	18
2.1.6	Infrastructure.....	19
2.1.7	Banks	19
2.1.8	Debris.....	21
2.1.9	Dredged Areas in the LDW Middle Reach.....	22
2.2	Sediment Chemistry Information.....	22
2.3	Previous and Ongoing Remedial Investigations and Actions.....	23
2.3.1	Early Action Areas.....	23
2.3.2	Enhanced Natural Recovery/Activated Carbon Pilot Study	25
2.3.3	Lessons Learned.....	26
2.4	Existing Habitat Conditions in Middle Reach	30
2.5	Waterway Usage in Middle Reach	31
2.5.1	Tribal Use and Treaty Rights	31

2.5.2	Beach Play and Tribal Clamming Areas	32
2.5.3	Public Access Points	32
2.5.4	Waterway Users.....	32
2.5.5	Federal Navigation Channel.....	33
2.6	Data Gaps Identification.....	34
3	Engineering Design Process.....	36
3.1	Design Objectives	36
3.2	Design Process	36
3.2.1	Pre-Design Investigation Phases.....	36
3.2.2	Remedial Design Phases.....	38
3.2.3	Design Process Sequencing	39
3.2.4	Design Quality Control.....	40
3.3	Remedial Action Area Designation	40
3.4	Recovery Category Finalization.....	41
3.5	Remedial Technologies Assignments.....	42
3.6	Sediment Management Areas Designation	42
3.7	Remedial Technologies Design Considerations	43
3.7.1	Dredging.....	43
3.7.2	Capping.....	52
3.7.3	Enhanced Natural Recovery	56
3.7.4	Monitored Natural Recovery.....	56
3.7.5	In Situ Treatment.....	57
3.8	Habitat Design Considerations.....	57
3.9	Other Design Considerations	58
3.9.1	Climate Change.....	58
3.9.2	Sea Level Rise.....	58
3.9.3	Hydrodynamics	58
3.9.4	Sediment Load.....	59
3.9.5	Design Approach.....	59
3.9.6	Green Remediation.....	59
3.9.7	Waterfront Facility Operational Considerations and Construction Sequencing	60
3.10	Pre-Construction and Construction Submittals.....	61
4	Remedial Design Support Activities.....	63
4.1	Pre-Design Investigation Activities.....	63
4.2	Base Mapping.....	64

4.3	Hydrodynamic Information	64
4.4	Zero-Rise Evaluation	65
4.5	Transload Facility Requirements.....	65
4.6	Potential Water Quality Impacts.....	66
4.7	Dredged Material Management.....	66
4.8	Waste Characterization	67
4.9	Clean Material Source Identification.....	67
4.10	Archaeological, Cultural, and Historic Surveys	67
4.11	Tracking Changes in the Middle Reach During Design.....	68
4.12	Source Control Integration.....	68
4.13	Site Access.....	69
4.14	Documenting Substantive Compliance with Applicable or Relevant and Appropriate Requirements.....	70
4.15	Permitting.....	70
5	Middle Reach Physical Conceptual Site Model and Expected Outcomes from Remedial Action	72
5.1	Sediment Sources.....	74
5.2	Sediment Transport.....	74
5.3	Remedial Action Effects on the Physical Conceptual Site Model	75
5.3.1	Dredging	75
5.3.2	Capping.....	76
5.3.3	Enhanced Natural Recovery	76
5.3.4	Monitored Natural Recovery.....	76
5.4	Anticipated Short-Term and Long-Term Post-Remediation Outcomes.....	76
5.4.1	Enhanced Natural Recovery, Capping, and Backfill Placement Areas.....	77
5.4.2	Dredged Areas.....	77
5.4.3	Areas Adjacent to Dredging.....	78
6	Remedial Design Deliverables	79
6.1	Pre-Remedial Design Deliverables	79
6.1.1	Pre-Design Investigation Quality Assurance Project Plans	79
6.1.2	Pre-Design Investigation Health and Safety Plan	79
6.1.3	Pre-Design Investigation Data	79
6.1.4	Pre-Design Investigation Data Evaluation Report	82
6.2	Remedial Design Deliverables.....	82
6.2.1	Preliminary (30%) Remedial Design	82

6.2.2	Intermediate (60%) Remedial Design.....	85
6.2.3	Pre-Final (90%) Remedial Design.....	85
6.2.4	Final (100%) Remedial Design.....	86
7	Remedial Design Project Schedule.....	87
8	References	90

TABLES

Table 1-1	Key Personnel and Support Contractors.....	8
Table 2-1	Overview of Areas Depicted in the ROD in the Middle Reach (RMs 1.6 to 3.0)...	11
Table 2-2	Summary of Early Action Areas, ENR/AC Pilot and Other Sediment Remediation Site Lessons Learned	27
Table 6-1	Remedial Design Elements.....	80
Table 7-1	LDW Middle Reach Remedial Design Project Schedule.....	87

FIGURES

Figure 1-1	LDW Remedial Design Coordination.....	9
Figure 2-1	Total Sediment Mass Balance Based on STM Predictions for 21-Year Period.....	17
Figure 3-1	LDW Middle Reach Remedial Design Timeline.....	37
Figure 3-2	Dredge Residuals Schematic	50
Figure 5-1	Physical Conceptual Site Model of Sediment Movement in the Middle Reach ..	73
Figure 7-1	Project Schedule	88

MAPS

Map 1-1	LDW Superfund Site Vicinity Map
Map 1-2	Middle Reach Vicinity Map
Map 1-3	2021 Bathymetric Conditions and Federal Navigation Channel Authorized Depth Reaches
Map 2-1	Bank Conditions
Map 2-2	Infrastructure
Map 2-3	Early Action Areas and Upland Listed Cleanup Sites
Map 2-4	Parks and Habitat Restoration, Beach Play, and Potential Clamming Areas
Map 4-1	Land Ownership

APPENDICES

Appendix A	Excerpts from Lower Duwamish Waterway Superfund Site Record of Decision
Appendix B	Excerpt from Final Feasibility Study, Lower Duwamish Waterway
Appendix C	Pre-Design Investigation Work Plan

ABBREVIATIONS

AC	activated carbon
AOC	Administrative Order on Consent
AOC2	Second Amendment to the Administrative Order on Consent
AOC3	Third Amendment to the Administrative Order on Consent
AOC4	Fourth Amendment to the Administrative Order on Consent
AOC5	Fifth Amendment to the Administrative Order on Consent
ARAR	applicable or relevant and appropriate requirement
BA	biological assessment
BMP	best management practice
BODR	Basis of Design Report
CERCLA	Comprehensive Environmental Response, Compensation, and Liability Act
Cm	centimeter
COC	contaminant of concern
CQAP	Construction Quality Assurance Plan
CSI	Construction Specification Institute
CSM	conceptual site model
CSO	combined sewer overflow
DQO	data quality objective
EAA	early action area
EBDRP	Elliott Bay/Duwamish Restoration Program
Ecology	Washington State Department of Ecology
ENR	enhanced natural recovery
EPA	U.S. Environmental Protection Agency
FEMA	Federal Emergency Management Agency
FNC	federal navigation channel
FS	Feasibility Study
HASP	Health and Safety Plan
HEC-RAS	Hydrologic Engineering Center – River Analysis System
ICIAP	Institutional Controls Implementation and Assurance Plan
LDW	Lower Duwamish Waterway
LDWG	Lower Duwamish Waterway Group
LTMMP	Long-Term Maintenance and Monitoring Plan

MHHW	mean higher high water
MIDP	Monitoring and Inadvertent Discovery Plan
MLLW	mean lower low water
MNR	monitored natural recovery
MOA	Memorandum of Agreement
MTCA	Model Toxics Control Act
OSHA	Occupational Safety and Health Administration
PCB	polychlorinated biphenyl
PDI	pre-design investigation
PDIWP	Pre-Design Investigation Work Plan
propwash	propeller wash
QA	quality assurance
QAPP	Quality Assurance Project Plan
QC	quality control
RAL	remedial action level
RAO	remedial action objective
RAWP	Remedial Action Work Plan
RCRA	Resource Conservation and Recovery Act
RD	remedial design
RDWP	Remedial Design Work Plan
RI	Remedial Investigation
RM	river mile
RMC	residuals management cover
ROD	Record of Decision
SCO	sediment cleanup objective
SD	storm drain
SMA	sediment management area
SOW	statement of work
STM	sediment transport model
T-117	Terminal 117
USACE	U.S. Army Corps of Engineers
WQMP	Water Quality Monitoring Plan

1 Introduction

This Remedial Design Work Plan (RDWP) describes the process that will be used to design the remedy for the middle reach of the Lower Duwamish Waterway (LDW) Superfund Site in King County, Washington, as selected in the U.S. Environmental Protection Agency's (EPA's) November 2014 Record of Decision (ROD; EPA 2014). This RDWP was prepared on behalf of the City of Seattle, King County, the Port of Seattle, and The Boeing Company, collectively referred to as the Lower Duwamish Waterway Group (LDWG).

In December 2000, LDWG entered into an Administrative Order on Consent (AOC) for Remedial Investigation/Feasibility Study (RI/FS) with EPA and the Washington State Department of Ecology (Ecology) to conduct an RI/FS for the LDW. In September 2001, the LDW was formally added to the National Priorities List as a Comprehensive Environmental Response, Compensation, and Liability Act (CERCLA, or Superfund) site; in February 2002, Ecology listed the LDW as a cleanup site under the Washington Model Toxics Control Act (MTCA). EPA and Ecology have divided lead agency responsibility for addressing the site: EPA is responsible for administering the cleanup of the sediments in the waterway, and Ecology is responsible for controlling sources of pollution to the waterway. The RI was completed in 2010 (Windward 2010) and the FS was completed in 2012 (AECOM 2012). A ROD was issued by EPA in 2014 (EPA 2014).

Five amendments to the AOC have been signed. The first amendment resulted in the fishers study (completed in 2016). The second amendment (AOC2) involved a pilot study to assess the effectiveness of activated carbon (AC) amendments to sand layer placement as a remedial technology. The third amendment (AOC3) specified pre-design studies, including collecting baseline data following early actions but before implementation of the full remedial action, surveying waterway users to update information on uses of the waterway, and preparing a design strategy report (Integral and Windward 2019) to help EPA ensure that all remedial design (RD) data needs are addressed in the appropriate sequence. The fourth amendment (AOC4) is currently addressing the RD of the upper reach of the LDW (river mile [RM] 3.0 to RM 5.0). The fifth amendment (AOC5), being addressed through this RDWP, addresses the RD of the middle reach of the LDW (RM 1.6 to RM 3.0). The remedial design approach outlined in this RDWP is consistent with the approach used for the upper reach of the LDW.

1.1 Remedial Design Work Plan Objectives

The primary objective of this RDWP is to describe the process to develop the detailed engineering design for the selected remedy for the middle reach of the LDW, as set forth in the

ROD and AOC5. Consistent with Section 6.3 of the AOC5 statement of work (SOW), this RDWP shall “include a proposed plan and schedule for implementing all RD activities for the LDW Middle Reach and identification and development of all RD supporting documents” (EPA 2021).

1.2 Remedial Design Work Plan Overview

This RDWP is organized as follows:

- **Section 1** introduces the RDWP; describes the site and selected remedy; discusses the general approach to remedial contracting, construction, maintenance, monitoring, and institutional controls; and describes RD project management.
- **Section 2** describes existing data.
- **Section 3** describes the engineering design process of the RD.
- **Section 4** describes additional activities that will support the RD process.
- **Section 5** presents the physical conceptual site model (CSM) for the middle reach, including expected outcomes of the remedial action.
- **Section 6** describes the RD deliverables.
- **Section 7** presents the RD project schedule.
- **Section 8** provides a list of references cited in this RDWP.
- **Appendix A** includes tables and figures extracted from the LDW Superfund ROD (November 2014) and a subsequent revisions memorandum (EPA 2015a).
- **Appendix B** provides a longitudinal cross section figure of the navigation channel excerpted from the Final Feasibility Study for the LDW.
- **Appendix C** is the Pre-Design Investigation Work Plan (PDIWP).

1.3 Site Description

The Duwamish River originates at the confluence of the Green and Black rivers near Tukwila, Washington, and flows northwest for approximately 12 miles, splitting at the southern end of Harbor Island in Seattle, Washington to form the East and West Waterways, prior to discharging into Elliott Bay in Puget Sound (Map 1-1). In the early years of the twentieth century, the last 6 miles of the Duwamish River were straightened and channelized into a commercial corridor for ship traffic, officially designated as the Lower Duwamish Waterway (LDW) and the East and West Waterways (located near the river mouth). The LDW spans 5 miles from the southern tip of Harbor Island to just upstream of the Turning Basin.

The middle reach of the LDW extends from the Duwamish Waterway Park just upstream of Slip 4 (RM 3.0) to just downstream of Slip 2 (RM 1.6) (Map 1-2). The middle reach includes a federal navigation channel (FNC), which is maintained by the U.S. Army Corps of Engineers (USACE). In

this reach, the width and depth of the FNC vary depending on location (Map 1-3). The middle reach consists of 111 acres of intertidal and subtidal habitat. The average width of the middle reach is 500 ft.

Comprehensive descriptions of the LDW environmental and physical site characteristics are presented in the *Lower Duwamish Waterway Remedial Investigation Report* (Windward 2010), the *Final Feasibility Study, Lower Duwamish Waterway* (AECOM 2012), and the ROD (EPA 2014).

1.4 Selected Remedy Summary

The selected remedy for the LDW is described in Section 13 of the ROD (EPA 2014). It addresses unacceptable human health risks associated with consumption of resident fish and shellfish, and with direct contact (skin contact and incidental ingestion of sediment) from net fishing, clamming, and beach play. It also addresses ecological risks to bottom-dwelling organisms (benthic invertebrates) and wildlife.

Remedial action levels (RALs) are contaminant concentrations that apply in sediment at specific locations and depths on a point-by-point basis (EPA 2014). Per the ROD, RALs are used to delineate areas that require active remediation. These RALs are dependent on the location, elevation type (i.e., intertidal vs. subtidal), Recovery Category, and depth interval in the sediment (e.g., 0 to 10 cm). In the intertidal areas, RALs apply to depth intervals of 0 to 10 cm and 0 to 45 cm. In the subtidal areas, RALs apply to depth intervals of 0 to 10 cm and 0 to 60 cm.¹ Shoal areas² within the FNC also have their own set of RALs. ROD Table 28 (included in Appendix A of this report) summarizes the RALs for each of the contaminants of concern (COCs). More information on RALs is presented in Section 2.2.1 of the PDIWP (Appendix C).

Based on RI/FS data, ROD Figure 18 (included in Appendix A of this report) shows the following remedial actions and estimated areas for the middle reach:

- Dredge or partially dredge and cap approximately 39 acres (35% of middle reach) of contaminated sediment.
- Place a thin layer (nominal 6 to 9 inches) of clean material, which may be combined with *in situ* treatment, on approximately 9 acres (8% of middle reach) of sediment in areas that meet the criteria for enhanced natural recovery (ENR).

¹ Subtidal RALs applicable to the 0- to 60-cm depth are dependent on Recovery Category designation and potential tug scour areas (see ROD Table 28 [included in Appendix A of this report] for additional details).

² Shoaled areas are defined as areas within the FNC with sediment accumulations above the authorized navigation depth.

- Apply location-specific cleanup technologies to approximately 5 acres (5% of middle reach) of contaminated sediment in any areas with structural or access restrictions (e.g., under structures and in the vicinity of dolphins/pilings, bulkheads, and riprapped or engineered banks).
- Implement monitored natural recovery (MNR) in approximately 51 acres of sediment:
 - **MNR Above Benthic Sediment Cleanup Objectives (SCOs):** Surface sediment contaminant concentrations are greater than benthic SCOs but below RALs in approximately 11 acres (10% of middle reach).
 - **MNR Below Benthic SCO:** Surface sediment contaminant concentrations are already below the benthic SCO in approximately 40 acres (36% of middle reach).

Early action areas (EAAs) comprise the remaining 7 acres (6%) in the middle reach and were identified for early cleanup actions during the RI phase to accelerate cleanup and hence reduce risks of exposure. The EAAs in the middle reach are detailed in Section 2.3.1 and Attachment A of the PDIWP.

The estimates of areas, volumes, and remedial construction time frame for the selected remedy are based on RI/FS data and analyses and other information included in the ROD (EPA 2014). These estimates will be refined during RD, based on area-specific pre-design investigations (PDIs), engineering analyses, updated Recovery Category assignments, and remedial technology assignment methodology identified on ROD Figures 19 through 23³ (included in Appendix A of this report).

1.5 General Approach to Contracting, Construction, Operation, Maintenance, and Monitoring for the Middle Reach

This section briefly describes options for remedy construction procurement; construction; and operation, maintenance, and monitoring with details to be developed during RD. Contracting for the RD is being conducted by LDWG. Future contracting for implementing the middle reach remedial action will be undertaken by an entity to be determined, which is referred to as the “implementing entity” in this document.

³ ROD Figure 19 and Figure 20 (as revised in the ROD Errata Correction Memo [EPA 2015]) present design criteria flow diagrams to determine appropriate active cleanup technologies to be applied to intertidal and subtidal areas, respectively. ROD Figure 21 presents the design criteria flow diagram to apply MNR in areas that are not subject to active remediation. ROD Figures 22 and 23 list the RALs and applicable depth intervals for intertidal and subtidal areas, respectively.

1.5.1 Contracting

The implementing entity will establish contractor selection criteria. The implementing entity will also develop its preferred contracting approach, including number of contracts, breakdown of work between contracts (if multiple contracts are used), insurance and bonding requirements, and contract administration processes. The design to be developed under this RDWP is assumed to be implemented using a design-bid-build project delivery method; however, that approach may be reevaluated during or after the RD is completed. LDWG, or the implementing entity, will coordinate with EPA on any anticipated changes to the project delivery method.

1.5.2 Construction

Remedial construction of the middle reach will proceed following source control sufficiency determinations, as described further in Section 4.12. In-water construction activities will occur during allowable construction windows designated for the LDW (generally from October through February) to protect threatened or endangered species under the Endangered Species Act. Remedial construction for the middle reach may span over multiple seasons, as defined by the allowable construction windows.

The implementing entity will provide overall quality assurance (QA) of remedial action construction. The implementing entity will execute the Construction Quality Assurance Plan (CQAP), which will be developed during RD consistent with the requirements of AOC5 SOW Section 6.10(b) (EPA 2021). The CQAP will describe QA activities that the implementing entity will perform before, during, and after construction. These QA requirements will include construction administration, on-site inspection, environmental monitoring, sediment confirmatory sampling, and communication or coordination with EPA.

The elements of the CQAP will be designed to work in concert with the construction quality control requirements in the specifications. The selected construction contractor will be responsible for providing quality control of its work. The bid document specifications will identify pre-construction and construction submittals that must be prepared by the contractor, and contractor quality control requirements during construction. Anticipated pre-construction and construction submittals that the selected construction contractor will be required to prepare are described in Section 3.10.

1.5.3 Maintenance and Monitoring, and Institutional Controls

The purpose of the Long-Term Maintenance and Monitoring Plan (LTMMP) is to ascertain attainment of cleanup levels and compliance with applicable or relevant and appropriate requirements (ARARs), to protect the integrity of the remedial actions, and to aid in the

evaluation of source control effectiveness. The final LTMMP will describe details of long-term monitoring and maintenance, including performance standards; sampling type, density, and frequency; interim benchmarks; and associated follow-up actions, as well as maintenance of remedy elements such as caps and ENR areas.

The LTMMP will be developed in accordance with *Guidance for Management of Superfund Remedies in Post Construction* (EPA 2017). The LTMMP will include both LDW-wide monitoring elements as well as elements specific to the remedy in the middle reach, such as specific monitoring requirements for caps, ENR, and MNR areas. The LDW-wide LTMMP outline is being developed during the upper reach RD. Per the AOC5 SOW (EPA 2021), the middle reach Preliminary (30%) RD shall develop an outline of the LTMMP specific to the middle reach, and the Pre-Final (90%) RD shall develop an annotated outline that discusses how the middle reach elements fit into the LTMMP approach for the LDW site as a whole. The LTMMP will remain as an annotated outline in the Final (100%) RD. The upper reach remedy is expected to be constructed first, and the implementing entity will complete and implement the LTMMP after construction is completed. It is expected that the LTMMP will be amended to include specific requirements for the middle and lower reaches following remedial construction of each reach.

An annotated outline of a Sediment Remedy Institutional Controls Implementation and Assurance Plan (Sediment Remedy ICIAP) will also be developed in conjunction with the LTMMP per AOC5 SOW (EPA 2021). The final Sediment Remedy ICIAP will identify the institutional controls necessary for the physical remedial actions. The Sediment Remedy ICIAP will include an evaluation of the most appropriate institutional, proprietary controls and location-specific use restrictions needed to ensure long-term effectiveness of the remedial action, consistent with Section 13.2.4 of the ROD (EPA 2014).

The Sediment Remedy ICIAP will be developed in accordance with *Institutional Controls: A Guide to Planning, Implementing, Maintaining, and Enforcing Institutional Controls at Contaminated Sites* (EPA 2012a) and *Institutional Controls: A Guide to Preparing Institutional Controls Implementation and Assurance Plans at Contaminated Sites* (EPA 2012b). For the protection of risks to human health from seafood consumption, EPA and Public Health Seattle-King County established a community-based Healthy Seafood Consumption Institutional Control Program for the LDW Superfund Site (US EPA's Institutional Control Implementation and Assurance Plan [ICIAP] for Seafood Consumption at the Lower Duwamish Waterway [LDW] Superfund Site [Public Health Seattle and King County 2019]). To avoid redundancy, the Sediment Remedy ICIAP will refer to the Institutional Control Program for institutional controls related to human health risks from seafood consumption.

Like the LTMMP, the Sediment Remedy ICIAP annotated outline will be developed during the upper reach RD for the entire LDW and modified during the middle reach RD. The revised Sediment Remedy ICIAP annotated outline will provide additional detail related to the middle reach remedial actions. The Sediment Remedy ICIAP will be updated with information for the lower reach following design of that reach.

Per AOC5 requirements, the Preliminary (30%) RD will include an outline of the Sediment Remedy ICIAP. Final (100%) RD will include a revised annotated outline of the Sediment Remedy ICIAP. In conjunction with implementation of other reaches, the implementing entity for the middle reach will complete and implement the Sediment Remedy ICIAP after construction within the reach is completed.

1.6 Remedial Design Project Management

1.6.1 Agency Oversight and Stakeholder Process

EPA will provide oversight for the RD process; USACE is EPA's technical advisor. Ecology and LDW stakeholders will review RD progress and provide input in accordance with the review process established by EPA. In general, this process involves LDWG submitting draft deliverables to EPA, who obtains stakeholder input. LDWG will address EPA comments and will submit revised deliverables to EPA. Figure 1-1 provides a schematic of the agency oversight and stakeholder relationships.

1.6.2 Respondent Team Organization, Responsibilities, and Authorities

Anchor QEA, LLC (Anchor QEA) is coordinating activities for LDWG, managing the team of subcontractors, and leading the RD for the middle reach of the LDW. Windward Environmental is leading the pre-design investigation, database management, and development of monitoring plans. Bright Engineering is leading structural and civil engineering support activities, and Long Bay Enterprises is leading site access and real estate support. The key personnel list is provided in Table 1-1.

**Table 1-1
Key Personnel and Support Contractors**

Title	Name	Firm Name
Project Manager	Tom Wang, PE	Anchor QEA
Project Engineer	Rebecca Gardner, PE	Anchor QEA
Remedial Sample Design Lead	Kathy Godtfredsen, PhD	Windward Environmental
Lead Geotechnical Engineer	John Laplante, PE, LEG	Anchor QEA
Lead Structural Engineer	Ade Bright, PE, SE	Bright Engineering
Field Lead	Susie McGroddy, PhD	Windward Environmental
Data Management Lead	Kim Goffman	Windward Environmental
Real Estate Lead	Cynthia Berne	Long Bay Enterprises
Community Engagement	Angela Ena	ECOSS
Statistical Analysis	Lorraine Brown	TerraStat Consulting Group
Archaeology	Tim Gerrish	Stell Environmental
Coastal Engineering	Kathy Ketteridge, PhD, PE	Blue Coast Engineering
Structural Engineering	Ade Bright, PE Khashayar Nikzad, PE	Bright Engineering TranTech Engineering

Other supporting contractors are included on the RD team to help provide data validation, field sediment and geotechnical sampling support, dive inspection and sampling, bathymetric and topographic surveying, private utility location, and analytical laboratories.

1.6.3 Communications

Monthly meetings will be held with EPA. Additional meetings will be scheduled at the request and discretion of EPA. In addition, as LDWG develops information during RD, EPA will present information and receive input through the Community Involvement process, which includes the Roundtable and potentially other public forums. The objective of the Roundtable forum is to discuss and identify ways to mitigate the potential impacts of the cleanup on affected communities, businesses, and waterway users. To address outreach activities during construction, a Community Outreach and Communications Plan will be prepared as part of the Pre-Final (90%) RD. The Community Outreach and Communications Plan will be based on the plan for the upper reach but will be specific to the needs of the middle reach.

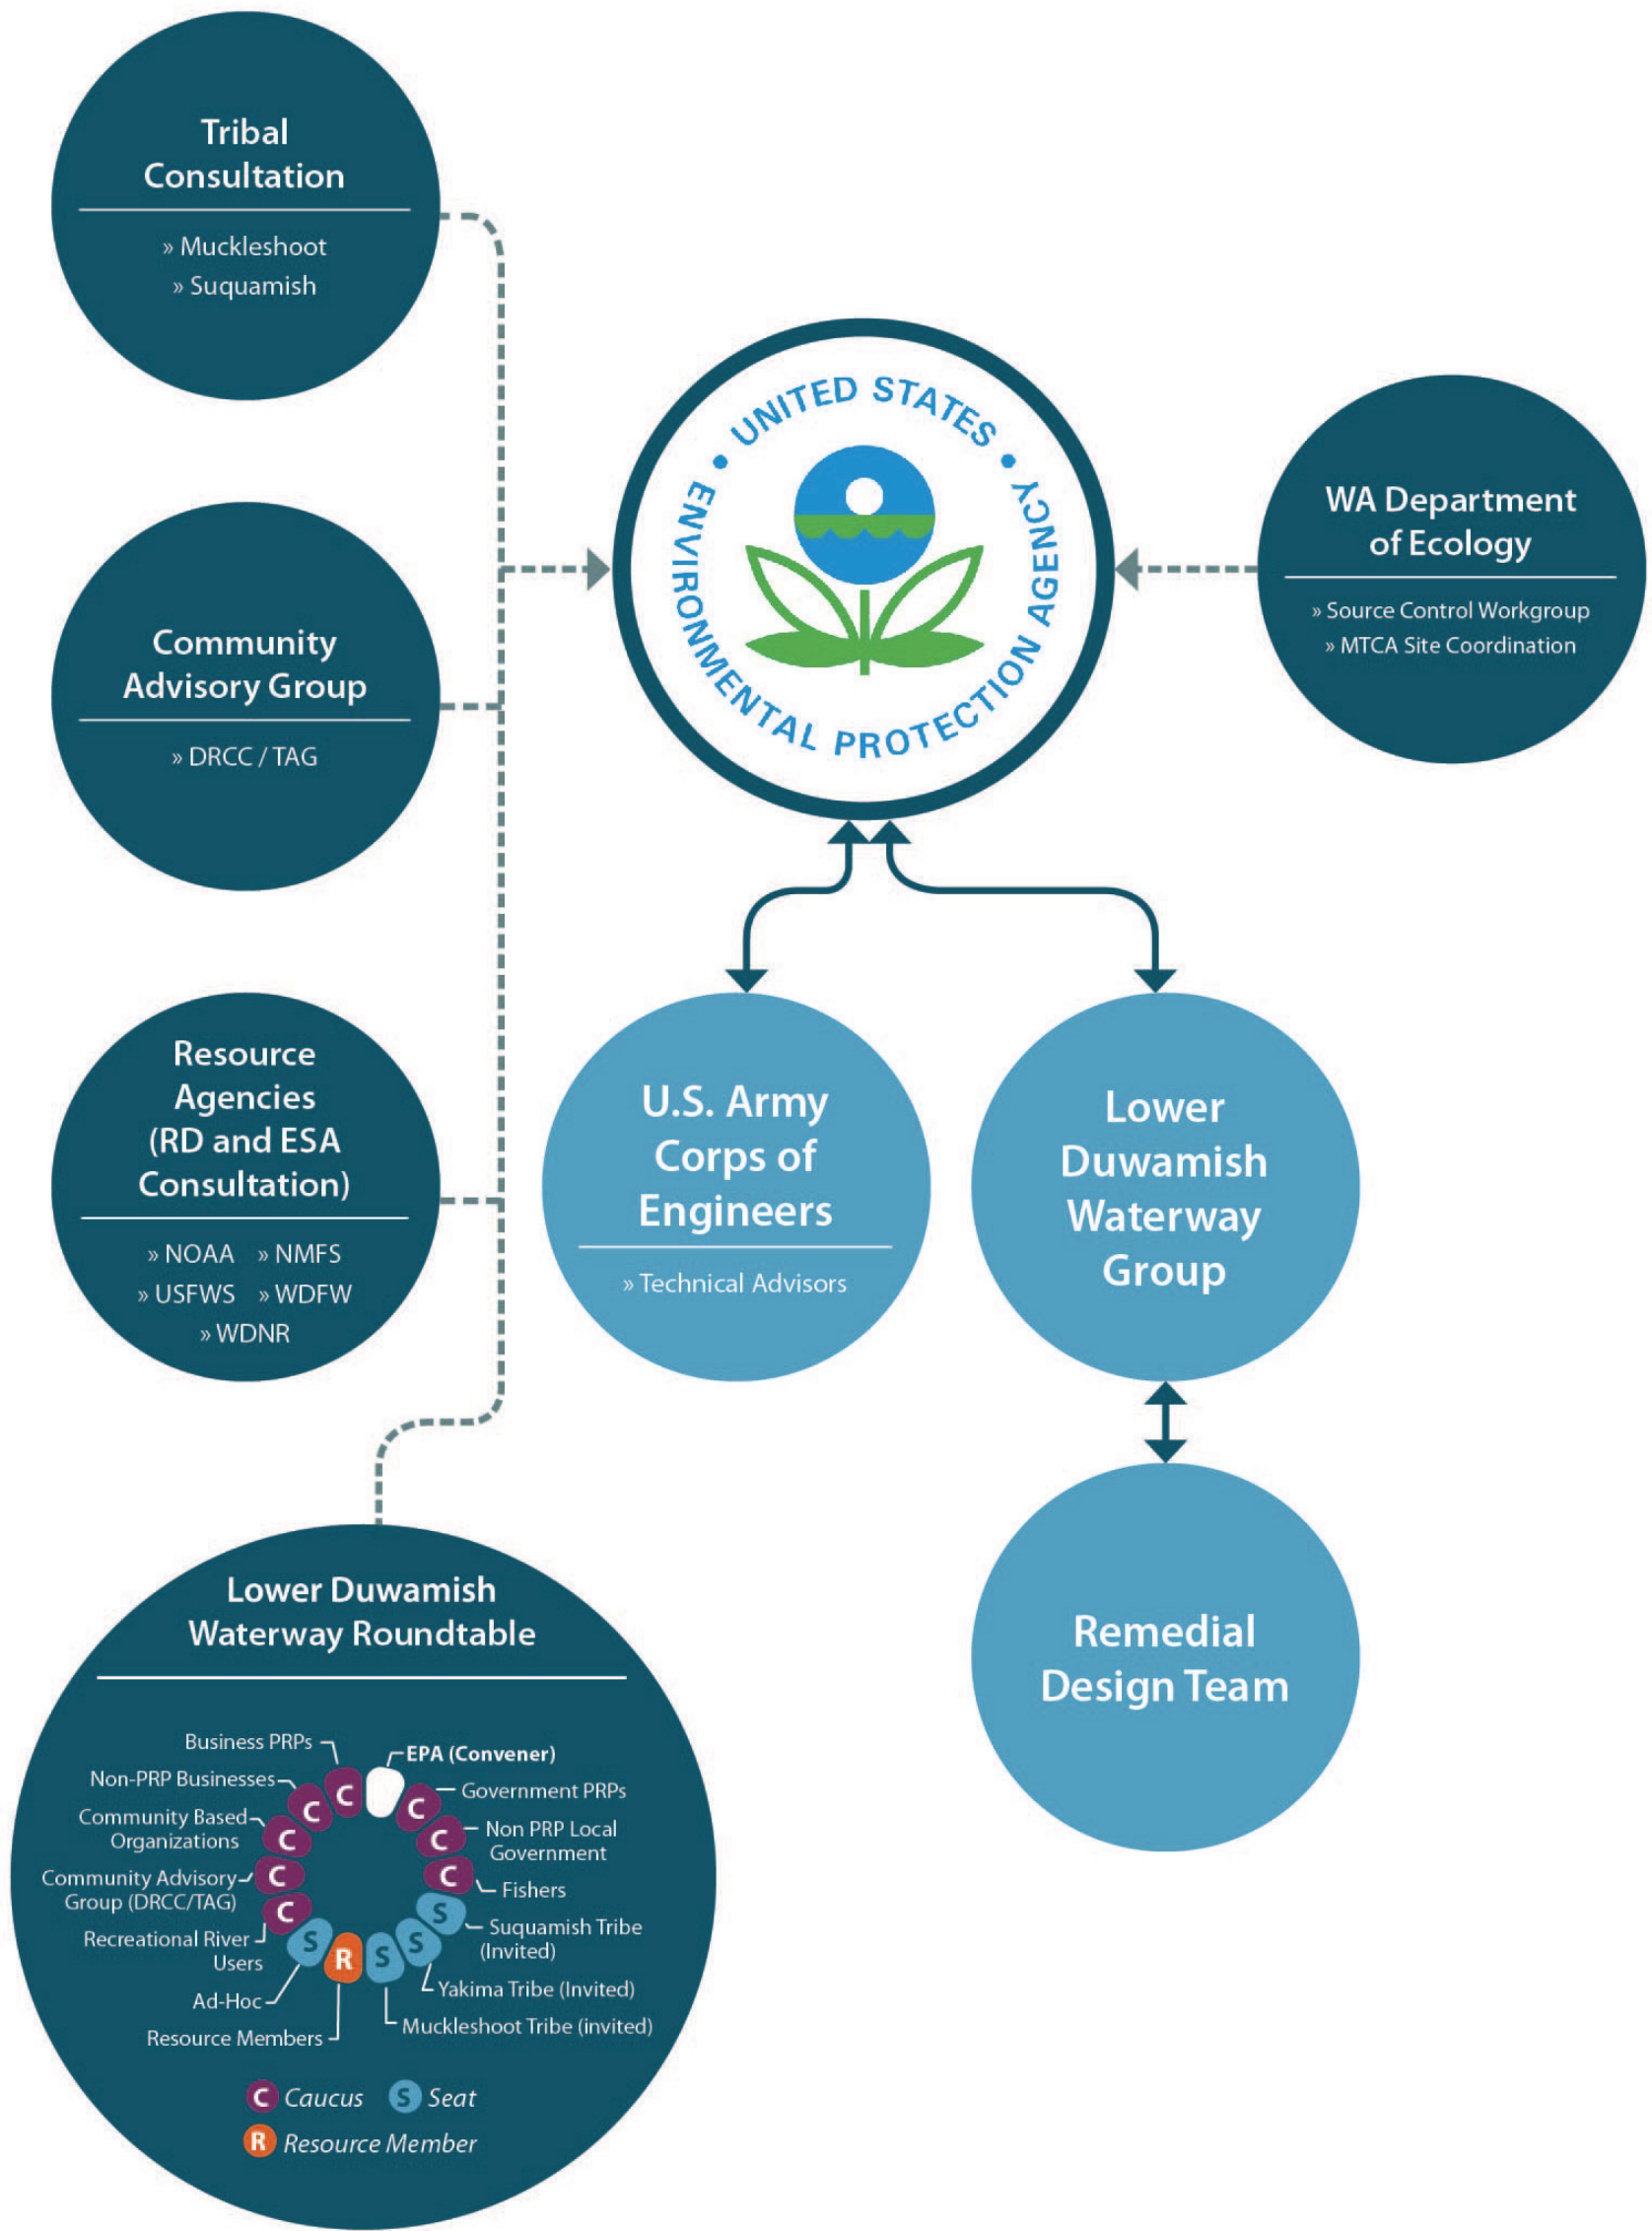


Figure 1-1. LDW Remedial Design Coordination
 REMEDIAL DESIGN WORK PLAN FOR LDW MIDDLE REACH

2 Existing Information Review

This section briefly summarizes site conditions in the middle reach that are relevant to developing the RD, references existing reports where additional information can be found, and reviews how this information will be used during the RD process. This section is based primarily on information developed for the LDW RI (Windward 2010) and FS (AECOM 2012), augmented with recent information in the following documents:

- *Technical Memorandum: Compilation of Existing Data* (Windward and Integral 2018)
- *Lower Duwamish Waterway Surface Sediment Data Report* (Windward 2019a)
- *Baseline Surface Water Data Collection and Chemical Analysis Data Report* (Windward 2019b)
- *Lower Duwamish Waterway Baseline Seep Data Report* (Windward 2018a)
- *Lower Duwamish Waterway Fish and Crab Data Report* (Windward 2018b)
- *Lower Duwamish Waterway Clam Data Report* (Windward 2019c)
- *Recovery Category Recommendations Report* (Integral et al. 2019)
- *Design Strategy Recommendations Report* (Integral and Windward 2019)
- *Draft Lower Duwamish Waterway Data Evaluation Report* (Windward 2018c)
- *Construction Report, Enhanced Natural Recovery/Activated Carbon Pilot Study* (Amec et al. 2018)
- *Year 3 Monitoring Report, Enhanced Natural Recovery/Activated Carbon Pilot Study* (Wood et al. 2021)
- *Waterway User Survey and Assessment of In-Water Structures – Data Report* (Integral et al. 2018)
- *Pre-Design Investigation Work Plan for the Lower Duwamish Waterway Upper Reach* (Windward and Anchor QEA 2019)
- *Remedial Design Work Plan for the Lower Duwamish Waterway Upper Reach* (Anchor QEA and Windward 2019)

In addition, Attachment A of the PDIWP, which is Appendix C of this RDWP (*EAA Data Including Monitoring and Perimeter Data*) presents information and cites reports related to EAAs.

The chemical data in all of these reports were not collected for RD purposes.

**Table 2-1
Overview of Areas Depicted in the ROD in the Middle Reach (RMs 1.6 to 3.0)**

Area Designation	Middle Reach (Excluding EAAs) (acres)	EAAs (acres) ^a	Total (acres)
Total Area	104	7	111
Bathymetric Elevations^b			
Intertidal	22	5	27
Subtidal	82	2	84
Areas of Interest for Site Use, Sediment Exposure, and Engineering Design (Areas May Overlap)			
Beach Play	12	0	12
Potential Clamming	14	3	17
Federal Navigation Channel	28	1	29
Berthing Areas	20	1	21
Under Structures	7	0	7
Recovery Categories^c			
Category 1	18	N/A	
Category 2	19		
Category 3	67		
Total	104		
Preliminary Remedial Technology Assignments^d			
Dredge	35	N/A	
Partial Dredge and Cap	4		
Cap	5		
ENR/ <i>in situ</i>	9		
MNR > SCO	11		
MNR < SCO	40		
Total	104		

Notes:

Areas are rounded for presentation.

- Two EAAs are within the middle reach. EAAs have been adjusted from the areas depicted in the ROD as needed based on as-built reports for Boeing Plant 2 and Slip 4.
- Based on the 2021 bathymetric survey and estimates across data gaps; acres will be adjusted during RD.
- Recovery Category areas have been adjusted slightly from the *Recovery Category Recommendations Report* (Integral et al. 2019) to reflect EAA boundary adjustments described in note a. Recovery Category boundaries will be adjusted during RD based on criteria in the ROD.
- Preliminary technology assignment areas have been adjusted slightly from the ROD to reflect EAA boundary adjustments described in note a. Remedial technology areas will be adjusted during RD based on criteria in the ROD.

2.1 Physical Conditions

The physical conditions of the LDW were described in the RI and FS. The sediment transport dynamics were evaluated in the sediment transport model (STM) as documented in *Lower Duwamish Waterway Sediment Transport Analysis Report* (Windward and QEA 2008) and *Lower Duwamish Waterway Sediment Transport Modeling Report* (QEA 2008). This section discusses the following physical site conditions in the middle reach:

- Geology and Hydrogeology
- Geomorphology
- Bathymetry
- Hydrodynamics and Sediment Transport
- Stratigraphy and Geotechnical Characteristics
- Infrastructure
- Banks
- Debris

2.1.1 Geology and Hydrogeology

The complex geology and hydrogeology of the Duwamish River basin are discussed in RI Section 2.5 and summarized in FS Section 2.1.3. The Duwamish River valley can be generally described as a glacial trough filled with alluvial deposits to a depth of as much as 200 ft below ground surface (FS Figure 2-3 [included in Appendix B of this report]). These deposits are underlain by either the bedrock unit or dense glacial deposits and non-glacial sedimentary deposits.

Within the LDW, native alluvium layers (consisting of sand, silt, gravel, and cobbles) are overlain by recently deposited organic sand and silt from upstream and lateral sources. The chemical characteristics of recently deposited sediment are discussed in Section 2.2 of this report. The physical properties of recently deposited sediment are summarized in RI Sections 2.5.4 and 2.5.5.

The groundwater system in the Duwamish River valley is described in RI Section 2.5.6. Native alluvium layers form the principal aquifer and groundwater pathway for the Duwamish River basin, and groundwater flow rates and gradients vary greatly. Groundwater flow near the LDW is generally toward the LDW; however, high tides cause temporary groundwater flow reversals close to the waterway. Areas subject to tidal influence are generally within 330 ft to 500 ft of the LDW bank (Booth and Herman 1998). Vertical flow gradients (both upward and downward) near the LDW develop from the complex interactions between groundwater, soil stratigraphy, infiltration of rainwater, and infiltration of tidally influenced LDW surface water (including higher

density brackish water). Where downward gradients intersect with upward gradients, the interaction has the potential to cause shallower groundwater to flow toward the LDW and discharge as seeps in the intertidal zone (RI Section 2.5.6.1).

During RD, hydrogeology information will be used in the following ways:

- RD capping design will consider advection of groundwater through areas that will receive a cap, similar to previous analyses performed within the LDW for EAAs. The rate of advection will be determined based on available data on the groundwater aquifer in the Duwamish River basin.
- RD will use local hydrogeologic data to select inputs to slope stability analyses.

2.1.2 Geomorphology

As described in RI Section 2.2 and FS Section 2.1.3, the LDW historically was a naturally meandering estuary that was extensively modified over the past 100 years or longer to straighten the waterway for navigation purposes by dredging and filling. Tide flats and floodplains were filled to straighten the river channel and to create upland areas for development, resulting in the abandonment of almost 3.7 miles of the original meandering river bed. Current side slips in the LDW are remnants of these old river meanders.

The current configuration, established in the early 1900s, consists of the FNC and Turning Basin, off-channel intertidal benches and banks, slips, and numerous berthing areas along the banks. Historically, the FNC was frequently dredged for navigational purposes, but has not been dredged since 1976 in the middle reach. Material excavated during dredging events to straighten and deepen the FNC in the early 1900s was used to fill the old meanders and the lowlands to bring them up to elevations similar to those of the surrounding uplands. Subsequent filling of the lowlands for continued development resulted in a surficial layer of fill in the vicinity of the LDW. The current shoreline includes armored banks, unarmored banks, dock faces, and vertical bulkheads (Map 2-1).

Information on the geomorphology of the middle reach will be used during RD in the following way:

- Bank erosion potential will be considered as part of recontamination evaluations and to inform the need to collect bank samples below mean higher high water (MHHW) to characterize chemical concentrations on the bank.

2.1.3 Bathymetry

Approximately 27 acres of the middle reach are considered intertidal, with bed elevations between 11.3 ft mean lower low water (MLLW; equivalent to MHHW) and -4 ft MLLW (Table 2-1). Approximately 84 acres of the middle reach are considered subtidal, with bed elevations below -4 ft MLLW. A 2021 bathymetric survey of the middle reach has been performed as part of RD for the middle reach. Some areas were not accessible at the time of the survey; these areas will be surveyed in 2022, and acreages of intertidal and subtidal areas will be updated. These acreages cited in this document are based on 2021 bathymetric survey elevations of the LDW (or interpolated elevations where survey data were not available) as shown in Map 1-3. Within the subtidal area of the middle reach, the FNC comprises 27.7 acres and is authorized to -30 ft MLLW from RM 1.6 to RM 2.0 (USACE Stations 113+00 to 134+00), -20 ft MLLW between RM 2.0 and RM 2.8 (USACE Stations 134+00 to 176+00), and -15 ft MLLW from RM 2.8 to RM 3.0 (USACE Station 176+00 to 187+00).

Bathymetric information will be used in RD in the following ways:

- Evidence of scour will be evaluated using high-definition survey images (i.e., sun-illumination maps). This information will be used to evaluate whether refinements to Recovery Category designations are needed.
- The deepest historical dredging within the FNC will be evaluated using available historical dredging bathymetric records. This information will be considered in estimating the maximum potential vertical extent of contaminated sediment and selecting core intervals for analyses where vertical extent is to be determined in the PDI.
- Bathymetric information of current conditions is used to determine the appropriate RAL at each location. The applicable RAL depends upon the bathymetric elevation of a remedial action area (see ROD Table 28; Figure 2 of the PDIWP [Appendix C]) as follows:
 - Intertidal areas (defined as above -4 ft MLLW) have different RALs and vertical points of compliance than subtidal areas.
 - The ROD defines “potential vessel scour areas” as between -4 ft MLLW and -18 ft MLLW south of the First Avenue South Bridge or between -4 ft MLLW and -24 ft MLLW north of the First Avenue South Bridge. These areas have a subsurface RAL for polychlorinated biphenyls (PCBs) in Recovery Category 2/3 areas.
 - Shoaled areas of the FNC (i.e., areas shallower than the authorized FNC elevation) have RALs that apply to sediments above the authorized FNC elevation plus 2 ft of overdredge (i.e., sediment above -32 ft MLLW from RM 0 to RM 2, -22 ft MLLW between RM 2 and RM 2.8, and -17 ft MLLW from RM 2.8 to RM 4.7).

- The remedial technology selection and design will be informed by current condition bathymetric elevations as follows:
 - Material placement must leave sufficient clearance in the FNC and berthing areas for vessels and future maintenance dredging.
 - Dredging and capping will be designed to minimize changes in middle reach net habitat areas including the following: 1) the net aquatic area (i.e., the surface area below MHHW); and 2) the net areas of elevation bands of most value for habitat, such as lower intertidal and shallow subtidal elevation ranges.
- Slopes where active remediation is occurring will be evaluated for stability.

2.1.4 Hydrodynamics and Sediment Transport

The hydrodynamics and sediment transport of the LDW (summarized in RI Section 2.6 and FS Section 2.1.3) were modeled during development of the STM.

The middle reach is an estuary environment, with freshwater entering from the Green/Duwamish River system and saltwater originating from Puget Sound. The location of the interface between freshwater and marine layer flows, referred to as the saltwater wedge, is variable within the middle reach depending upon both river flow and tidal stage. During times of high river flow and low tide stages, the saltwater wedge can be located as far downstream as the downstream extent of the middle reach (RM 1.8), whereas during low-flow conditions and high tide stages, the saltwater wedge can extend upstream of the middle reach. The upstream location or “toe” of the saltwater wedge is typically located between Slip 4 (RM 2.8) and the Turning Basin (RM 4.7).

River bottom velocities vary greatly within the middle reach depending upon the river flow rate and the presence or absence of the saltwater wedge at a given location and time. The saltwater wedge tends to reduce flow velocities near the river bottom because the less dense freshwater of the river will flow on top of the saltwater wedge; therefore, river bottom velocities are higher when the saltwater wedge is located at the downstream limits of the middle reach. Additional detail on the hydrodynamics of the LDW is available in the recent University of Washington study (Horner-Devine et al. 2017), which suggests that the salt wedge can extend upstream of the Turning Basin (RM 4.7) higher than previously modeled, depending on tides and river discharge. Future sea level rise will affect the upstream extent of the salt wedge. The potential change to the upstream extent of the salt wedge does not change the physical conceptual site model (Section 5) and will not affect the remedial design; design criteria will be based on high flow and high-velocity events.


Based on the STM, approximately 220,000 metric tons of upstream sediment and 1,100 metric tons of sediment from lateral loads enter the LDW annually (Figure 2-1). The highest deposition rates are located between RM 4.0 and RM 4.9 where the water velocity is reduced due to the widening and deepening of the LDW (i.e., the Turning Basin and the FNC) compared to upstream. The LDW continues to be net depositional on average within the middle and lower reaches, with approximately 28,000 metric tons of the sediment deposited between RM 0 and RM 4.0. The STM values cited in the text are based on estimates developed during the RI/FS process, which included an uncertainty and sensitivity analysis. STM bounding runs conducted during that process included runs with upstream sediment inputs similar to the new, lower estimates for upstream loads produced by the U.S. Geological Survey (Senter et al. 2018).

A further assessment of the effects of differences in upstream inputs was conducted (*Effects of Changes in Estimated Upstream Sediment Load on Lower Duwamish Waterway Sediment Transport Modeling; Recovery Category Recommendations Report - Appendix A* [Integral et al. 2019]). Because the STM is calibrated to empirically measured sedimentation rates, the lower estimate of sediment load entering the LDW from upstream made by the U.S. Geological Survey resulted in only small changes to the STM-modeled sedimentation rates within most of the LDW. Therefore, consistent with the conclusions of the Appendix A memorandum (Integral et al. 2019), the STM sedimentation rate values from the RI/FS process have been retained for use in RD.

The STM scour depth is based on a 100-year high-flow event. Modeling analyses have shown that a 500-year high-flow event results in scour depths similar to the 100-year flow event because of morphological characteristics upstream of the LDW and flow regulation by the Howard Hanson Dam.

Hydrodynamics and sediment transport information will be used in RD in the following ways:

- Capping design will use predicted maximum river flow velocities generated by the hydrodynamic model to develop cap design criteria (along with other currents and wave conditions such as propeller wash [propwash] and wakes).
- The STM 100-year scour predictions and estimated net sedimentation rates were used to define Recovery Category areas, which inform the technology selection based on ROD Section 13.2.

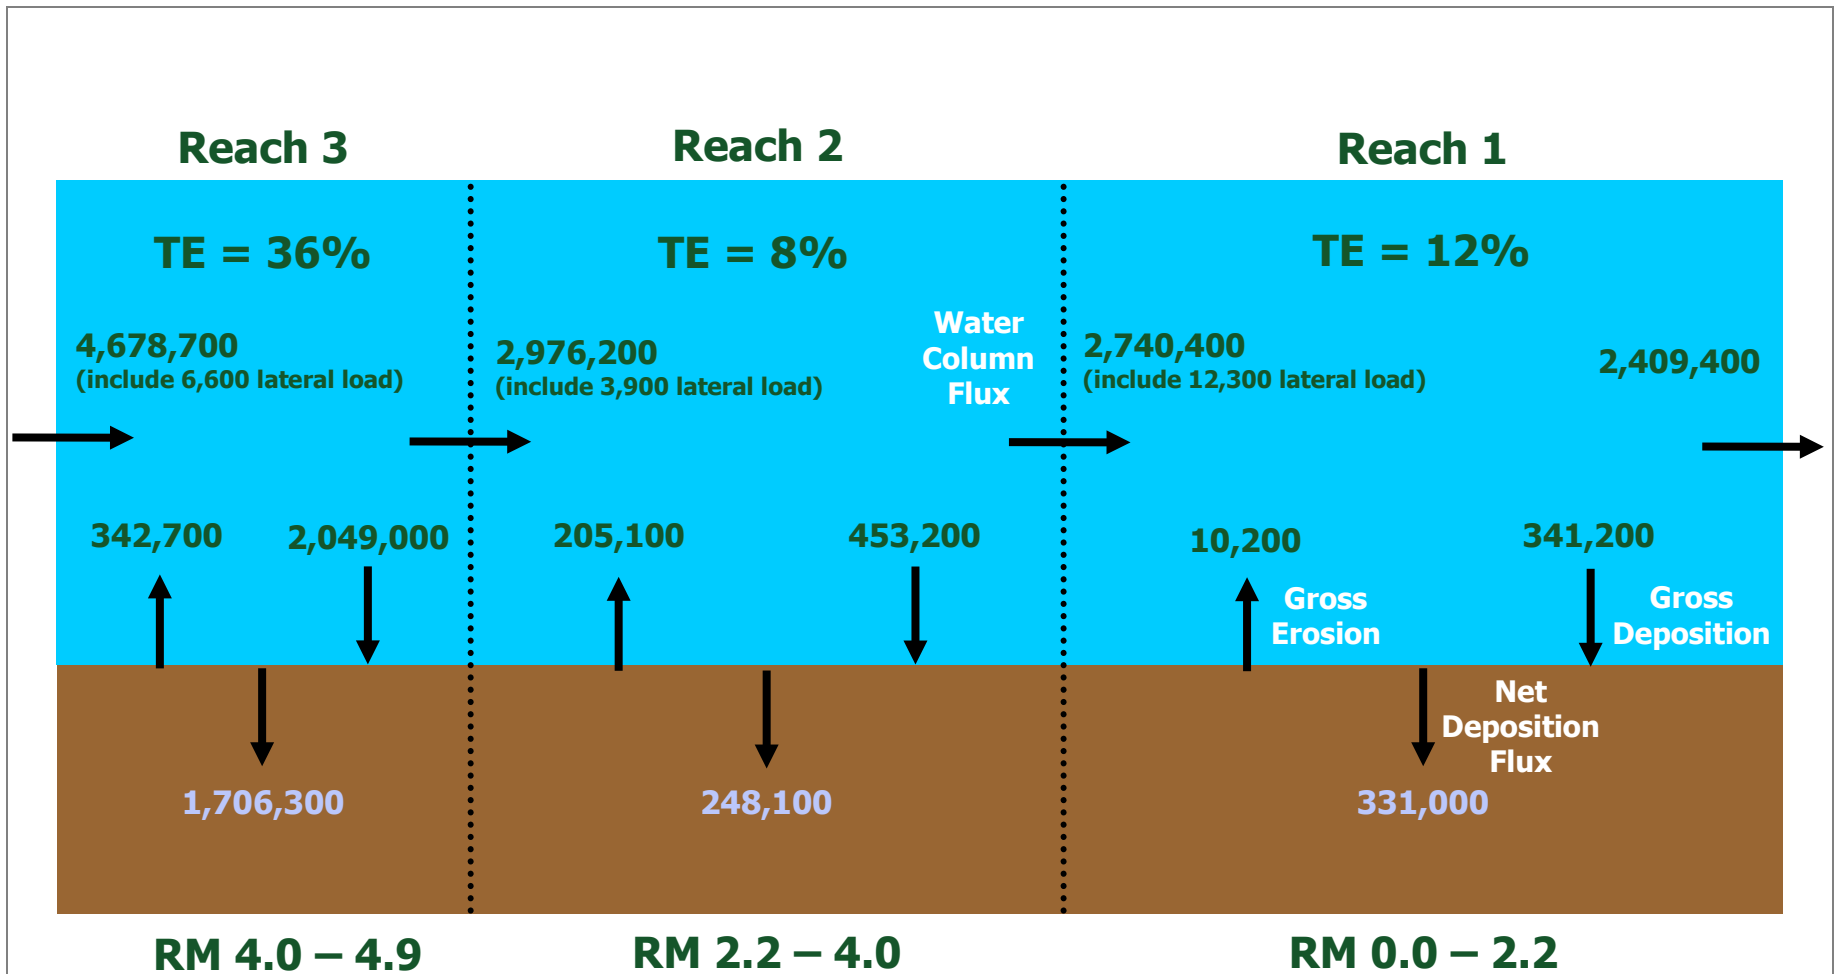

Notes:
 Sediment flux units are metric tons.
 RM: river mile
 STM: sediment transport model
 TE: trapping efficiency

Source: Integral, Anchor QEA, and Windward Environmental LLC, 2019. Recovery Category Recommendations Report – Final. Prepared for: U.S. Environmental Protection Agency, Region 10. February 11, 2019.

\\FUJI\Anchor\Projects\City of Seattle\LDW - Middle Reach_Task 300 RDWP\RDWP_Figures\source\Figure 2-1_STM mass balance.docx
 5/2/20229

Figure 2-1. Total Sediment Mass Balance Based on STM Predictions for 21-Year Period
 REMEDIAL DESIGN WORK PLAN FOR LDW MIDDLE REACH

2.1.5 Stratigraphy and Geotechnical Characteristics

As described in Section 2.1.1, the Duwamish River valley is generally a trough filled with alluvial deposits; the upper horizons of these have been dredged and filled in the current waterway configuration. The LDW is a net depositional environment, with organic-rich, soft, recent sediment deposited on native alluvium. The effects of contaminant releases, when present, are observable in these soft, recent sediments deposited in the LDW after industrial development. Therefore, the depth to the top of native alluvium represents the maximum potential vertical extent of contamination (see FS Figure 2-3 [included in Appendix B of this report]). This assumes no subsurface (i.e., groundwater) source of contamination, consistent with RI conclusions (e.g., RI Section 9.4.6 and *Quality Assurance Project Plan: Porewater Sampling of the Lower Duwamish Waterway* [Windward 2005]).

Limited geotechnical data characterizing the LDW sediments are summarized in FS Section 2.6.2. Sediment composition varies throughout the LDW, ranging from sand to mud (fine-grained silt and clay) with varying amounts of organic material, depending on the source of the sediments and the local current velocity. Silt with varying amounts of organic material is the dominant sediment type in much of the LDW main channel and in the slips.

The stratigraphy and geotechnical properties of recent sediment (deposited after development of the LDW) will be used in the following ways:

- In the PDI, sediment cores in potential dredging areas will identify the thickness of sediment units below mudline. In potential dredging areas, the depth to the top of the native alluvium layer in previously collected cores or observed in the field will help to inform the vertical elevation to analyze core samples during PDI Phase II.
- In the PDI, for banks with known or suspected contaminated sediment, the thickness of soft sediment deposited over the existing riprap layer on armored banks will be evaluated to help define the potential extents and quantities of contaminated sediment overlying riprap-armored banks.
- The Basis of Design Report (BODR) will describe the geotechnical properties of the sediment layers to identify stable slope angles that can be achieved during dredging and capping remedial action.
- The compressibility and shear strength of soft sediment will be evaluated in the PDI to develop specifications for placement activities (e.g., capping, ENR, residuals management cover [RMC]) to account for potential compaction or bearing strength failure of the substrate during placement.
- Bank caps will be designed to be statically stable and will be evaluated for seismic risk.

- Geotechnical properties such as density and shear strength will be used to evaluate the ease with which sediment can be dredged with standard equipment.

2.1.6 Infrastructure

Existing infrastructure located within the middle reach was described in the FS (Section 2.6), and additional information on in-water structures has been summarized in *Waterway User Survey and Assessment of In-Water Structures – Data Report* (Integral et al. 2018). As shown in Map 2-2, infrastructure includes waterfront facility berthing, overwater structures (e.g., piers, docks, floats, bridges, flow diversion structures, covered boat slips), piling (e.g., erosion control structures, fendering, mooring piles), bridges, and utilities (e.g., underwater cables and pipe structures, overwater cables, storm drains [SDs], outfalls). Where outfalls or pipes with unknown origins are present in areas with active remediation or MNR to benthic SCO, additional information will be acquired and included in the RD documents. In addition, bank infrastructure includes armored banks and bulkheads (Map 2-1). RD will take into account, and will not preclude, reasonably anticipated future land uses.

Infrastructure is assumed to remain intact during PDI. During RD, any changes to infrastructure will be tracked through coordination with waterway users (see Section 4.11). During RD, the location, condition, and type of infrastructure will be considered for the following purposes:

- Potential impacts to existing infrastructure from remedial actions will be evaluated (e.g., considering stability of structures and banks adjacent to dredging or capping areas).
- Protective setback distances from existing structures and other protective measures will be determined to prevent adverse impacts.
- Remedial technologies that can be effectively used adjacent to existing infrastructure will be determined through assessing constructability (e.g., considering equipment access constraints) and equipment capabilities during RD.
- Costs of protective measures versus demolition and replacing in-kind will be evaluated if appropriate. This is a standard practice of design, is an iterative process (beginning as early as the Preliminary [30%] RD step) and is incorporated into the next design draft after it is conducted.
- Potential impacts of remedial action on maintenance, repair, or replacement of existing infrastructure.

2.1.7 Banks

LDW middle reach banks are defined as the transition area from the LDW subtidal or intertidal bed to the upland areas above MHHW. The banks are typically delineated as starting at the toe,

where the relatively flat waterway bed (which will vary in elevation) begins to steeply slope to the top of bank (i.e., area where the slope flattens in the upland and is located above MHHW). The toe of banks can significantly vary in elevation because banks may be adjacent to berthing or navigation areas (with toe of bank elevation controlled by navigation needs) or banks may be adjacent to intertidal mudflats.

Bank conditions in the LDW have been characterized by Ecology (summarized in FS Section 2.6.3) and complemented by baseline sampling by LDWG at Ecology's request. The middle reach includes 3.65 miles of armored banks, 0.6 mile of unarmored banks, 1.55 miles of dock faces, and 0.24 mile of vertical bulkheads (Map 2-1). For RD purposes, armored banks are defined as bank areas that have an engineered surface armoring (e.g., riprap armoring, gabion armoring, bulkhead [sheetpile, concrete]) to prevent bank erosion. Banks that have no armoring or that consist of poorly placed or maintained armoring such that significant gaps in armoring exist (e.g., banks with intermittently exposed soil) will be classified as unarmored banks.

The RD will conduct a detailed investigation of middle reach bank areas during the Phase II PDI that are adjacent to RAL exceedance areas delineated in the PDI Phase I data evaluation report. During Phase II PDI, the RD may need to investigate middle reach bank areas that have evidence of erosion (as identified through the PDI Phase I data evaluation) and that have evidence that the area may be a potential source. During the RD, bank information will be used in the following ways:

- Bank conditions (e.g., armored vs. unarmored) adjacent to active remedial action areas will be factored into RD. For example, dredging and capping design will need to account for existing armored and unarmored banks to maintain bank stability by considering appropriate construction offsets or bank redesign requirements.
- For applicable bank areas adjacent to Phase I RAL exceedance areas or that may be a potential source of contamination to LDW, banks will be evaluated for geotechnical stability and potential for erosion. Eroding banks adjacent to active remedial areas will be evaluated as potential sources. Eroding banks that are not source material and not above RALs will not be addressed by the RD. The source evaluation will consider chemistry data (existing and PDI data), bank physical conditions (e.g., visible erosion, oversteepening or undercutting), and the presence and condition of bank armoring, in coordination with EPA and Ecology (see Section 4.12).
- If a bank area is contiguous to a RAL exceedance area and/or is identified as a potential source, additional coordination with EPA and Ecology will be required during the Preliminary (30%) and Intermediate (60%) RD stages to inform the sediment and bank

remedial design plan, in conjunction with potential upland cleanup actions.⁴ Following PDI Phase I data evaluation, additional bank characterization may be required in bank areas. Bank areas with RAL exceedances below MHHW will be part of the RD plan; bank contamination above MHHW will be identified as potential sources.

- Sedimentation on bank riprap armor occurs mostly from natural river processes, including ongoing deposition and/or scour during various flow events, and may also have contribution from lateral discharges and suspended sediments from vessel propwash. In remedial action areas, the thickness of soft sediment over existing riprap used to armor banks will be evaluated to help define the potential extents and quantities of contaminated sediment overlying riprap-armored banks in PDI Phase II, using probing or coring as appropriate.
- To inform RD (such as volume calculations, excavation, backfilling, and armoring design), topographic surveys will be performed on bank areas that are adjacent to Phase I RAL exceedance areas or other areas that may be needed to support remedial activities (e.g., habitat mitigation, site access or staging areas, potential source locations if applicable). The PDI Phase I (and potentially Phase II) Data Evaluation Report will identify bank topographic characterization needs in coordination with EPA.

2.1.8 Debris

The presence of debris within the LDW was discussed in FS Section 2.6.1.3. Debris is common in industrial waterways such as the LDW, deposited over decades of waterway use. Submerged and emergent debris will impact the implementation of remedial technologies. For example, larger debris (larger than 1 meter in size) or significant quantities of debris can reduce mechanical dredging production rates and increase dredge residuals.

As with many industrial waterways, much of the debris in the LDW is likely to be beneath the mudline and may or may not be visible or detectable at the surface. While it is not possible or necessary to fully inventory all debris, efforts are made in RD to identify observable large debris,

⁴ In accordance with the *Memorandum of Agreement* (MOA; EPA and Ecology 2014), EPA and Ecology will coordinate before initiating active in-waterway cleanup to ensure that sources have been sufficiently controlled. In addition, the MOA states as follows:

- EPA intends to provide Ecology with the baseline monitoring data and remedial design data required by the ROD for the area targeted for active in-waterway sediment remediation activities at least six months prior to the anticipated date that a source control sufficiency evaluation and recommendation is needed.
- Ecology will coordinate with EPA in preparing source control sufficiency evaluations for areas targeted for active in-waterway sediment cleanup activities and will submit associated recommendations to EPA for its concurrence.

and the specifications will require the contractor to be prepared to manage debris in any location. Identifying debris during RD will be accomplished using the following methods:

- The bathymetric survey will be used to identify potential near-surface debris. Debris on the order of a meter in size can typically be seen in high-resolution bathymetric surveys.
- Visual debris surveys of intertidal areas will be conducted at low tide in active remediation areas during PDI (Phase II).
- Focused debris surveys (e.g., side scan sonar, diver inspection survey) may be conducted (if determined to be needed) in dredging and capping areas during PDI (Phase II or III). Site history will be reviewed to identify areas with potential subsurface obstructions (e.g., pile stubs).

Debris will be factored into the RD and remedial action in the following ways:

- The quantity, type, and size of observed debris will inform remedial equipment selection or design details.
- To the extent available, debris characterization information will be included in the bid document plans and specifications to inform the selected contractor about site conditions and guide the contractor's selection of construction equipment.
- The contractor's Remedial Action Work Plan (RAWP) will develop an approach to remove and manage debris encountered during construction, with the expectation that debris may be encountered anywhere and equipment shall be capable of managing it.

2.1.9 Dredged Areas in the LDW Middle Reach

Maintenance dredging has not been performed in the middle reach FNC since 1976; select berthing areas within the middle reach have been maintenance dredged. PDIWP Map 17 depicts locations where dredging events since 1992 have been completed. PDIWP Section 3.5 has additional information on past maintenance events within the middle reach.

2.2 Sediment Chemistry Information

Existing sediment chemistry data have been summarized in the RI, FS, and in recent RD-relevant data reports listed in Section 2. An evaluation of existing chemistry data is included in the PDIWP (Appendix C).

Additional sediment chemistry data will be collected in PDI Phases I and II (and Phase III if needed). Sediment chemistry data are the key part of RD, as discussed further in Section 3, and will be used for the following purposes:

- Establishing horizontal extents of contamination (i.e., areas exceeding RALs; Section 3.3)

- Evaluating contaminant trends in the surface sediment and shallow subsurface sediment as a line of evidence to evaluate Recovery Category designations (Section 3.4)
- Applying remedial technologies (i.e., delineating areas exceeding technology-specific upper limit concentrations such as those for ENR; Section 3.5)
- Establishing vertical extents of contamination (i.e., the depth of RAL exceedances) in dredging areas (Section 3.7.1)
- Developing dredge prisms (Section 3.7.1)
- Performing predictive modeling to assess long-term sediment cap effectiveness (Section 3.7.2)

2.3 Previous and Ongoing Remedial Investigations and Actions

This section describes how lessons learned from previous and ongoing investigations and actions will be considered during RD, focusing on early actions in the LDW, the LDW ENR/AC pilot study, and upland contaminated sites along the LDW shoreline. During RD, previous actions and existing remedies within the middle reach will be considered to ensure that implementation does not compromise the integrity of completed or ongoing studies or remedial actions. Relevant lessons learned from the concurrent upper reach design process (AOC4) will also be considered in RD.

2.3.1 Early Action Areas

Six EAA remedial actions have been performed in the LDW, including from south to north: Norfolk EAA, Boeing Plant 2 EAA, Jorgensen Forge EAA, Terminal 117 (T-117) EAA, Slip 4 EAA, and Duwamish/Diagonal EAA (Map 1-1). As shown in Map 2-3, two of these EAAs are located within the middle reach (Slip 4 EAA and part of Boeing Plant 2 EAA). In addition to providing locations of these two EAAs, Map 2-3 also provides known locations of Resource Conservation and Recovery Act (RCRA) and MTCA listed cleanup sites adjacent to the boundary of the middle reach of the LDW.

Lessons learned from these early actions will be integrated into the RD for the middle reach. The LDW EAAs were implemented by different entities using different remedial technologies. The following sections summarize each EAA.

2.3.1.1 Norfolk

The Norfolk EAA is located next to the Boeing Developmental Center, upstream of the Turning Basin at RM 4.9 east bank (E) in the upper reach. It was identified as a cleanup area by the Elliott Bay/Duwamish Restoration Program (EBDRP) because of sediment contamination associated with a City of Seattle SD and King County combined sewer overflow (CSO). In 1999, King County

dredged 1 acre of contaminated sediment and backfilled the area with clean material. Monitoring post-construction continued annually through 2004.⁵ Long-term monitoring was completed in 2004.

In addition, in 2003, Boeing removed sediment from the LDW offshore of the Boeing Developmental Center south outfall (Boeing South), adjacent to the Norfolk EAA, as part of Ecology's Voluntary Cleanup Program (Ecology and Leidos 2018).

2.3.1.2 Jorgensen Forge

Jorgensen Forge is a steel and aluminum forging and distribution facility located south (upstream) of Boeing Plant 2 at RM 3.7E in the upper reach. Originally developed in 1942 by the Navy, the property has had several owners over 70 years. Earle M. Jorgensen (previous owner and operator of the facility until 1992) conducted removal of 1.6 acres of contaminated bank and sediments in the Jorgensen Forge EAA followed by backfilling with clean material in 2014. A revised Supplemental Engineering Evaluation/Cost Analysis for additional cleanup work is expected to be released for public comment in 2022, and planning for additional cleanup work is ongoing. Jorgensen Forge is also the name of an adjacent upland site being investigated under an MTCA Administrative Order.

2.3.1.3 Boeing Plant 2

Boeing Plant 2 is located on the east side of the LDW (RM 2.9E to RM 3.6E), with areas within the upper reach and the middle reach. Boeing built Plant 2 along the LDW in the late 1930s to manufacture military aircraft for the U.S. Government. Boeing remediated over 18 acres of contaminated sediment within the LDW by dredging and backfilling with clean material between 2012 and 2015 and restored nearly 1 mile of fish and wildlife habitat in 2013.⁶ The portion of the early action within the middle reach is shown in Map 2-3. Long-term monitoring of the Boeing Plant 2 EAA is ongoing. Boeing Plant 2 is also an upland cleanup site with previously performed and planned remedial actions.

2.3.1.4 Terminal 117

T-117 is a former asphalt shingle manufacturing facility located in the upper reach in Seattle's South Park neighborhood on the river's west bank (RM 3.6 west bank [W]). From 2012 to 2015, the Port of Seattle and City of Seattle remediated 1.4 acres of contaminated sediment by

⁵ Closure reports and post-closure monitoring reports (through 5 years post-construction) can be found on the King County Wastewater Treatment Division's Sediment Management website available at:

<https://www.kingcounty.gov/services/environment/wastewater/sediment-management/projects/Norfolk.aspx>.

⁶ Additional information on the Boeing Plant 2 cleanup can be found on the EPA's website available at:

<https://www.epa.gov/hwcorrectiveactionsites/hazardous-waste-cleanup-boeing-plant-2-tukwila-washington>.

dredging and backfilling with clean material from the bank and mudflat. Upland excavation was also a component of the cleanup.⁷ Long-term monitoring of the T-117 EAA is ongoing.

2.3.1.5 Slip 4

Slip 4 is a 6.4-acre navigational slip on the east side of the river, located within the middle reach (RM 2.8W). For many years, nearby industries used Slip 4 as a berthing area for vessels and for various industrial activities, and SDs and emergency sewer overflows⁸ were historically routed into the water here. Between October 2011 and February 2012, the City of Seattle removed contaminated sediment, capped remaining contamination with clean material, and restored wildlife and fish habitat in the area shown in Map 2-3.⁹ A residuals management layer was also placed adjacent to the EAA cleanup. Long-term monitoring of the Slip 4 EAA is ongoing.

2.3.1.6 Duwamish/Diagonal

The Duwamish/Diagonal EAA is located in the lower reach on the river's east bank, a half-mile south of Harbor Island (RM 0.4E to RM 0.6E). It was identified as a cleanup area by EBDPR because of sediment contamination associated with City of Seattle SDs and CSOs, a King County CSO, and a former sewage treatment plant outfall. Between 2003 and 2004, King County implemented a cleanup, restoring 7 acres of habitat for salmon and other species by removing contaminated sediment and capping remaining contamination with clean material. In addition, a clean sand layer was added over 4 acres in 2005 to address dredge residuals. The remediation area and a perimeter area were monitored post-construction annually through 2010.¹⁰

2.3.2 Enhanced Natural Recovery/Activated Carbon Pilot Study

In 2015, LDWG initiated the ENR/AC pilot study (under Amendment 2 to the AOC) to determine whether ENR material amended with AC can be successfully applied to reduce the bioavailability of PCBs in contaminated sediments in the LDW. The study was designed to compare the effectiveness of ENR with added AC compared to ENR without added AC in three areas in the LDW (intertidal plot, subtidal plot, and scour plot; these plots are located in the upper and lower reaches of LDW). Project construction was completed in January 2017 (Amec et al. 2018), and

⁷ Project documents and construction summaries can be found on the T-117 cleanup page available at: <http://www.t117.com/>.

⁸ In contrast to a CSO, an emergency sewer overflow is an overflow point that only relieves the system if there is a mechanical failure and rarely or never discharges.

⁹ Additional project information can be found in the *Slip 4 Early Action Area Removal Action Completion Report* (Integral 2012).

¹⁰ Additional information can be found on King County Wastewater Treatment Division's Sediment Management website available at: <https://kingcounty.gov/services/environment/wastewater/sediment-management/projects/DuDi.aspx>.

the pilot project monitoring (post-construction, Years 1, 2, and 3) was completed with final report of the pilot study findings issued in 2021 (Wood et al. 2021).

The pilot study monitoring results indicate that ENR material reduced the bioavailability of PCBs to such an extent that improvements achieved by adding AC were inconsequential. Both the ENR material and ENR material amended with AC were generally stable over the 3-year monitoring period. Additionally, no evidence was found indicating adverse effects of AC on benthic invertebrate communities over the 3-year monitoring period (Wood et al. 2021). Based on this pilot study, EPA and Ecology have decided there is also no clear benefit in adding AC to ENR in the LDW. In the LDW cleanup, AC may be used as a layer in sediment caps or where waterway structures (like docks) make dredging or capping contaminated sediment difficult. These uses of AC in the LDW will be considered during RD, consistent with the ROD (Section 13.2.1.2).

2.3.3 Lessons Learned

The lessons learned from the EAAs and the ENR/AC pilot study are summarized based on project documentation and discussions with personnel involved in the work (Table 2-2). The Removal Action Completion Reports for Jorgensen Forge and Slip 4 (Anchor QEA 2016; Integral 2012) both contained well-organized lessons learned sections. For the other EAAs (Norfolk, Boeing Plant 2, T-117, and Duwamish/Diagonal), key lessons learned were culled from pertinent sections of construction reports. Lessons learned from the ENR/AC pilot study construction activities can be found in the Pilot Study Construction Completion Report (Amec et al. 2018).

To be useful in the context of this RDWP, the lessons learned for the EAAs and other similar sediment remediation projects in the LDW have been distilled into common themes that are considered applicable to future cleanup in the LDW (Table 2-2). These lessons learned are also similar to experiences at other sediment cleanup sites located outside of the LDW (i.e., Puget Sound and national sediment remediation projects). Key lessons learned from the EAAs and other similar sediment remediation projects will be incorporated into the RD.

Table 2-2

Summary of Early Action Areas, ENR/AC Pilot and Other Sediment Remediation Site Lessons Learned

Topic	Lesson Learned	Recommendations for Consideration
Communications	Early and frequent communication between the implementing entity, EPA, the contractor, the community, Tribes, and property owners and tenants is critical to project success.	<p>The EAAs report a number of successes in early and continuing communications. Core recommendations include the following:</p> <ul style="list-style-type: none"> • Engage stakeholders during all project stages. • Develop communications plans. • Understand community concerns. • Perform frequent outreach. • Provide multiple outlets of communication. • Hold structured meetings (e.g., during construction). • Have identified contacts for issues that arise. • Perform early coordination to plan for construction challenges.
Affected Users and Site Access	Negotiations for site access, business disruption, alternative facilities, and Tribal fishing disruption are costly, complex, and time consuming, and the requirements must be integrated into the RD.	<ul style="list-style-type: none"> • Initiate access negotiations early (e.g., after 60% design). • Include access costs in cost estimate.
Design Specification Approach; Measurement and Payment Approach	Contractors can identify project efficiencies to improve project outcomes.	<ul style="list-style-type: none"> • Develop performance specifications; avoid prescriptive means and methods that limit flexibility. • Include provisions for contractor’s value engineering proposals.
	Measurement and payment approaches affect project incentives.	<ul style="list-style-type: none"> • Develop a measurement and payment scheme with incentives that align with project goals.
	Transloading and transportation can be key production rate and cost drivers.	<ul style="list-style-type: none"> • Allow for contractor flexibility in selecting and implementing transloading and transportation options. Recognize that rail capacity has a large impact on production rates and is influenced by outside factors (e.g., competing projects, infrastructure limitations).
	Dredging and placement tolerances can affect production rates.	<ul style="list-style-type: none"> • Provide reasonable tolerances (e.g., overdredging and overplacement allowances) considering both production rates and material (disposal or purchase) costs.
	Actual quantities may differ from design quantities.	<ul style="list-style-type: none"> • Develop measurement and payment approaches that consider uncertainty (e.g., unit costs, contingency items).

Topic	Lesson Learned	Recommendations for Consideration
Dredging and Excavation	Dredge residuals are intrinsic to dredging and may be observed within and around the perimeter of the dredging area. Dredge residuals concentrations can be transient. Residuals management cover (RMC) has effectively managed dredge residuals in the LDW and on other sediment remediation sites.	<ul style="list-style-type: none"> • Develop a dredge residuals management plan that uses BMPs during dredging, post-dredge sampling, and targeted contingency actions (e.g., RMC, contingency re-dredging) to achieve defined performance goals.
	Debris in industrial waterways is common. Debris in the LDW is likely to be beneath the mudline and may or may not express itself at the surface. Debris can have significant impacts on production rates, equipment effectiveness, and sediment resuspension.	<ul style="list-style-type: none"> • Clearly identify in specifications that the contractor shall expect significant debris (observable and buried) during construction. • Plan equipment and removal means and methods to remove a wide variety of debris. • Use reasonable methods to identify large observable debris during RD.
	Both environmental and digging buckets are necessary to achieve both production rate and environmental dredging objectives.	<ul style="list-style-type: none"> • Allow the contractor to use a digging bucket as necessary for rock, debris, and consolidated sediment.
	BMPs will require modification over time.	<ul style="list-style-type: none"> • Plan to adaptively manage BMPs during the duration of the project.
	Work near structures has additional uncertainties and risks.	<ul style="list-style-type: none"> • Require structural surveys. • Plan for contingencies.
	Subsurface conditions are uncertain, particularly in banks.	<ul style="list-style-type: none"> • Plan for contingencies, particularly in bank areas.
	Dredge return water management has been successful in the LDW using a variety of approaches.	<ul style="list-style-type: none"> • Manage water with BMPs and engineering controls and return water to LDW. This approach successfully meets all water quality requirements without costly upland treatment and discharge.
	High-resolution progress surveys improve feedback and dredging accuracy.	<ul style="list-style-type: none"> • Require multi-beam progress surveys.
RAWP and Other Pre-Construction Submittals	Development and approval can take months to finalize.	<ul style="list-style-type: none"> • Award contract several months before the opening of the in-water work window.
Construction Sequencing and Phasing	The short in-water work window in the LDW compresses project schedule.	<ul style="list-style-type: none"> • Plan for the potential need for night work by coordinating with EPA and the neighboring community. • Allow flexibility to optimize efficiency and appropriate dredging season stop points.

Topic	Lesson Learned	Recommendations for Consideration
Water Quality	Water quality criteria exceedances (e.g., turbidity at a compliance distance) can occur during dredging and during placement of capping/ENR material.	<ul style="list-style-type: none"> • Turbidity is the primary water quality driver, not COCs. • Develop clear communications and response protocols with EPA. • Develop an adaptive approach using BMPs that minimize releases during dredging. • Develop appropriate response actions to address turbidity water quality criteria during clean material placement. • Consider fixed monitoring stations. • Recognize that the saltwater wedge affects turbidity.
Material Placement	The placement of granular activated carbon requires additional QC and handling steps.	<ul style="list-style-type: none"> • Specifications should provide clear requirements on handling of granular activated carbon (e.g., pre-wetting procedures).
	Additional material needs to be placed to meet minimum design thicknesses for caps and ENR.	<ul style="list-style-type: none"> • Provide reasonable overplacement allowances to meet design criteria. • Consider the average thickness that will be placed to meet minimum thicknesses.
	Cap and ENR thickness measurements have uncertainty and can vary depending on the measurement approach.	<ul style="list-style-type: none"> • Establish accurate surveying and positioning control prior to conducting placement. • Use several methods of determining cap thickness, such as surveys, tracking quantities, "bucket maps," and coring/probing. • Anticipate subgrade settlement below placed material. • Timely measurement and acceptance of placed thickness is essential to avoid construction delays.
Compliance Sampling	The compliance sampling approach can affect construction.	<ul style="list-style-type: none"> • Carefully develop a compliance sampling approach that can evaluate the appropriate project goals and limits down time
	Some backfill types cannot be sampled.	<ul style="list-style-type: none"> • Develop contingencies for sampling coarse material.
	Ongoing site processes (e.g., sedimentation and resuspension) affect long-term monitoring results.	<ul style="list-style-type: none"> • Long-term monitoring should consider site processes.

2.4 Existing Habitat Conditions in Middle Reach

RI Section 2.8 and FS Section 2.1.5 summarize the habitat types in the entire LDW. The natural habitat types in the LDW include intertidal mudflats, tidal marshes, and subtidal areas. Intertidal marshes contain marsh soils (generally fine-textured and nutrient-rich), supporting grasses, sedges, rushes, and various other plants. For example, the south landfall of the First Avenue Bridge is a small intertidal marsh within the middle reach.

Intertidal mudflats are generally defined as the gently sloping areas from MLLW up to the edge of intertidal marsh vegetation (Blomberg et al. 1988). Intertidal mudflats, composed of unvegetated intertidal areas with sand or mud substrate, are dispersed in relatively small patches within the middle reach. Intertidal mudflats serve as sources of nutrients for primary producers and provide food and habitat for benthic invertebrates, fish, shorebirds, and aquatic mammals. Intertidal mudflats also attenuate boat wakes for upslope tidal marshes (Battelle 2001). Approximately 14 acres of the middle reach were identified in the ROD as potential clamming areas based on bathymetric elevations (shallower than -4 ft MLLW) and considering substrate and salinity conditions. Potential clamming areas are a subset of the intertidal areas.

Several habitat restoration projects have been performed (or are currently planned for construction) within the middle reach; these include the following (Map 2-4):

- The Washington State Department of Transportation constructed a fish and wildlife habitat restoration channel that connects to an emergent vegetation area at the south landfall of the First Avenue Bridge at RM 2.1W.
- Alaskan Park and Shoreline Habitat is located at RM 2.8W.
- The Boeing Plant 2 habitat project is located at RM 2.9E.

During RD, the middle reach habitat conditions will be considered in the following ways:

- Existing middle reach habitat areas will be identified to help ensure that the RD restores the site to pre-construction bed elevations to the extent practicable.
- Existing and post-construction middle reach habitat areas will be summarized in the BODR as part of Endangered Species Act consultation and Section 404(b)(1) evaluations. The summary will identify existing habitat areas (divided into established elevation bands); proposed post-construction habitat areas (divided into established elevation bands); substrate materials for caps, ENR, or placement of backfill materials in any identified habitat areas; and locations where loss of aquatic habitat is unavoidable (e.g., capping around infrastructure) and how those losses are offset in other locations. Should habitat mitigation be necessary for ARAR compliance, mitigation requirements

will be assessed in the Preliminary (30%) to Intermediate (60%) RD stages and finalized in the Pre-Final (90%) RD.

2.5 Waterway Usage in Middle Reach

The RD will consider location-specific waterway usage so that the remedy minimizes interference with existing site uses during remedial construction, and it informs the RD to accommodate existing and future uses post-construction. This section describes important current and reasonably anticipated future land use of the middle reach.

2.5.1 Tribal Use and Treaty Rights

As described in the ROD (Section 3), the LDW is one of the locations of the Muckleshoot Tribe's commercial, ceremonial, and subsistence fishery for salmon, as part of its Usual and Accustomed fishing area. The Suquamish Tribe actively manages aquatic resources north of the Spokane Street Bridge, just north of the LDW study area. The Tribes, as sovereign nations, have engaged in government-to-government consultations with EPA on the cleanup process and decisions. The Tribes have also broadly and actively participated in meetings determining the course of the cleanup to date. EPA plans to continue to consult with the Muckleshoot and Suquamish Tribes throughout design, construction, and long-term monitoring of the remedy, including any potential modifications to the remedy. In addition, although not a federally recognized Tribe, the Duwamish Tribe uses Herring's House Park (located north of the middle reach) and other parks along the Duwamish River for cultural gatherings.

Tribal consultation will occur during the design and construction process at a schedule determined by EPA and could include topics such as commercial fishing, shoreline use, access points, cultural activities, or other tribal interests. Tribal use within the LDW was considered during the development of the ROD, and Tribal use will be considered during RD by maintaining aquatic area with beneficial water depths for fisheries (e.g., shallow subtidal). Close coordination will be maintained with the Muckleshoot and Suquamish Tribes during RD and construction, and agreements for any needed fishery disruption will be negotiated prior to construction. Tribal input will be sought by EPA during RD, and Affected Tribes will be consulted as per Section 106 of the National Historic Preservation Act. Monitoring and Inadvertent Discovery Plans (MIDPs) will be developed for sampling and construction.

2.5.2 Beach Play and Tribal Clamming Areas

The middle reach contains three potential beach play areas, designated in the RI/FS as Beaches 4, 5, and 6, encompassing 12 acres of the middle reach.¹¹ In addition, the middle reach contains 17 acres (including EAAs; Table 2-1) where the intertidal sediments are suitable for clam habitat and could support clamming, including Tribal clam harvest. Beach play and Tribal clamming were considered in the RI/FS/ROD process in the development of cleanup levels and RALs.

2.5.3 Public Access Points

Potential public access locations are important to consider during RD in order to maintain public safety and to minimize the impacts of construction on the public. Potential public access points from the shoreline within the middle reach are shown on Map 2-4. The First Avenue South boat ramp, located at RM 2E immediately south of the First Avenue South Bridge, provides a public access boat launch. The S. Michigan Street Shoreline Street End at RM 2E is just north of the First Avenue South Bridge. The Duwamish River Public View Point is located at the mouth of Slip 4 at RM 2.9E. The Gateway North/8th Avenue South street end public access is located at RM 2.7E. Public beach access is available at Gateway Park North at RM 2.75E, taftaucid Park at RM 2.8W, and Duwamish Waterway Park at RM 3.0W (just south of the middle reach but gives access to beaches within the reach). The EPA's Roundtable forum may identify other potential public access issues that could be considered when developing RD details.

Construction of enhanced public access is beyond the scope of this remediation project; however, should plans for enhanced public access be developed separate from remediation, those plans could be considered in RD to avoid conflicts between the public access design completed by others and the RD. EPA will use the Roundtable forum to coordinate public input on the Preliminary (30%) and Intermediate (60%) RD; impacts and safety concerns identified in EPA comments based on public input will be addressed in the next iteration of design. In addition to EPA's Roundtable forum, a Community Outreach and Communications Plan will be developed during Pre-Final (90%) and Final (100%) RD phases so that potential public access closures are effectively communicated to the public during construction.

2.5.4 Waterway Users

LDWG contacted waterway users in 2018 as part of pre-design activities, as summarized in *Water User Survey and Assessment of In-Water Structures – Data Report* (Integral et al. 2018). Waterway users were divided into three categories: waterway-dependent users, recreational use businesses and associations, and owners of residential and waterfront properties without water-

¹¹ Part of Beach 5 is located in the upper reach.

dependent facilities. Waterway-dependent users include waterfront property owners and their tenants that are supported by bank infrastructure (e.g., docks, piers, wharves, berthing areas) and operators of commercial tug, barge, and cargo vessels. Berthing areas comprise approximately 20 acres within the middle reach (see Table 2-1).

Recreational use businesses and associations include businesses that support recreational boating and owners of recreational areas (i.e., municipal park owners). Owners of residential and waterfront properties without water-dependent facilities include all property owners and tenants without apparent water-dependent facilities and those who own residential properties (with or without minor waterfront structures such as docks and piers).

Discussions with waterway users are important for identifying the current and reasonably anticipated future land uses, assessing waterfront infrastructure and banks near remediation areas, and identifying changes during RD and potential sources of disruption during construction. Approximate berthing maintenance depths for most berthing areas were documented in the FS. Unlike the FNC, berthing area maintenance elevations are not formally defined, but based on operational needs and identified in USACE dredging permits. During RDWP development and RD, LDWG will conduct additional outreach to coordinate with water-dependent users on operational needs and structural limitations, the RD approach, PDI coordination, construction sequencing planning, and planned future construction activities.

The completed design will be compatible with current and reasonably anticipated future land uses. In areas that require remediation (see Section 3.3), the design will maintain water depths in berthing areas and avoid damaging existing waterfront infrastructure such as overwater structures, armored banks, and utilities. For example, per the ROD, the top of the cap or ENR layer must be below the operational depth plus an additional 2 ft.

As noted earlier, during Pre-Final (90%) and Final (100%) RD phases, a Community Outreach and Communications Plan will be developed that includes communication with waterway users.

2.5.5 Federal Navigation Channel

The FNC supports water-dependent industry along the LDW. As discussed in Section 2.1.3, the ROD incorporated evaluation and remedial action for shoaled areas (i.e., areas with bed elevations shallower than the authorized depth) if sediment concentrations are above the RALs

at depths up to 2 ft below the authorized depth.¹² Sample intervals will be determined in the PDI Quality Assurance Project Plan (QAPP).

In addition, the ROD requires appropriate post-construction clearances for placement activities (i.e., a 2-ft buffer between the authorized depth and the top of an ENR layer, and a 4-ft buffer between authorized depth and the top of a cap). Furthermore, the ROD requires a 10-ft horizontal buffer outside of the FNC for placement activities to account for equipment tolerances, and the potential for material to slough into the channel (ROD Section 13.2.1.1). The considerations for RD technologies in the FNC are discussed in Section 3.7.

2.6 Data Gaps Identification

The PDIWP provides a conceptual sampling plan based on the data types summarized in Appendix B of the *Design Strategy Recommendations* Report (Integral and Windward 2019). In addition, the PDIWP identifies data quality objectives (DQOs) for the Phase I and II investigations (Section 4.1).

The following bullets summarize the data that are anticipated to be collected during the PDI (PDIWP Section 3.4):

- Middle reach bathymetric survey data to support the potential refinement of Recovery Category areas, potential vessel scour areas, and applicable RALs. An initial bathymetric survey was conducted in October 2021, and the results will be provided as an appendix to the PDI QAPP. An additional bathymetric survey is anticipated to be conducted in 2022 to fill data gap areas that were not covered (due to presence of vessels and other obstructions preventing access) during the initial survey.
- Sediment chemistry data to delineate RAL exceedance areas, as noted earlier, and to determine the following:
 - Required dredge elevations in dredging areas and partial dredging and capping areas
 - Refined area boundaries of ENR and MNR to benthic SCO areas
- Possible collection of toxicity test data in areas where active remediation is anticipated if only benthic RAL exceedances exist
- Focused topographic survey data in bank areas with adjacent RAL exceedance areas that have dredging or capping remedies

¹² The ROD indicates that “where contaminant concentrations exceed RALs only at depths below the top 2 ft, cleanup may be deferred if USACE determines it is not currently an impediment to navigation, but must be dredged in the future if USACE determines that the area has become an impediment to navigation.” USACE will be provided the opportunity to comment on design documents as determined by EPA.

- Area-specific sediment geotechnical properties including geologic characterization, sediment index, and sediment strength and consolidation properties to achieve the following:
 - Determine sediment stability and stable dredge cut side-slope requirements
 - Characterize sediment dredgeability
 - Support sediment consolidation assessment for cap design
 - Support selection of dredge equipment
 - Support design of sediment handling, transport, dewatering, treatment systems, and disposal requirements
- Specialized surveys as appropriate for debris characterization
- Sediment transport and erosion/scour/disturbance process information (such as bathymetry and engineering analyses) to support the following:
 - Delineation of MNR and ENR areas
 - Design of ENR areas
 - Cap design
 - Outfall scour protection

3 Engineering Design Process

3.1 Design Objectives

This RDWP has been developed to support the preparation of a design that is constructable, environmentally protective, effective, and consistent with the ROD requirements. Sequencing the data collection that informs RD is important to ensure that appropriate data for RD are collected at the applicable phase of RD, and that the RD will be conducted so that design elements may be refined as new information becomes available.

When possible, the design will specify performance requirements instead of prescribing the means and methods of the remedial construction. Performance-based specifications describe the performance criteria that the contractor is required to meet during construction, which allows for the contractor to develop project-specific means and methods that take advantage of contractor creativity and expertise. The contractor will propose the specific means and methods in their RAWP, subject to approval by the Engineer and EPA. This approach also allows for adaptive management that can incorporate real-time lessons during construction rather than rigid prescriptive specifications. However, prescriptive method specifications will be used for those design elements that cannot be flexible (e.g., minimum cap layer thickness, sequencing and access constraints, etc.) and will also be used to set project-wide minimum requirements for communications, environmental protection, and health and safety.


3.2 Design Process

This section discusses the general design process phases for RD and how PDI data will be used in design. Figure 3-1 graphically depicts the progression of the RD process and how the various PDI and RD phases interrelate with one another.

3.2.1 *Pre-Design Investigation Phases*

The PDIWP (Appendix C) details the phased approach that will be used for the PDI. The first phase of sampling is generally focused on defining the horizontal extent of RAL exceedances by targeting sediment depth intervals with applicable RALs: surface sediment (0 to 10 cm), subsurface sediment (0 to 45 cm in intertidal areas and 0 to 60 cm in subtidal areas), and FNC shoaling intervals. The Phase I PDI data will be used to define initial remediation areas, identify any additional data gaps in the horizontal extents of contamination, help identify areas for vertical contamination extent investigation (e.g., the depth of contaminated sediment in dredging areas) in both open water and under structures, and help define investigation needs at adjacent bank areas.

Draft LDW Middle Reach Remedial Design Timeline

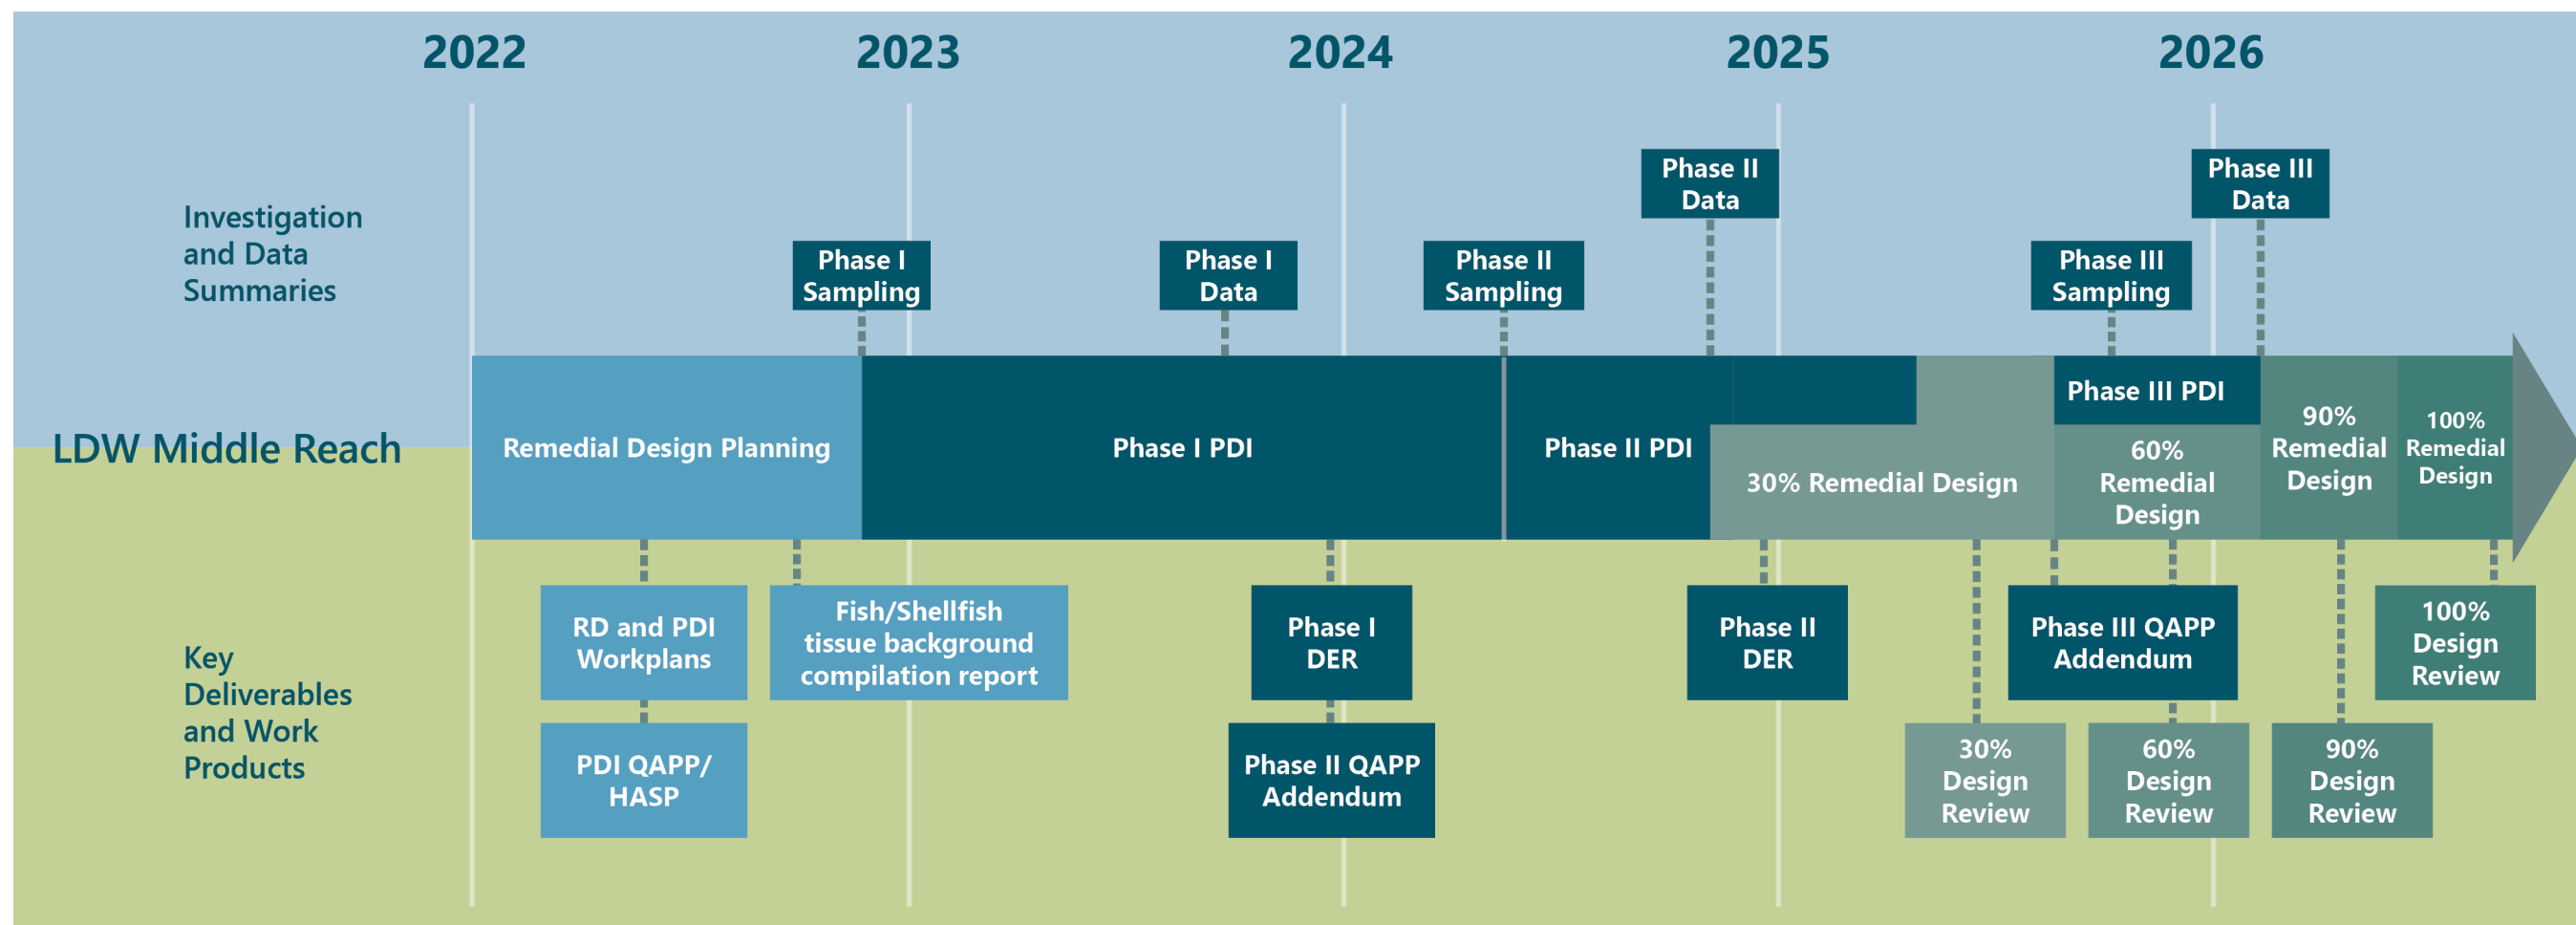

\\FUJI\Anchor\Projects\City of Seattle\LDW - Middle Reach\Task 300 RDWP\RDWP_Figures\source\Fig3-1_Timeline.docx
5/2/2022

Figure 3-1. LDW Middle Reach Remedial Design Timeline
REMEDIAL DESIGN WORK PLAN FOR LDW MIDDLE REACH

The Phase II PDI will focus on: addressing additional horizontal extent data gaps identified in Phase I to refine horizontal extents of required remediation areas; collecting subsurface data to define vertical extents of required dredging; and collecting engineering data (e.g., geotechnical, structural conditions, thickness of contaminated sediment overlying riprap-armored banks) to inform RD. LDWG may discuss with EPA the potential need to conduct some limited Phase II PDI type investigations during Phase I in difficult-to-access areas, due to the complexity in obtaining access to active waterfront facilities or facilities with long-term barge storage. Phase III PDI will be conducted, if necessary, to address any data gaps that remain following the Phase II PDI.

PDI Data Evaluation Reports will present the investigation results, in addition to refining the RAL exceedance areas (Section 3.3), revising Recovery Category designations (Section 3.4), and refining the preliminary technology assignments (Section 3.5).

3.2.2 Remedial Design Phases

RD is generally defined as those activities to be undertaken to develop construction plans and specifications, general provisions, special requirements, and other technical documentation necessary to solicit bids for construction of the remedial action. The RD also includes identification of the required documentation to be provided by the construction contractor, subject to approval by EPA, during the pre-construction and construction phases, and annotated outlines, conceptual plans, or initial drafts of certain documents to be finalized after construction.

The Preliminary (30%) RD will incorporate data from the Phase I and II PDIs. Key deliverables of the Preliminary (30%) RD package will include a draft BODR, preliminary plans (i.e., drawings), and an outline of the contract specifications.

The Intermediate (60%) RD package will incorporate EPA input on the Preliminary (30%) RD and advance the preliminary design concepts presented therein. Coordination with EPA and resource agencies will continue during Intermediate (60%) RD to ensure that the design is compliant with ARARs, and that approvals can be obtained in advance of the planned construction period.

The Pre-Final (90%) RD package will incorporate EPA input on the Intermediate (60%) RD, incorporate any data obtained during a Phase III PDI (if needed), and will be a near-final package including a CQAP and Water Quality Monitoring Plan (WQMP).

The Final (100%) RD package will incorporate EPA comments on the Pre-Final (90%) design submittal and include final versions of all supporting design deliverables. The remediation construction implementing entity will determine the requirements of the final bid document plans and specifications as noted in Section 1.5.1.

Outreach and coordination with waterway users and other stakeholders will take place before field sampling events, as detailed in the PDI QAPP. The components of each RD deliverable are discussed in detail in Section 6.

3.2.3 Design Process Sequencing

The following bullets provide a summary of the design process sequence to delineate remedial action areas, select remedial technologies, and delineate sediment management areas (SMAs; defined in Section 3.6) consistent with the RD phases and Figure 3-1:

- Collect bathymetry survey data.
- Perform site reconnaissance surveys prior to PDI sampling to assess existing shoreline and structures conditions.
- Phase I PDI
 - Develop sun-illumination maps (i.e., map with shading to enhance the appearance of bathymetric features).
 - Adjust Recovery Category area designations where appropriate based on new bathymetry (i.e., sun-illumination maps).
 - Collect Phase I PDI data.
 - Evaluate RAL exceedances.
 - Adjust Recovery Category area designations where appropriate based on Phase I PDI data.
 - Preliminarily delineate remedial action areas, using interpolation methodology.
 - Preliminarily assign remedial technologies.
 - Identify data gaps for Phase II PDI.
- Phase II PDI
 - Collect Phase II data including horizontal delineation data gaps identified in Phase I, vertical extent data, bank characterization data, and engineering data.
 - Finalize interpolated RAL exceedance areas for use in 30% RD.
- Preliminary (30%) RD
 - Develop remedial action areas.
 - Select remedial technology¹³ (i.e., dredge, partial dredge and cap, cap, ENR, ENR/AC, MNR).
 - Identify data gaps for Phase III PDI (if needed).
- Intermediate (60%) RD

¹³ It is expected that remedial technology assignment at the Preliminary (30%) RD will be roughly 90% complete, but remedial technologies in particular areas may be refined as design is further developed.

- Delineate SMAs considering common adjacent remedial technologies, site physical characteristics, constructability, and other engineering factors as appropriate.
- Design remedial actions (e.g., horizontal and vertical limits for dredging; cap thickness and erosion protection; ENR; treatment; dredging or capping construction offsets from existing infrastructure).
- Collect Phase III PDI data, if data gaps were identified during 30% RD.
- Pre-Final (90%) RD
 - Refine SMAs and RDs, if any, based on Phase III PDI.
- Final (100%) RD
 - Finalize RD.

The following sections provide additional details for several key design components of the RD process.

3.2.4 *Design Quality Control*

RD submittals to EPA will be reviewed using the design team’s internal quality control processes, and they will also be reviewed by LDWG, EPA, and other stakeholders including affected users. Analytical data are collected using EPA-approved QAPPs and validated to ensure the data are of suitable quality to make RD decisions.

Other internal quality control processes occur prior to submittals to EPA. Engineering designs are peer-reviewed internally by senior engineers, calculations are cross-checked, and experienced construction managers thoroughly evaluate implementation plans to ensure constructable designs. Constructability and value engineering reviews will be performed during the 60% design phase to gauge equipment and material availability, construction cost escalation, contractor concerns, and other risk factors that may impact implementation of the remedy.

3.3 Remedial Action Area Designation

The ROD provides RALs to be used in identifying areas that will require remedial action. The RALs are listed in ROD Table 28 (included in Appendix A of this report); these RALs vary for different Recovery Category areas, intertidal and subtidal areas, and in shoaled areas of the FNC. The RAL exceedance areas will be delineated by applying data interpolation method(s) to the design dataset for the middle reach, as defined in the PDIWP.

Once the interpolation method or a combination of methods (e.g., inverse distance weighting, kriging, Thiessen polygons) define the RAL exceedance areas, the remedial action areas will be defined in 30% design.

The remedial action areas identify the boundaries where remedial action will occur. Remedial action areas will be developed by taking the interpolated RAL exceedance areas and overlaying practical engineering and site condition considerations. The remedial action area boundaries will therefore encompass the RAL exceedance area boundaries.

Bank areas will be designated for remedial action based on the RALs identified in Table 28 of the ROD. Bank areas will be evaluated using the following general approach:

- Bank areas will be visually inspected during Phase I PDI to assess their general conditions (e.g., armored condition, stability).
- Phase I PDI results and coordination with MTCA site managers will inform which bank areas may exceed RALs and will be sampled during Phase II PDI.
- Armored banks in good condition will not be sampled below the armor layer; sediment overlying the armor layer may be sampled on banks adjacent to RAL exceedance areas.

3.4 Recovery Category Finalization

Recovery Categories and other considerations identified in the ROD define where remedial technologies can be used. Generally, Recovery Category 1 designates areas where only dredging and/or capping are applicable; Recovery Categories 2 and 3 designate areas where MNR, ENR, dredging, and capping are all applicable.

ROD Table 23 (included in Appendix A of this report) summarizes the criteria used to assign final Recovery Categories. The *Recovery Category Recommendations Report* (Integral et al. 2019) evaluated the Recovery Category designations in the ROD based on the waterway user survey and new chemistry data and recommended minor revisions. Within the middle reach, two locations were modified: Boyer Towing at RM 2.3W, and Waste Management transload property at RM 2.8E. Both locations were modified from Category 3 to Category 2 based on site use (vessel berthing).

The PDI QAPP and the Phase I and Phase II PDI Data Evaluation Reports will review, and potentially revise, the Recovery Category designations using new bathymetric survey and PDI chemistry data. These final Recovery Category boundaries will then be used in RD.

3.5 Remedial Technologies Assignments

A remedial technology or technologies will be assigned to each remedial action area. Preliminary remedial technology assignments presented in the ROD will be refined during RD based on PDI data and engineering judgment. The remedial technologies will be assigned based on ROD criteria summarized in ROD Tables 27 and 28 and Figures 19 through 23 (included in Appendix A of this report). The technology assignment criteria in the ROD include the following:

- RAL exceedance and magnitude of exceedance (i.e., upper limit for ENR)
- Recovery Category
- Bathymetric elevation (intertidal, subtidal, and bathymetric elevation compared to future maintenance dredging)
- FNC and berthing area maintenance dredging requirements (e.g., horizontal and vertical tolerances compared to maintenance dredge depths)
- Access constraints and the presence of structures

The remedial technology assignments will also consider equipment tolerances, structure protection offsets, constructability, proximity to outfalls, debris, potential restrictions on future waterway use and related institutional controls, and the conditions in adjacent areas. Per ROD Section 13.2.4, where institutional controls would interfere with waterway activities required for use of a particular area, dredging may be required instead of capping. Areas where this may be the case will be identified in the DER.

The QAPP and the Phase I and Phase II PDI Data Evaluation Reports will review, and potentially revise, the remedial technology assignments using new bathymetric survey and PDI chemistry data and using the revised Recovery Category delineations described in Section 3.4. This step is necessary in order to collect the appropriate data for the next phase of PDI (such as vertical extent in dredge areas or lateral extent of ENR areas.) The technology assignments will continue to be revised in the RD submittals.

3.6 Sediment Management Areas Designation

Once the middle reach remedial action areas are delineated and remedial technologies are assigned to each remedial action area, the middle reach will be divided into SMAs in the Intermediate (60%) RD (where appropriate). SMAs represent discrete areas within the site in which different remedial technologies may be implemented or where unique constructability issues may exist. SMAs are discrete areas within the larger site that can be managed differently from one another using the applied technology and monitoring, but are considered part of the larger site. SMAs provide a method for referencing individual remedial action areas in the bid

documents, and a method for overlaying constructability considerations in the assignment of remedial technologies to an SMA. SMA designations will rely on engineering judgment.

In many cases, a remedial action area boundary will naturally form a discrete unit that will become its own SMA. In other cases, a contiguous remedial action area may be split into two or more SMAs based on physical constraints or use of multiple remedial technologies. Some of the considerations for delineating SMAs will include the following:

- **Sediment stability.** SMA delineation will consider sediment stability, including scour potential, proximity to berthing areas and outfalls, and the location of steeper slopes (e.g., banks and adjacent to FNC). Uncertainty in Recovery Category boundaries, when developing SMA delineation, will be addressed by considering Recovery Category designations in adjacent areas.
- **Structures and offsets.** Areas under structures that require remediation will be evaluated to assess whether it makes sense to delineate them as separate SMAs. In addition, SMA delineation will consider structural offsets needed to protect overwater structures, engineered slopes, and utilities.
- **Site physical conditions.** The SMA delineation will consider site physical conditions, such as the FNC, berthing areas, intertidal areas, habitat areas that are defined as areas where bathymetric elevations are shallower than -10 ft MLLW, and habitat restoration sites, for compliance with the Endangered Species Act and Section 404 of the Clean Water Act.
- **Constructability.** SMA delineations may be influenced based on constructability considerations, such as equipment access, presence of piling and debris, and location of structures.

The SMA delineations may be refined throughout the design process as the RD progresses in each area. The transition between each SMA and adjacent areas (e.g., other SMAs or EAAs) will be designed to provide a constructable and stable transition.

3.7 Remedial Technologies Design Considerations

3.7.1 Dredging

For areas where dredging is the selected remedial technology, dredging design will be guided by the *USACE Technical Guidelines for Environmental Dredging of Contaminated Sediments* (Palermo et al. 2008) and engineering professional judgment based on past sediment remediation designs. The dredging design will consider lessons learned from EAAs and other cleanup sites discussed in Section 2.3.3.

The first step in the dredging design process will be to define the horizontal and vertical extents of dredging based on PDI data, then calculate resulting dredge areas and volumes. The dredge areas and volumes will be refined throughout RD considering constructability and protection of infrastructure and utility areas. The extent of the dredge areas will be presented on design drawings.

As identified in the ROD (Section 13.2.1.1), if 1 ft or less of contaminated sediment would remain at concentrations greater than the human health RALs or the benthic SCO after dredging to sufficient depth to accommodate a cap, all contaminated sediments are required to be dredged. If more than 1 ft of contamination would remain after dredging to sufficient depth to accommodate a cap, sediments can be partially dredged and capped.

Following the initial definition of the dredge areas and volumes, different types of dredging equipment and material transport systems will be evaluated based on project requirements, site conditions, and implementation efficiencies. Factors influencing the selection of the types of dredging equipment to be used include but are not limited to the following:

- Water depth to accommodate equipment draft
- Mobilization and site access constraints
- Dredge cut thickness
- Presence of debris
- Sediment type and physical or geotechnical characteristics
- Production rates and schedule requirements
- Dredged material transport methods
- Availability and locations of potential transload facilities
- Environmental monitoring requirements

Identification of anticipated dredging equipment types (e.g., mechanical versus hydraulic dredging) will occur as early in the design process as practicable to allow for progress on dependent design processes (i.e., material handling, transloading, and transport). The selected remediation contractor will select and identify its dredging equipment and construction means and methods in the contractor's RAWP. However, the RD may specify general types of dredging equipment (e.g., mechanical versus hydraulic dredging) to be used for specific site conditions in order to reduce construction uncertainties.

Throughout the design process, dredge area boundaries may need to be refined based on concurrent design activities. Where dredging occurs near the bank and structures, the dredge design will evaluate the stability of both the existing bank side slopes and the new side slopes that will result from dredging. In addition, identification of cultural resources, critical habitats,

and utilities may require modifications to the design dredge prism. A slope setback may be required in areas where the design dredge prism may undermine the toe of the slope or existing structures to prevent undermining or reducing the stability of slopes and structures. An alternate remedial action may be required to manage the remaining contaminated sediment that cannot be removed. The extent of any necessary slope setbacks or structural offsets and how remaining contaminated sediment will be managed will be presented on the design drawings.

The Preliminary (30%) RD will develop an overall dredging strategy and preliminary dredging plans showing the horizontal and vertical limits of dredging based on the results of PDI data and other considerations. The Preliminary (30%) RD will also include a list of the relevant technical specifications governing dredging.

The Intermediate (60%), Pre-Final (90%), and Final (100%) RD phases will refine dredging plans based on additional data collection after the PDI phases, siting of marine access points and materials transport, and results of infrastructure information not available at the Preliminary (30%) RD phase. In addition, subsequent phases of RD will evaluate and identify anticipated dredge equipment types and methods based on the required dredge extents and site conditions, building from the Preliminary (30%) RD. The specifications outlined during the Preliminary (30%) RD will be further developed and finalized during subsequent RD phases, and in response to EPA comments.

3.7.1.1 Dredging Design Factors for Federal Navigation Channel and Shoaled Areas

Shoaled areas are defined in the ROD as areas in the FNC with sediment accumulation above the FNC authorized depth in the middle reach (-30 ft MLLW from RM 1.6 to RM 2, -20 ft MLLW between RM 2 to RM 2.8, and -15 ft MLLW from RM 2.8 to RM 3.0). As described in the ROD (Section 13.2.1.1), shoaled areas in the FNC will be dredged as the remedial action if contaminant concentrations exceed RALs at any elevation above the authorized depth plus 2 ft below, which is the maintenance depth in the middle reach (i.e., 2 ft below the authorized depth, or -32 ft MLLW from RM 1.6 to RM 2, -22 ft MLLW between RM 2 to RM 2.8, and -17 ft MLLW from RM 2.8 to RM 3.0). The RD will consider the USACE's FNC authorized navigation depths, over-dredge requirements, and lateral offsets from the channel as required by the ROD. When dredging is required within and to the edge of the FNC, the dredge prism will extend an additional 10 ft (lateral) outside of the FNC.

Partial dredging plus capping design within the FNC and shoaled areas will also factor in any follow-on capping such that all post-remedy surfaces in these areas will be maintained at or below the ROD-mandated FNC authorized depth offsets.

3.7.1.2 Dredging Design Factors for Areas Outside the Federal Navigation Channel

Outside the FNC, the dredge design will consider navigation depths that are maintained by private or public entities (called berthing areas in the ROD, but could include slips, entrance channels, or restoration areas).

Dredging may be required in some areas that would otherwise be designated for capping if institutional controls required to prevent damage to a cap (such as deed restrictions) are not compatible with the current or reasonably anticipated future use of that area.

The dredge design and required follow-on material placement activities (e.g., capping, backfill, or RMC) would be designed to avoid the loss of aquatic habitat and preserve an appropriate range of habitat elevations in the intertidal zone. Habitat design considerations are discussed further in Section 3.8.

3.7.1.3 Dredging Design Factors for Infrastructure and Slope Areas

The RD will incorporate design factors when dredging adjacent to existing infrastructure, utilities, and slopes. During the 30% and 60% design phases, the RD will identify areas where dredging is impractical based on the operational characteristics of the dredging equipment and equipment access constraints. In addition, dredging may need to be offset from existing slopes and structures to prevent adverse impacts to stability. Dredging offsets and slopes for protecting existing structures and utilities will be developed during the 30% and 60% design phases and will consider factors such as the type of utility (e.g., power, drainage, communications) or type and condition of existing structures.

In locations where standard dredging equipment cannot remove the material due to obstructions, or where offsets for structural stability prevent removal, alternate remedial technologies will be evaluated in coordination with EPA during the 30% and 60% design phases (e.g., under structures and in the vicinity of dolphins/piling, bulkheads, and riprapped or engineered banks).

Debris and abandoned pilings will be removed or replaced from remedial action areas in the middle reach as necessary or as required by EPA to implement the remedy. In some circumstances, removal in the vicinity of certain infrastructure will require structural and/or geotechnical engineering assessments of the infrastructure; in such cases, alternate means for sediment removal will be evaluated on a case-by-case basis. Potential obstructions may include but are not necessarily limited to the following:

- Structures (e.g., bridge abutments, wing walls, bulkheads, mooring dolphins) whose structural stability may be adversely impacted by dredging

- Low clearance structures (such as bridges and piers)
- Armored banks
- Other physical obstacles within the waterway that cannot be removed (e.g., concrete cribs, very large boulders, bedrock, stormwater outfalls)
- Buried utilities or utility crossings (underground or overhead)

3.7.1.4 Sediment Resuspension Management During Dredging

Dredging activities will result in resuspended sediment. Some causes of resuspension include disturbance of the bed by dredging buckets (mechanical dredging) or hydraulic cutterheads (hydraulic dredging), loss of sediment from dredging buckets as the bucket is raised or lowered through the water column, propwash disturbance from dredging equipment and attendant vessels (e.g., tugboats), sediment spillage or discharge from haul barges, debris preventing bucket closure, and disturbance from dredge or barge anchoring. Areas with high debris density will experience higher sediment resuspension during removal (USACE 2008a).

The RD will evaluate potential methods to reduce sediment resuspension during dredging activities (e.g., best management practices [BMPs] for operational controls, specialized dredging equipment such as an environmental bucket). A range of BMPs to reduce sediment resuspension will be evaluated and described in the BODR. The feasibility and effectiveness of various BMPs is dependent upon project- and site-specific considerations, including the following:

- Water quality compliance criteria
- Water depth
- Waterway velocities and flow
- Vessel traffic frequency
- Waterway constraints for installing or anchoring resuspension barriers (e.g., navigation, Tribal Usual and Accustomed fishing)
- Waterway elevation variability
- Dredging equipment and methods
- Geotechnical properties of dredge material
- Waterway access

A WQMP will be developed (see Section 6.2.3) during RD to provide a mechanism to assess water quality during in-water remedial actions, evaluate the overall effectiveness of the control approach, and inform contingency actions to address potential water quality criteria exceedances.

3.7.1.5 In-Water Dredged Material Transport

The design for dredged material in-water transport is directly linked with the dredging methods and dredged material handling, dewatering, and water treatment. The anticipated dredged material in-water transport design will be based on the dredge equipment type selection during RD. Dredged material in-water transport methods and performance requirements will be identified and finalized in combination with dredge equipment type and anticipated dewatering processes. Minimum performance requirements for in-water transport (e.g., spill prevention, barge loading, U.S. Coast Guard requirements, barge seaworthiness) will be included as performance specifications.

The selected remediation contractor will be required to prepare a Vessel Management Plan. The minimum requirements for the plan will be developed at the Pre-Final (90%) RD phase and will include information about anticipated vessel operations necessary to complete the remedial actions such as types of vessels, access points, and vessel frequency.

3.7.1.6 Dredged Material Handling, Dewatering, and Water Treatment

Dredging operations will require material handling, potential dewatering, and potential water treatment to prepare the dredged sediment and debris for disposal at an off-site landfill. The design and location of the material handling processes will be informed by the removal technology, transport constraints, requirements of the disposal facility, and the upland transport method used to transport the material to the disposal facility.

Design for material handling, potential dewatering, and potential water treatment activities will consider the following elements:

- Space and area available along the river for material transloading, temporary stockpiling, potential dewatering, and potential water treatment
- Availability and capacity of commercial transload facilities
- Amount and type of debris to be processed
- Dredging volumes
- Dredging production rates
- Dredged material physical characteristics
- Results of sediment treatment study work (if necessary) to be performed in support of these operations (e.g., leachate testing and *ex situ* stabilization)
- Amount of water to be treated, if necessary
- Water discharge requirements (e.g., barge discharge, transload facility discharge)
- Transport and offloading methods from the in-water work area to transload facility and then to disposal facility


The Preliminary (30%) RD will evaluate potential locations for commercial transload facilities and water treatment operations (if needed) as discussed in Section 4.5. The Preliminary (30%) RD will also assess the potential need and property availability for constructing a new, dedicated middle reach transload facility. The actual location of a transload facility will be finalized in the contractor's RAWP due to the dependency on contractor means and methods, the available space (which could change over time), and the disposal facility's dredged material acceptance criteria. Design plans and specifications will be developed to identify performance requirements for material transloading, handling, potential dewatering, potential water treatment, and discharge that are compatible with site constraints and comply with ARARs and EPA requirements.

3.7.1.7 Upland Dredged Material Transport and Disposal

Building on the results from the dredge material handling, dewatering, and water treatment evaluation, upland transportation and disposal processes will be evaluated and potential transloading and disposal facility locations and transport methods will be preliminarily identified. The operational constraints imposed by available sediment transload, available rail and/or truck transport capacity, and disposal facilities may affect dredging production rates, in-water transportation design, waterway access, rail or truck transload design, and potential sediment dewatering and water treatment design. The potential locations for the transload and disposal facilities will be evaluated during Intermediate (60%), Pre-Final (90%), and Final (100%) RD so that results may be factored into the design reports and construction bid documents. Trucking and rail transport requirements (e.g., lined and covered truck beds or containers), haul route requirements (e.g., routes, dust control), and disposal facility requirements (e.g., documenting facility permits and approvals) will be evaluated throughout RD and presented in the BODR.

3.7.1.8 Dredge Residuals Management

Dredge residuals refer to the contaminated sediments found at the post-dredge surface, either within or adjacent to the dredging area, as depicted in Figure 3-2. Generated residuals refers to contaminated sediments that have been disturbed or resuspended by the dredging equipment but not captured and therefore settled back to the sediment bed; they tend to be relatively thin deposits (e.g., on the order of inches). Missed inventory (i.e., undisturbed residuals) refers to contaminated sediments that have been uncovered but not removed from within the remedial action area. The primary causes of missed inventory are incomplete characterization that may result in the RD not completely capturing the full contamination depth in pockets within the remedial action areas, and incomplete dredging due to technical and logistical limitations (e.g., structural setbacks) (USACE 2009).

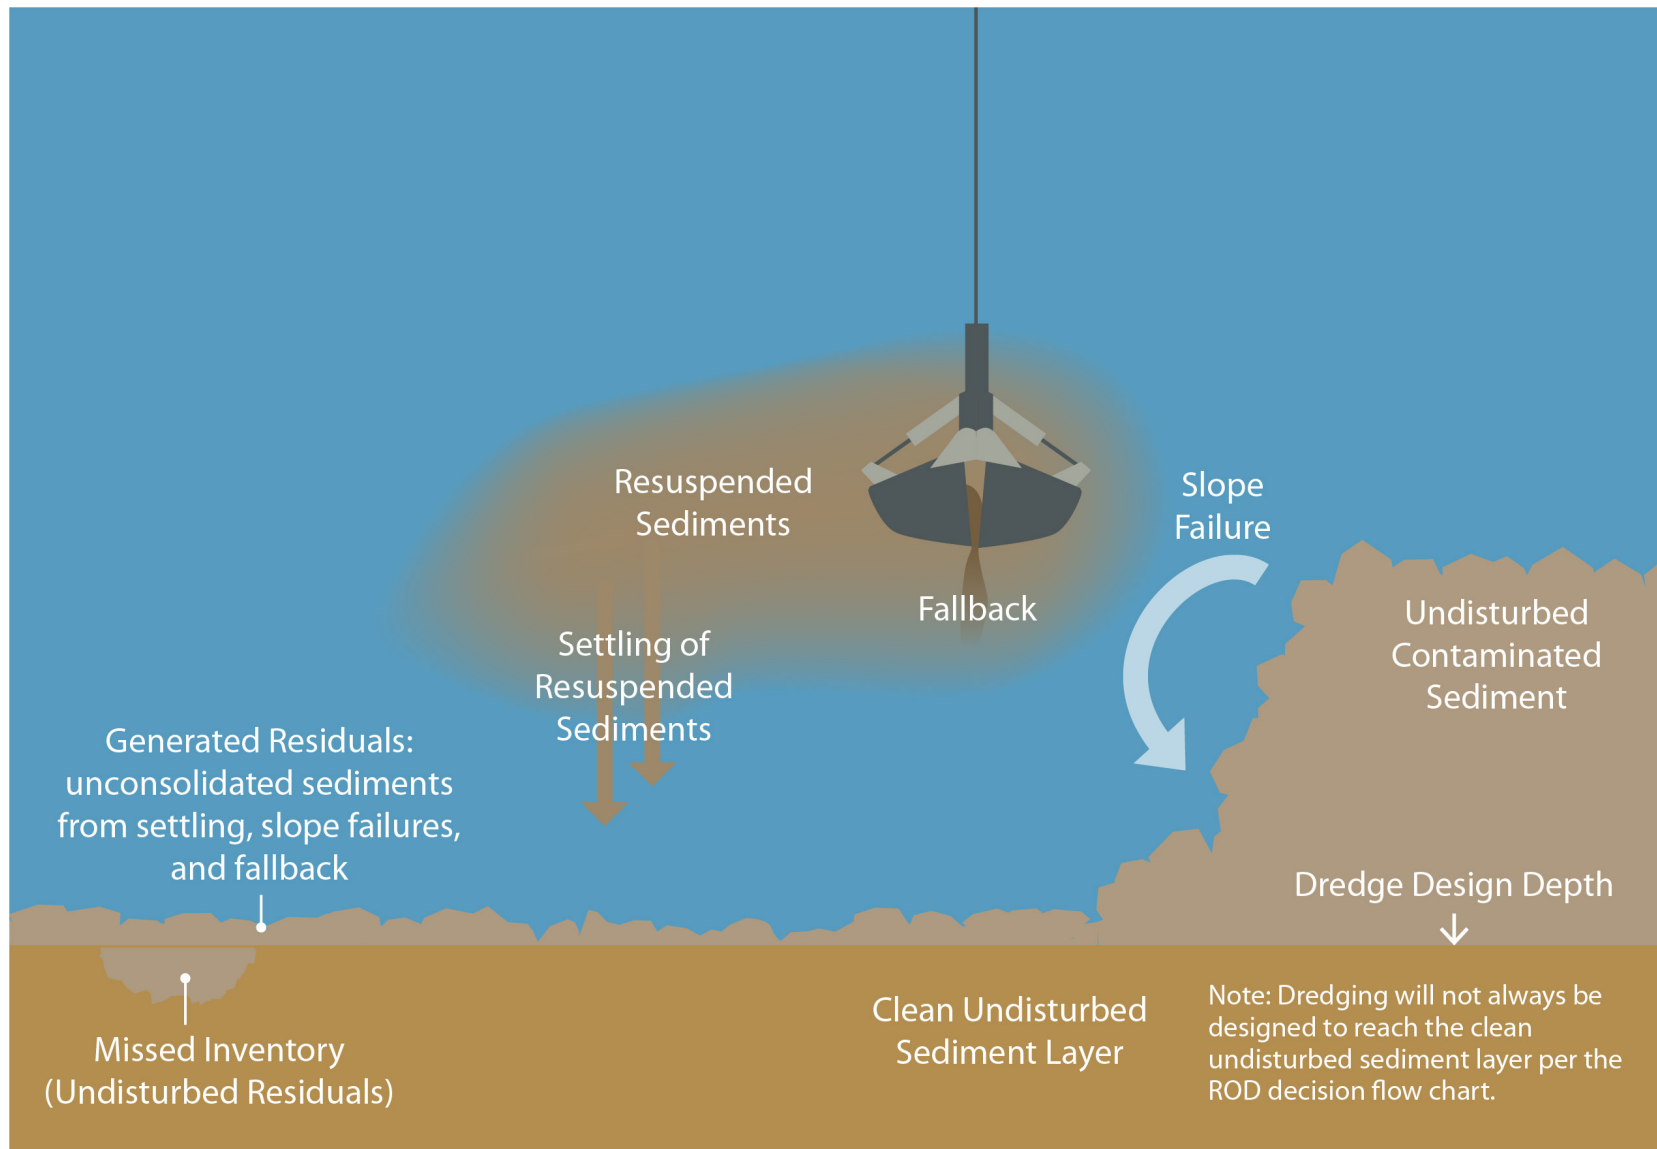

\\FUJI\Anchor\Projects\City of Seattle\LDW - Middle Reach_Task 300 RDWP\RDWP_Figures\source\Figure 3-2_DredgeResiduals.docx
5/2/2022

Figure 3-2. Dredge Residuals Schematic
REMEDIAL DESIGN WORK PLAN FOR LDW MIDDLE REACH

The RD will develop a multiple-pronged strategy that anticipates dredge residuals and establishes a phased approach to proactively plan for and respond to them. LDWG will work with EPA to determine how to discern generated residuals from missed inventory and what actions would be required to manage residuals. Dredge residuals will be managed by including appropriate dredging performance standards in the specifications, developing a dredge residuals monitoring approach and decision framework in the CQAP, and including appropriate dredge residuals response requirements in the plans and specifications.

The three general management approaches for dredge residuals are anticipated to include contingency re-dredging, RMC, and MNR (USACE 2008b). Contingency re-dredging can be conducted to attempt to reduce contaminant concentrations at the surface, but this approach has often been inefficient with little reduction in residual concentrations (USACE 2008a). Typically, contingency re-dredging is used to target only high-concentration dredge residuals or pockets of missed inventory.

The second management strategy is to place clean sand RMC. This approach provides greater certainty in achieving dredge residuals performance criteria (USACE 2008a) and RMC is regularly used to manage thin deposits of generated residuals. Placing RMC has a similar purpose as placing an ENR layer to accelerate the natural recovery process and is described further in the next section.

After required dredging is completed, and in areas where the residuals concentration is sufficiently high (as determined by post-dredge compliance testing), RMC may be used to address dredge residuals. The RMC is typically a relatively thin layer (e.g., nominally 6 to 12 inches [15 to 30 cm]) of clean sand as determined during RD. If generated residuals result in concentrations above RALs within the federal navigation channel, alternatives to RMC alone may be necessary to avoid final elevations that exceed the authorized depth plus allowable overdredge. The RD will include the following RMC design components:

- Materials specifications
- Potential material source identification
- Estimates of surficial post-dredge residual contaminant concentrations
- RMC thicknesses
- RMC horizontal extents
- RMC placement methods

3.7.1.9 Post-Dredge Backfilling

Backfilling dredged areas with clean material will be necessary in some areas to restore pre-dredge elevations for habitat purposes. Backfill can also serve a residuals management

function. The RD will include design of backfilling integrated, as appropriate, with the design for habitat replacement and reconstruction (see Section 3.8). The backfilling design will include the following:

- Materials specifications
- Potential material source identification
- Estimates of surficial post-dredge residual contaminant concentrations
- Backfill thicknesses
- Backfill horizontal extents
- Backfill placement methods

3.7.2 Capping

The RD for cap areas will consider the physical, chemical, hydrodynamic, and hydrogeological properties of cap areas. These factors include bathymetry, existing infrastructure and obstructions, groundwater advection, bioturbation, intertidal site use, and potential erosive forces, such as current velocities, propwash, and wave or wake action.

Caps will be designed to isolate and stabilize existing sediments in general accordance with the *Assessment and Remediation of Contaminated Sediment Program Guidance for In Situ Subaqueous Capping of Contaminated Sediments* (Palermo et al. 1998). The guidance document recommends a generalized approach to designing an *in-situ* cap, including considerations of the following specific design components:

- Assessment of the potential contaminant mobility from the sediment into the water column, and design of a cap component to prevent breakthrough within a given design life
- Assessment of bioturbation potential of local burrowing benthic organisms, and design of a cap component to physically isolate them from contaminated sediment
- Assessment of cap design in intertidal areas where potential clamming may occur
- Evaluation of construction and placement methods, and identification of performance objectives and monitoring methods for cap placement and long-term assessment
- Identification of candidate capping materials that are physically and chemically compatible
- Assessment of the operational considerations and determination of restrictions or additional protective measures (e.g., institutional controls) needed to ensure cap integrity
- Evaluation of the long-term effects of sea level rise and climate change on cap integrity

In addition, the following design consideration will also be evaluated:

- Assessment of intertidal seeps and preferential groundwater flows that affect groundwater velocities and cap construction in intertidal areas

Cap modeling performed during RD will determine the cap thickness, cap material types, and material gradation. The cap will be designed to resist the following erosive forces, as applicable:

- **Hydrodynamic flows:** The caps will withstand scour from high-flow events. Caps near outfalls will be designed to withstand currents associated with the outfall flows, including surface flows at low tide.
- **Propwash and wakes:** The cap design will assess the potential forces from propwash and vessel-generated wakes. Representative recreational and commercial vessels will be selected for evaluation during RD; the selected design criteria vessel(s) will be identified in the BODR.
- **Wind-generated waves:** The effects of wind-generated waves will also be evaluated during the cap design, although the wind-generated wave impacts are expected to be minor relative to the other erosional forces in the middle reach. The capping design consists of several steps that are integrated with the other major design components. The first step in the capping design is to identify the areal extent of capping that can be used as described in Sections 3.3, 3.4, and 3.5. Identification of critical habitats and utilities may require modifications to the extent of capping. The areal extent of capping will be used to quantify capping areas and cap material volumes. ROD Figures 19 and 20 (included in Appendix A of this RDWP) identify where capping may be used.

The materials at the top of the cap (i.e., cap surface) will be sized to resist erosive forces, and available material sources will be considered in developing cap material specifications. Once cap material volumes and material specifications have been developed, a combination of performance and method specifications will be developed to specify means and methods for cap material transport, handling, and placement.

The Preliminary (30%) RD will develop preliminary capping plans (i.e., drawings) showing the horizontal limits of capping. The Preliminary (30%) RD will also include a list of the relevant technical specifications related to capping.

The Intermediate (60%), Pre-Final (90%), and Final (100%) RD phases will refine capping plans, siting of marine access points and capping materials transport, and results of infrastructure information not available at the Preliminary (30%) RD phase. Prospective sources of cap material and methods for transporting the material will be identified. The specifications outlined during

the Preliminary (30%) RD will be further developed and finalized during subsequent RD phases, and in response to EPA comments.

3.7.2.1 Capping Design Factors for Federal Navigation Channel

Capping design within the FNC will consider final post-remedy surface elevations, such that they are maintained at or below the ROD-mandated authorized depth offsets. In order to avoid potential damage to a cap during federal maintenance dredging, the top of any cap will be at least 4 ft below the FNC-authorized depth as required by the ROD.

3.7.2.2 Capping Design Factors for Intertidal Areas and Areas Outside Federal Navigation Channel

For areas outside the FNC where navigation depths are maintained by private or public entities (called berthing areas in the ROD, but could include slips or entrance channels), any capping remedial action will have a top surface at a minimum of 2 ft below the operating depth as determined during RD.

Material placement (e.g., capping, backfill, or RMC) would be designed to avoid the loss of aquatic habitat and preserve an appropriate range of habitat elevations in the intertidal zone. This includes cap thickness and material selection design considerations within Tribal clamming areas in the intertidal zone. Habitat design considerations are discussed further in Section 3.8.

3.7.2.3 Capping Design Factors for Infrastructure and Slope Areas

The RD will incorporate cap design factors when capping adjacent to or under existing infrastructure, utilities, and slopes. The RD will identify areas where capping may be impractical based on the operational characteristics of the capping equipment and the presence of permanent structures or obstructions that could potentially interfere with capping activities.

Besides the potential impact to water depths, capping can also have adverse impacts to structure and slope stability due to the added weight of the cap. Similar to dredging, cap placement offsets may be necessary to prevent impacts to the stability of existing structures, slopes, and utilities. The cap design will consider factors such as the type and condition of existing structures and slopes, and the geotechnical conditions of areas of stability concern. The extent of any necessary slope setbacks or structural offsets and how remaining contaminated sediment will be managed will be presented on the design drawings.

In locations where standard capping equipment cannot place cap material due to obstructions, alternate methods for placing cap materials will be evaluated. The design will consider applying

location-specific capping technologies to areas with structural or access constraints (e.g., under structures and in the vicinity of dolphins/piling, bulkheads, and riprapped or engineered banks).

Potential obstructions are similar for capping and dredging equipment and may include but are not necessarily limited to the following:

- Structures (e.g., bridge abutments, wing walls, bulkheads, mooring dolphins) whose structural integrity may be adversely impacted by capping
- Low clearance structures (such as piers)
- Other physical obstacles within the waterway that cannot be removed prior to capping (e.g., concrete cribs, very large boulders, bedrock, stormwater outfalls)
- Buried utilities or utility crossings

3.7.2.4 Sediment Resuspension Management During Capping

Capping activities will result in turbidity impacts. Most of this turbidity will be from fines contained in the clean cap material as it descends through the water while being placed; however, some resuspension of the bed sediment may occur depending upon the contractor's cap placement method. Sediment resuspension during capping may also result from propwash disturbance from capping equipment and attendant vessels (e.g., tugboats), clean material spillage from haul barges, and disturbance of the bed from capping equipment or barge spudding/anchoring.

Disturbance of the existing bed sediments during capping is commonly managed by specifying limits on the initial lift thickness of the cap material, to avoid bearing capacity failure of the sediments, as well as requiring placement techniques that spread the cap material.

Turbidity from clean fines in the capping material can be reduced to an extent by limiting the fines content in the materials specification. However, some fines are always present and the need to evenly spread the capping material will result in the resuspension of the clean fines.

Many of the other resuspension mechanisms mentioned above can be limited through BMPs, such as avoiding spudding or propwash (as practical) in cap placement areas.

Capping operations have been used extensively in the Pacific Northwest and nationally to isolate contaminated sediment. Lessons learned from many previous sediment remediation projects indicate that special equipment or barriers are not necessary to ensure protectiveness during clean cap placement operations. The BODR will identify proven BMPs typically required during capping operations that the contractor will be required to follow in order to limit sediment resuspension in addition to performance specifications.

3.7.3 *Enhanced Natural Recovery*

ENR entails placing a thin layer (nominally 6 to 9 inches thick [15 to 23 cm]) of clean material to accelerate natural recovery processes. ENR is not applicable in Recovery Category 1 areas. In Recovery Category 2 and 3 areas, ENR may be selected for intertidal and subtidal areas based on COC concentrations and the potential for sediment scour, as indicated in ROD Table 28 and on ROD Figure 17 (included in Appendix A of this report).

The RD will design ENR thickness considering material type, placement tolerances, and protectiveness. Habitat-compatible ENR material specifications will be developed during RD for habitat areas as discussed in Section 3.8. The ENR may include *in situ* treatment using AC or other amendments as discussed in Section 3.7.5.

3.7.3.1 **Enhanced Natural Recovery Design Factors for Federal Navigation Channel**

The ENR design within the FNC will consider final post-remedy surface elevations, such that they are maintained at or below the ROD-mandated authorized depth offsets. The top of any ENR layer will be a minimum of 2 ft below the FNC-authorized depth.

3.7.3.2 **Enhanced Natural Recovery Design Factors for Areas Outside Federal Navigation Channel**

For areas outside the FNC where navigation depths are maintained by private or public entities (called berthing areas in the ROD, but could include slips, entrance channels), the surface of any ENR layer will be a minimum of 2 ft below the operating depth, as determined during RD.

The ENR design will consider factors such as the type and condition of existing slopes and banks, and the geotechnical conditions of areas of stability concern, to determine effectiveness and stability of ENR materials in these areas.

3.7.3.3 **Sediment Resuspension Management During Enhanced Natural Recovery Placement**

ENR placement will result in resuspended sediment similar to capping placement as described in Section 3.7.2.4. The BODR will identify BMPs that the contractor will be required to follow to limit potential sediment resuspension during ENR placement operations.

3.7.4 *Monitored Natural Recovery*

MNR will be applied in all areas below the benthic RALs but above the benthic SCO (remedial action objective [RAO] cleanup level) that are not remediated through capping, dredging, or ENR. For all areas where MNR is applied, compliance monitoring of surface sediments (top

10 cm) will be implemented to evaluate whether the RAO 3 cleanup levels (benthic SCO criteria) are being achieved in a reasonable time frame or are not met within 10 years after remediation.

A decision framework will be developed in the LTMMP to identify potential contingency measures if RAO 3 is not met in a reasonable restoration time frame. In contrast, MNR below benthic SCO areas will be monitored as part of the site-wide monitoring program to track progress toward achieving RAOs 1 and 2.

3.7.5 *In Situ Treatment*

Based on the results of the ENR/AC pilot study (Wood et al. 2021), improvements achieved by adding AC to ENR were inconsequential within the PCB concentration ranges and timeframes evaluated. Therefore, EPA and Ecology have decided there is also no clear benefit in adding AC to ENR in the LDW. However, AC may be used as a layer in sediment caps or where waterway structures (like docks) make dredging or capping contaminated sediment difficult. The effectiveness and potential impacts of using *in situ* treatment or amendment technologies, as well as the areas best suited for these technologies, will be defined during RD considering the findings from the ENR/AC pilot study (see Section 2.3.2), the PDI results, and other considerations.

In some of the Recovery Category 1 areas adjacent to structures (e.g., the bridge piers) where dredging setbacks will be required, EPA may approve the use of *in situ* treatment (using AC or another amendment). EPA may also consider ENR with *in situ* treatment in areas with COC concentrations up to the benthic cleanup screening level if it can be demonstrated that it will maintain its stability and effectiveness over time.

3.8 Habitat Design Considerations

To meet the substantive requirements of the Endangered Species Act and Section 404 of the Clean Water Act, sensitive species and their habitat will be identified within the active remediation areas as part of a biological assessment. The biological assessment (BA) will be prepared as a Pre-Final (90%) RD submittal and will evaluate potential impacts associated with the remedial actions.

A goal of the RD is to reestablish habitats impacted by the remedial activities, which may include restoring intertidal area elevations and substrate (i.e., restore dredged areas to pre-dredge elevations with suitable backfill). The RD will include an evaluation of pre-construction and proposed post-construction habitat areas and substrates, which will be considered in the Endangered Species Act consultation and Section 404(b)(1) evaluations. Materials used for caps,

ENR, and backfill placement will be evaluated to assess habitat suitability in consultation with EPA. During RD, details and specifications will be developed for habitat elements for the reestablishment of targeted habitats.

EPA will use the information in the BA and the RD to conduct their Endangered Species Act consultation.

3.9 Other Design Considerations

3.9.1 *Climate Change*

Climate change impacts potentially affecting the greater Puget Sound region and relevant to the LDW include sea level rise; changes in precipitation patterns; and overall hydrological changes. Climate change adaptation generally focuses on evaluating the system's vulnerability to climate change and implementing adaptation measures, when warranted, to ensure the remedy continues to prevent human or environmental exposure to contaminants of concern (EPA 2015b).

3.9.2 *Sea Level Rise*

Climate change is expected to continue to increase sea levels over the next few hundred years (CIG/UW 2017). Anticipating an increase in mean sea level will correspond to a likewise increase in design water levels at the site; however, not all components of the RD are anticipated to be affected by an increase in design water levels. For example, dredging will not be impacted by the increase in water depth, and caps and ENR layers are designed for constant or tidal immersion. The design of engineered components of the remedy (e.g., shoreline caps) will need to incorporate potential long-term impacts from climate change by including erosion-resistance aspects (i.e., increasing elevations of anticipated shoreline stabilization; Webb and Schuchardt 2017).

3.9.3 *Hydrodynamics*

Increases in design water levels may result in a change (e.g., decrease) to bottom currents due to river/tidal currents and propwash velocities. These changes in bottom currents will be considered in the RD for engineered caps. In addition to rises in sea level, the increase of flooding in low-lying areas, higher tides, increased storm intensity and frequency, and heavier precipitation events could change LDW flow velocities and/or the frequency of high-flow events; however, ongoing water management practices at the Howard Hanson Dam effectively control peak river flows (USACE 2014; Brettmann 2017). The *Adaptation Strategies for Resilient Cleanup Remedies* (Ecology 2017) identifies potential vulnerabilities for sediment cleanup sites, such as

the increased risk for scour, erosion, and habitat loss; the compromise of overwater structures; and the effect on remedy integrity and performance (e.g., caps, ENR).

Additional modeling of climate change on future hydrodynamics is not necessary for RD. First, propwash velocities tend to control cap design because they are much higher than velocities due to river flows. Second, ongoing water management practices at the Howard Hanson Dam effectively control most peak river flows in the Duwamish River (USACE 2014). Sea level rise will be considered external to the hydrodynamic model for similar reasons.

3.9.4 *Sediment Load*

Uncertainties in estimates of sediment load were evaluated as part of the RI/FS process. Climate change impacts and land use changes of upstream areas in the Green-Duwamish watershed may affect the relative and total sediment contributions to the Duwamish Waterway. Past modeling addressed uncertainty in upstream sediment loads by using bounding assumptions 50% greater or 50% less than the estimated average upstream sediment load. These results will be considered in RD. No further modeling of these effects on sediment loads is planned due to the infeasibility of predicting changes to sediment load that have many contributory factors (e.g., upland development, agricultural practices, erosion, dam operations, stormwater discharges).

3.9.5 *Design Approach*

The RD will be developed using existing model results and design parameters based on existing environmental conditions and analyses (e.g., using the existing results from previous hydrologic and STM model runs, existing tidal ranges, etc.). The Intermediate (60%) and Pre-Final (90%) RD will evaluate potential impacts on the design from climate change and include revised design and long-term monitoring elements as appropriate to improve the resiliency of the remedy. The LTMMMP outline will identify any expected measures for climate change adaptation, such as defining events that may trigger additional monitoring elements (e.g., 100-year high-flow events could trigger surveys or inspections in some locations).

3.9.6 *Green Remediation*

The RD will assess and specify greener construction activities to the extent practicable (e.g., during dredging, sediment handling, transportation, and disposal) consistent with EPA Region 10's *Clean and Green Policy* (EPA 2009a), the *Superfund Green Remediation Strategy* (EPA 2010), and *Green Remediation Best Management Practices: Integrating Renewable Energy* (EPA 2022). The BODR will identify guidance documents that will be reviewed to inform the RD

(e.g., ASTM E2876-13, *Standard Guide for Integrating Sustainable Objectives*, ASTM E2893, *Standard Guide for Greener Cleanups*). Additional guidance documents (if used) will be identified in the BODR. The core elements identified in these EPA documents include the following:

- Use energy conservation/efficiency approaches (including Energy Star equipment) and electric construction equipment where applicable.
- Use cleaner fuels (e.g., low-sulfur fuel or biodiesel), diesel emission controls and retrofits, and emission reduction strategies.
- Use water conservation/efficiency approaches (including Water Sense products).
- Use reused/recycled materials within regulatory requirements.
- Minimize transportation of materials and use rail rather than truck transport to the extent practicable.
- Protect land and ecosystems near the site.

Anticipated remedial construction activities will be evaluated to identify potential opportunities to implement the remedy consistent with the goals of the Green Remediation Strategy. Construction approaches that can be specified to address multiple goals will be highlighted.

3.9.7 Waterfront Facility Operational Considerations and Construction Sequencing

The middle reach is an active reach of the LDW. Construction sequencing will need to consider marine activities within the middle reach, with the objective of reducing interruptions to waterway use to a practical extent. The specifications included with the RD plans will establish contractor requirements for coordination and outreach activities to waterfront facilities. The 60%, 90%, and 100% design packages will identify and refine known constraints based on ongoing coordination with waterway users, and develop preliminary construction sequencing that considers waterfront facility operation. The specifications will also require the contractor to develop a detailed work plan (RAWP) and a schedule in their RAWP that presents the sequencing and duration of each project element. Throughout construction, the detailed schedule will be regularly updated in consideration of actual construction progress and ongoing coordination with waterway users. During 30% RD, LDWG will perform outreach to waterway users and owners to gather recommendations on how to improve the coordination process. Lessons learned during implementation of the PDI will be provided to the contractor for use in development of these plans. The implementing entity will work closely with the contractor to obtain access agreements and information necessary to develop and adapt the construction schedule throughout the project.

3.10 Pre-Construction and Construction Submittals

Final (100%) RD will identify pre-construction and construction submittals that the selected construction contractor will be required to prepare. These pre-construction and construction submittals are delivered by the contractor.

The primary pre-construction submittal will be the construction contractor's RAWP. The RAWP will describe construction details. For example, the construction contractor will be responsible for identifying and securing specific transload facility locations and staging areas, listing equipment types and numbers to be used during construction, identifying haul routes, and listing import material sources. The contractor will also be responsible for developing and implementing the Vessel Management Plan, coordinating with Tribal fishing activities, and developing detailed construction schedules.

The contractor's RAWP is anticipated to address the following minimum construction elements:

- Contractor's Organization and Communication Plan
- Contractor's Health and Safety Plan (including community health and safety)
- Contractor's Construction Quality Control Plan
- Construction schedule and work hours
- Construction sequencing
- Location of transload and disposal facilities
- Staging areas and site preparation
- Engineering controls for all active remedial actions (e.g., dredging, capping, ENR, treatment)
- Environmental controls and BMPs
- Dredging and material placement operations (i.e., capping, ENR, *in situ* treatment, RMC)
- Dredge materials handling, potential dewatering, potential water treatment, and discharge operations
- Material transload, transportation, and disposal operations
- Vessel Management Plan

Additional anticipated pre-construction submittals often include the following:

- Insurance and bonding
- Disposal facility certifications
- Contractor's surveyor licensing/certifications
- Example contract administration forms (e.g., progress payments, change notifications, value engineering proposal requests, requests for information)

4 Remedial Design Support Activities

This section describes activities that will be conducted throughout the middle reach to support the RD process, as outlined in Section 3. These activities will provide the information needed to complete RD and to comply with ARARs. Results will be incorporated into the design and documented in the BODR. The deliverables associated with the design support activities are included under each effort and are summarized in Section 6.

4.1 Pre-Design Investigation Activities

RD will follow a phased approach that allows sufficient time for data gathering, engineering analyses, and EPA review at key project milestones. Field investigations that are needed to support the middle reach RD are detailed in the PDIWP (Appendix C). PDI will be conducted at the initial stage of the RD to address DQOs outlined in Appendix C and at a minimum will include the following:

- Sediment quality characterization to determine preliminary remedial action areas and technology assignment
- Geotechnical studies to inform dredge and cap design and work around existing infrastructure
- Physical and geophysical surveys, bathymetric/topographic surveys, and infrastructure condition surveys to inform remediation technology selection; geometric design of dredging, capping, and ENR; construction offsets and no-work area location; slope stability; and habitat conditions and considerations

The PDIWP (Appendix C) describes in detail the conceptual sampling plan (i.e., general principles applied for the sampling decision) and proposed data collection efforts for the two PDI phases to support RD. If any data gaps remain following the Phase II PDI, the Preliminary (30%) RD documents, or in EPA's review of those documents, a Phase III PDI sampling event will be conducted. A summary of the phased PDI studies, results, and preliminary remedial action areas and technology assignments will be presented in PDI Data Evaluation Reports (see Section 6.1.4).

An updated bathymetric survey was performed in October 2021 in accordance with the EPA-approved *Quality Assurance Project Plan: Pre-Design Surveys of the Lower Duwamish Waterway Middle Reach* (Anchor QEA 2021), in advance of the Phase I PDI. Additional bathymetric surveying is anticipated to be conducted during or prior to the Phase I PDI field sampling to supplement the initial bathymetric survey to fill data gaps in the survey coverage. The updated bathymetry will inform potential refinements to Recovery Category assignments.

4.2 Base Mapping

A base map of the middle reach is necessary to support RD because it is the basis for developing plans, identifying property lines, establishing potential access points (e.g., public roadways, haul routes), determining constraints due to structure presence (e.g., bridges, underwater clearance), and identifying utility locations. Detailed maps of the site are available and will be supplemented as needed during RD. Base mapping activities that will supplement existing mapping will be obtained from the following additional field surveys:

- Bathymetric and topographic surveys
- Structure and debris surveys (as-builts where available; structure dimensions from surveying; and condition assessments from visual inspection)
- Utilities (private locate, utility owner, National Oceanic and Atmospheric Administration maps as sources)
- Habitat delineation

In addition to field surveys, mapping conducted by others may be acquired and used to aid in the RD, such as aerial photography, adjacent infrastructure, property boundary maps, and historical landmarks.

All supporting mapping information obtained will be merged into the base map using the tidal reference datum of MLLW (the average of the lower low-water height of each daily epoch), for the Final (100%) RD process. The compiled base map of the entire middle reach will be prepared during Preliminary (30%) RD.

4.3 Hydrodynamic Information

Existing hydrodynamic modeling information will inform cap design stability criteria and cap material specifications to protect the cap against both predicted velocities up to the 100-year discharge event and vessel-induced scour forces (e.g., propeller scour, vessel wakes). The hydrodynamic model's predicted velocities and flow directions will also be used to assess sediment resuspension impacts during dredging and select appropriate types of sediment resuspension BMPs if needed.

The anticipated range of climate change effects on hydrology, peak river flow velocities, sea level, and bathymetry will be incorporated into the RD analyses as discussed in Section 3.9.1.

4.4 Zero-Rise Evaluation

A zero-rise evaluation may need to be conducted to ensure that the RD complies with federal and state floodplain management ARARs, depending on the specifics of the RD.

Section 60.3(d)(3) of the National Flood Insurance Program and King County Code

Section 21A.24.240 (zero-rise flood fringe) stipulate that any development or alterations to the floodplain shall not increase the base flood elevation or energy grade line elevation during the occurrence of the 100-year flood discharge. Per the Federal Emergency Management Agency (FEMA) Region 10 guidance document *Procedures for "No-Rise" Certification for Proposed Developments in the Regulatory Floodway* (FEMA 2013), a "no-rise" certification may need to be obtained for the middle reach remedial action based on hydraulic analyses.

If a zero-rise evaluation is required, the USACE's Hydrologic Engineering Center – River Analysis System (HEC-RAS) hydraulic model would be used to evaluate the effect of the remedial action on the 100-year flood elevation. This model would be used to estimate the pre-construction and post-construction flood stage elevations in the middle reach and upstream and downstream of it. HEC-RAS is the FEMA-accepted modeling tool used for determining the base flood elevations reported in FEMA Flood Insurance Studies. The existing HEC-RAS floodplain model developed by FEMA for the Duwamish River would be used directly to represent pre-construction conditions and would be modified at the site location to represent post-construction conditions.

The remedial approach presented in the 30% BODR will include estimates of dredge material removed and fill placed (i.e., backfill, capping, ENR, and RMC) and cross sections illustrating the pre- and post-construction bathymetry. This information will be used to make a preliminary determination regarding whether the constructed remedy may result in a net increase or decrease in flood flow capacity. The zero-rise analysis may need to be conducted to demonstrate that the remedial action does not result in unacceptable flood rise in the Lower Green/Duwamish River during the 100-year return interval flood event. Results from the zero-rise analysis, if required, will be documented in the 60% BODR.

4.5 Transload Facility Requirements

A transload facility is a specified location where dredged material will be offloaded from one mode of transportation (in-water, such as barges) and loaded onto another mode (upland, such as trucks or rail) for upland transport and off-site landfill disposal. The transload facility typically serves the following purposes: dredged material temporary stockpile; rehandling operations; *ex situ* treatment (if applicable); dewatering and water treatment (if applicable); equipment

laydown for temporary storage; water-based equipment mooring and adjacent upland staging; and decontamination area (including wheel wash for haul trucks and related equipment).

Commercial transload facilities have been previously set up at existing facilities to support dredging and capping projects within the LDW and have been used by some of the EAA projects. The current infrastructure, condition, and capacity of these existing commercial facilities will be evaluated during RD.

Existing transload facilities may have production rate limitations, and they can also be used by multiple projects at the same time. LDWG may decide to assess if there is a gap between the need and available space for staging and will provide recommendations on how to overcome any gaps identified as the RD progresses. Results from the assessments will be documented in the BODR.

4.6 Potential Water Quality Impacts

Potential water quality impacts due to sediment resuspension associated with dredging and other remedial actions (in-water work) are expected to be temporary and located at or close to the point of disturbance. Water quality monitoring has been conducted during the construction of the EAAs and many similar regional sediment remediation projects. The most common water quality issue observed has been occasional exceedances of turbidity criteria, either during dredging or placement of clean cap/ENR material. As discussed in Section 3.7, a range of BMPs will be evaluated and summarized in the BODR to minimize and reduce the degree of resuspension.

4.7 Dredged Material Management

Two regional Subtitle D landfills (Waste Management, Inc., located at Columbia Ridge, Oregon, and Allied Waste, Inc., located at Roosevelt, Washington) are permitted to accept “wet” sediment (i.e., containing free liquid) generated from mechanical dredging, thereby avoiding the need to stabilize or dewater mechanically dredged materials prior to transport. Hydraulically dredged sediment would need to be dewatered prior to transport to landfills. However, the overall need for treatment studies will be assessed when preparing the Phase II PDI Data Evaluation Report that will inform dredging, dewatering, water management, transportation, and disposal design. LDWG may decide to assess specific dredged material treatments if PDI data evaluation suggests there may be value in treating the dredged material, but treatment studies are not anticipated at this time.

No dredged material treatment studies are anticipated to be needed to complete RD. If specific dredged material treatment studies are determined to be necessary, a QAPP addendum for treatment studies would be developed for the Phase II PDI. Findings from these potential studies and how they will be incorporated into RD will be described in the 60% RD.

4.8 Waste Characterization

The PDIWP (Appendix C) summarizes the characterization of potential waste material (i.e., dredged material) to provide preliminary data about whether the waste material meets both regulatory requirements and bulk chemistry and leachate concentration requirements for disposal at specific commercial landfill facilities. Waste characterization data are anticipated to be collected as part of Phase II or Phase III PDI and summarized in the Phase II or Phase III PDI Data Evaluation Report.

4.9 Clean Material Source Identification

Locally available sources of aggregate material (e.g., commercial sand and gravel quarries) that can supply materials for capping (e.g., sand, gravel, armor rock) and ENR (e.g., sand) will be identified during RD. The contractor will ultimately select appropriate material suppliers that can meet the design quantities, gradations, and chemical quality criteria established for each material type during RD.

If a cap amendment, such as AC, is included as a component of the design, vendors that can meet the design quantities and other prescriptive criteria established for cap amendment materials will also be identified during RD.

The BODR will present the results from the supplier research and material source identification.

4.10 Archaeological, Cultural, and Historic Surveys

The LDW and vicinity encompasses cultural resources including archaeological sites, districts, historic buildings and structures, objects, traditional fishing locations, and areas of cultural or spiritual significance. Consistent with Section 106 of the National Historic Preservation Act of 1966, and to comply with historical and archaeological preservation requirements, any cultural resources in the vicinity of the middle reach potentially impacted by remedy implementation (e.g., upland areas used for staging) and included or eligible for inclusion in the National Register of Historic Places will be assessed to determine whether remediation plans need to accommodate cultural resources. Confirmation of this assessment will be documented in the BODR.

A cultural resources review for PDI work will be prepared for the middle reach. The purpose of this review is to provide background information and a historic context for the project site, and identify known cultural and historic properties. Similar to the upper reach, a MIDP will be prepared for PDI work and will be submitted as an appendix in the QAPP. A separate MIDP will also be prepared for construction, including specifications to ensure protection of historical Native American artifacts and cultural and archaeological resources. Confirmation of Section 106 compliance will be conducted during the Preliminary (30%) RD. The construction MIDP will be drafted at the Pre-Final (90%) RD phase and finalized during the Final (100%) RD.

4.11 Tracking Changes in the Middle Reach During Design

Bank or in-water construction activities (e.g., permitted maintenance dredging) within the limits of the middle reach may take place during the anticipated RD duration. Middle reach construction activities could modify existing conditions. Therefore, any planned or completed construction activities within the middle reach from 2022 (representing the middle reach RD notice to proceed) through anticipated RD completion in 2026 (see Section 7) will be tracked and summarized in the BODR. Construction activities will be documented by tracking USACE permits and through communications with water-dependent users (see Section 2.5).

In addition, the 2018 waterway user survey (Integral et al. 2018), plus findings from the Phase I PDI (in terms of horizontal delineation of extents of contamination and remedial technologies assignments), should help to identify remaining data gaps needed to support the design (e.g., assessing waterfront infrastructure and banks near remediation areas, identifying potential sources of disruption during construction).

Should non-remediation-related construction take place between RD and remedial construction, the implementing entity will review the changed conditions and revise the Drawings and Specifications as necessary.

4.12 Source Control Integration

Remedial construction of the middle reach will proceed following source control sufficiency evaluations and recommendations by Ecology and concurrence by EPA. Ecology has identified 24 source control areas for the LDW as part of their source control strategy (Ecology 2016) for the LDW sediment remedy. Nine of these source control areas (5 through 9 and 18 through 21) drain to the middle reach. Sufficiency recommendations will be developed by Ecology for areas targeted for active in-waterway sediment remediation (although areas may be bundled in documentation). EPA is expected to complete the sufficiency determinations by Final (100%) RD for the middle reach. Ecology may consult on source control evaluations with the LDW Source

Control Workgroup (currently consisting of representatives from Ecology, King County, the City of Seattle, the Port of Seattle, Puget Sound Clean Air Agency, Washington State Department of Transportation, and EPA; see ROD Section 13.2.7).¹⁴

Ongoing coordination between Ecology, EPA, and LDWG (during RD) and the implementing entity (during contracting and remedial action) will be necessary to ensure that the RD details (e.g., areas targeted for active in-waterway sediment remediation activities) pertaining to source control activities are provided to Ecology in a timely manner, through routine check-ins and at critical RD milestones. The following proposed milestones represent anticipated coordination check-ins during RD, which may be modified at the direction of EPA:

- Following the PDI Phase I data evaluation, when approximate active remedial action areas are delineated based on initial RAL exceedance areas
- Following Preliminary (30%) RD, when remedial action area boundaries, bank remediation footprints, and technology assignments are nearly complete
- Following Pre-Final (90%) RD, when remediation contracting schedules are being planned to accommodate the source control sufficiency determinations that precede remedial construction

4.13 Site Access

Site access must be considered throughout RD (e.g., for PDI field sampling, RD geotechnical work, and in planning for equipment and materials staging, shore access during construction). Depending on the owner and the nature and duration of the access, written agreements or other legal documentation (e.g., leases, easements, deed restrictions) may be required.

Waterway and adjacent property ownership is shown in Map 4-1. The aquatic portion of the middle reach main waterway consists mostly of public-owned aquatic land (e.g., the Port of Seattle), with some submerged portions of adjacent upland parcels. Access agreements are not needed for sampling or transient access to Port- owned portions of the LDW Superfund Site, and it is anticipated that access for RD purposes to waterway and upland properties owned by LDWG parties will be readily approved. Access agreements may be required by private owners of waterway or adjacent property. There are a number of private owners for parts of the aquatic lands (especially within the slips and smaller embayments) who have waterfront facilities with active operations in the middle reach. Properties where access agreements are needed will be identified prior to PDI implementation.

¹⁴ Information on the current status of source control efforts can be found on Ecology's website available at: <https://ecology.wa.gov/Spills-Cleanup/Contamination-cleanup/Cleanup-sites/Toxic-cleanup-sites/Lower-Duwamish-Waterway/Source-control>.

During the PDI, sampling will occur in active berths, under structures, and in the vicinity of dolphins/pilings, bulkheads, and riprapped or engineered banks. LDWG will proactively coordinate with property owners to provide notification, obtain access agreements, or obtain temporary vessel relocation agreements, as necessary, based on specific access needs.

Property acquisition, leases, or easements may be needed for remedial activities during construction that disrupt businesses or for off-site staging areas that may be required for the contractor's material and equipment staging. Coordination with property owners or lessees will be needed during RD to accommodate construction near infrastructure and under structures. Construction equipment selection will account for access constraints for vessels transiting the LDW.

As stated in Section 6, site access will be discussed in the BODR, construction access and easement requirements will be included in the Preliminary (30%) RD, a Draft Permitting and Site Access Plan will be included in the Pre-Final (90%) RD, and a Final Permitting and Site Access Plan will be included in the Final (100%) RD. Proprietary controls will be evaluated in the ICIAP outline submitted as part of the 90% and 100% RD submittals.

4.14 Documenting Substantive Compliance with Applicable or Relevant and Appropriate Requirements

ARARs are legally applicable or relevant and appropriate substantive standards, requirements, criteria, or limitations under any federal environmental law, or promulgated under any state environmental or facility siting law that is more stringent than under federal law. ARARs for the remedial action are presented in Table 26 of the ROD (included in Appendix A of this report). Sections 3 and 4 describe key design elements that will be used to comply with anticipated ARARs. The RDWP does not list all potential design needs; 30% design must be developed to help identify applicable ARARs and assess whether there are data gaps and additional design elements needed to comply with those ARARs. The BODR will include descriptions of how substantive compliance with ARARs will be achieved and documented.

4.15 Permitting

Federal, state, and local permits are not required for CERCLA response actions that are completely conducted on site. On-site response action must be performed in compliance with the substantive requirements of all ARARs (EPA 1992a), which are identified in Table 26 of the ROD. Permitting for any necessary off-site work (e.g., landfill permits for creating a new project-specific landfill, building permits for transload structures or staging that are considered to be outside the site boundary) will be identified and discussed in the BODR.

If any material is to be removed from the site for transloading, treatment, or disposal at pre-existing facilities, the compliance status of these facilities will be confirmed before beginning the removal action by contacting the appropriate EPA regional Off-Site Rule coordinator.

A Draft Permitting and Site Access Plan will be included in the Pre-Final (90%) RD, and a Final Permitting and Site Access Plan will be included in the Final (100%) RD.


5 Middle Reach Physical Conceptual Site Model and Expected Outcomes from Remedial Action

Section 8 of the ROD establishes the following RAOs for the LDW cleanup:

- **RAO 1:** Reduce risks associated with the consumption of contaminated resident LDW fish and shellfish by adults and children with the highest potential exposure to protect human health.
- **RAO 2:** Reduce risks from direct contact (skin contact and incidental ingestion) to contaminated sediments during net fishing, clamming, and beach play to protect human health.
- **RAO 3:** Reduce to protective levels risks to benthic invertebrates from exposure to contaminated sediments.
- **RAO 4:** Reduce to protective levels risks to crabs, fish, birds, and mammals from exposure to contaminated sediment, surface water, and prey.

To meet these cleanup objectives, EPA selected a remedy that uses a variety of remedial technologies targeted to different areas of the waterway (e.g., dredging, partial dredging and capping, capping, ENR, MNR to benthic SCO, and MNR below benthic SCO). The predicted outcomes of the selected remedy are summarized in ROD Section 13.4. This section describes the physical CSM for the middle reach and includes physical impacts from implementing remedial actions in order to conceptually discuss the expected outcomes from remediation. This physical CSM, as shown in Figures 5-1 and 2-1, was also informed by the lessons learned from the remediation of the EAAs (Section 2.3.3).

The physical CSM is intrinsic to the RI/FS process, the selected remedy, and the approach to RD for the remedial technologies described in Section 3.7. The RD process takes into consideration the physical CSM when conducting engineering evaluations, establishing design criteria, and developing monitoring plans. For example, the physical CSM factors into residuals management design, water quality monitoring planning, source control sufficiency determination, dredging and material placement design, CQAP development of during construction monitoring, and long-term monitoring to assess MNR effectiveness.

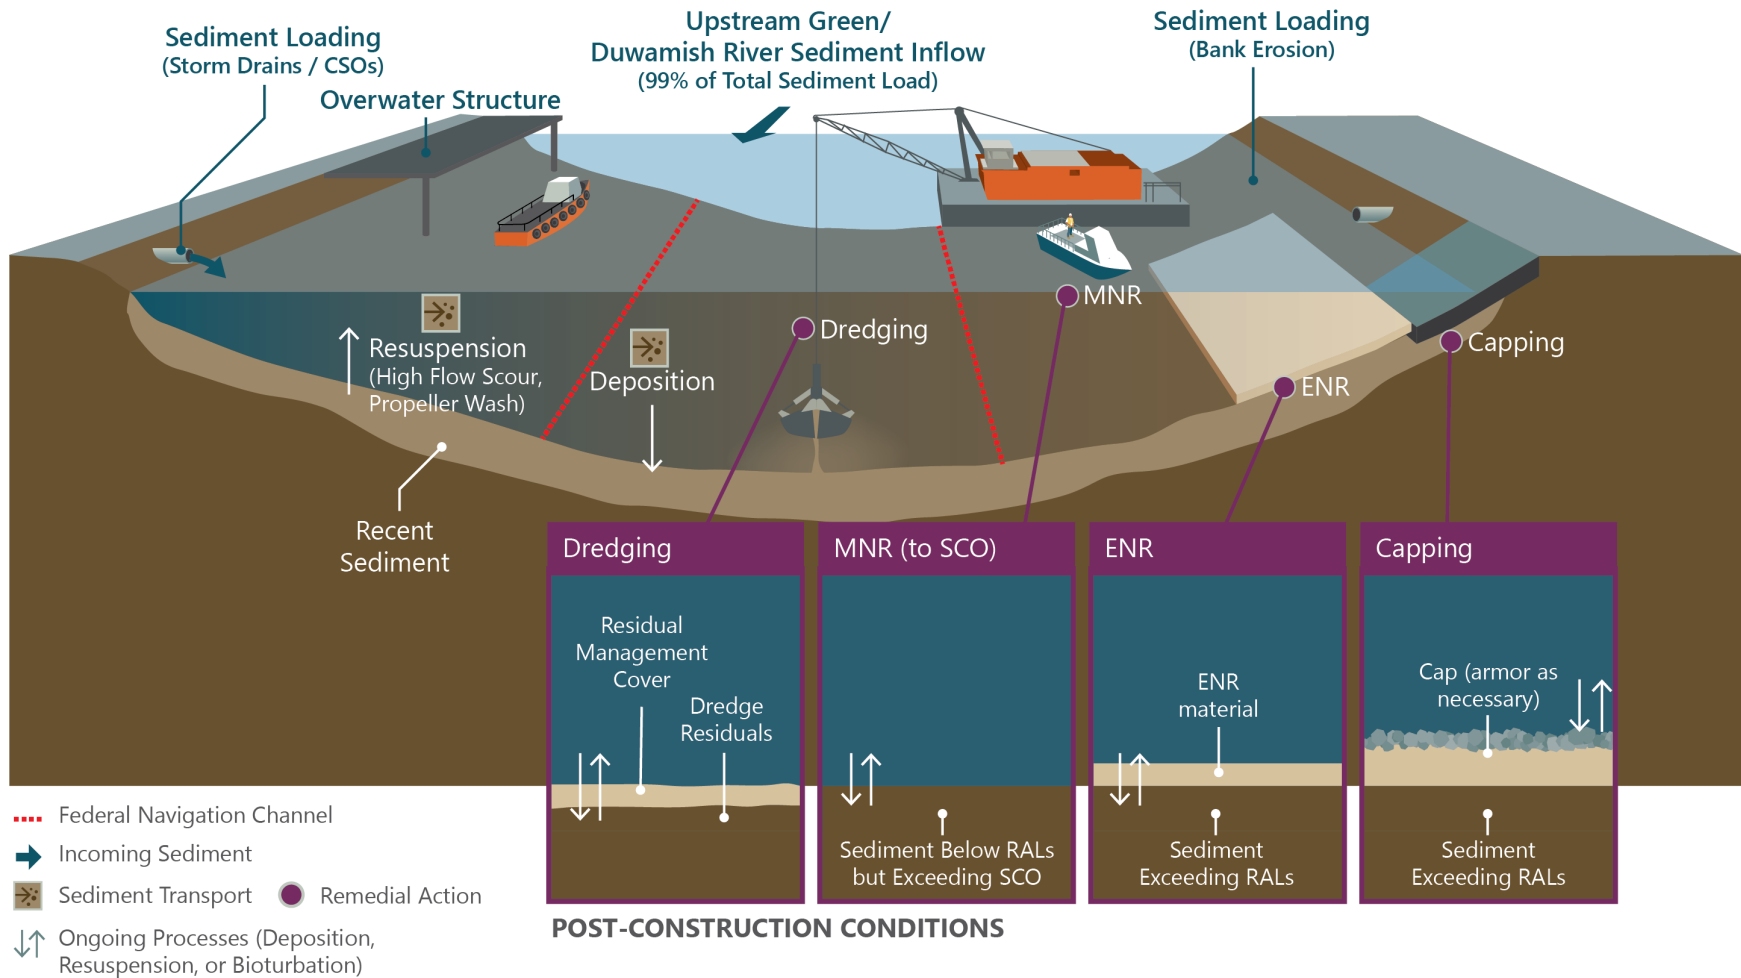

Note: Figure 5-1 does not illustrate other processes relevant to the remedial action, such as groundwater seeps, bioturbation, and contamination mobility.

\\FUJI\Anchor\Projects\City of Seattle\LDW - Middle Reach_Task 300 RDWP\RDWP_Figures\source\Figure 5-1_CSM Schematic.docx
5/2/2022



Lower Duwamish Waterway Group
Port of Seattle / City of Seattle / King County / The Boeing Company

CSO: combined sewer overflow
ENR: enhanced natural recovery
MNR: monitored natural recovery
SCO: Sediment Cleanup Objective
RAL: remedial action level

Figure 5-1. Physical Conceptual Site Model of Middle Reach Remediation
REMEDIAL DESIGN WORK PLAN FOR LDW MIDDLE REACH

5.1 Sediment Sources

As discussed in Section 2.1.4 and illustrated in Figure 5-1, 99% of sediment entering the LDW originates from the upstream Green-Duwamish River system, with more than one-third of it depositing in the upper reach. The middle reach is also net-depositional as shown in Figure 2-1. As a general trend, concentrations in the middle reach will approach upstream sediment concentrations over time following the sediment remediation required by the LDW ROD. Studies by Ecology (data received from Ecology by Windward [Ecology 2009]), the USACE (2009a, 2009b), the U.S. Geological Survey (Conn and Black 2014; Conn et al. 2015; Conn et al. 2018), and King County (data received from King County by Windward [King County 2016a]) have been conducted to characterize upstream suspended solids that enter the LDW. The Pre-Design Studies Data Evaluation Report (Windward 2020) provides a summary of these data including estimates of contaminant concentrations on suspended solids.

CSOs, SDs, and bank erosion are secondary sources of sediment into the middle reach. Source tracing samples by Seattle, King County, and other entities have been conducted to characterize drainage solids that enter the LDW. The Pre-Design Studies Data Evaluation Report (Windward 2020) provides a summary of these data including estimates of SD and CSO contaminant concentrations on solids for the LDW as a whole.

5.2 Sediment Transport

In addition to sediment transported from the Green River into the middle reach, other sediment transport mechanisms include sediment scour and resuspension caused by high-flow events and vessel maneuvering, as discussed in Section 2.1.4 (Figure 5-1).

Episodic high-flow events (e.g., greater than a 2-year event) can result in increased bottom velocities and bed resuspension. The saltwater wedge, where present, tends to reduce flow velocities near the river bottom because the freshwater river flow will flow on top of the saltwater wedge; therefore, river bottom velocities are higher when the saltwater wedge is absent. Potential scour areas in the middle reach from Green River high-flow events were identified based on STM predictions in the southern end of the middle reach. Sediment resuspended during a high-flow event is likely to be carried downstream and redeposited in an area with lower velocities. Most areas in the middle reach that are predicted to scour during a high-flow event are still net depositional on annual time scales.

Propwash from maneuvering vessels is the other primary cause of potential resuspension in the middle reach (Figure 5-1). The FS analysis found evidence for propwash impact from maneuvering vessels near berthing areas, and minor resuspension/mixing from transiting vessels

in the FNC (FS Section 2.3.1.1). The location of propwash scour on the sediment bed depends on the vessel characteristics, bathymetry, sediment characteristics, configuration of the docks, and the docking procedures used during vessel maneuvering. Propwash forces are sensitive to the water depth below the prop, the amount of throttle used during maneuvering, and the duration that the prop is activated in a given location. Compared to high-flow scour, most material that has been resuspended by propwash is likely to redeposit in a nearby location due to the much smaller footprint that can be impacted by propwash and the rapid drop-off of propwash velocities at increasing distances from the vessel's propeller.

5.3 Remedial Action Effects on the Physical Conceptual Site Model

Project experience in the EAAs (Section 2.3.1) and in other cleanup sites similar to the LDW can provide insight into the expected outcomes from remedial actions. This section and Figure 5-1 briefly describe and depict the effect a remedial action has on the physical CSM and the conceptual expected outcome from using different remedial technologies during and following construction.

5.3.1 Dredging

Dredging removes sediment contaminated above applicable RALs from the waterway to the maximum extent practicable. Furthermore, the process of dredging generates resuspended sediments (i.e., dredge residuals) that are intrinsic to environmental dredging projects (USACE 2008a).

Most resuspended sediment from dredging is expected to settle near the dredging area and have approximately the average concentration of the dredged material. Dredge residual deposits tend to be thin (e.g., less than a couple of inches thick [5 cm]) with low density, high water content, and very low strength, and are therefore difficult to re-dredge.

In the short term, dredging impacts the physical CSM because it results in additional resuspension of contaminated sediments, which can cause a short-term increase in observed surface sediment concentrations within and adjacent to the dredging area. An RMC layer may be placed on recently dredged areas or other areas affected by residuals as an engineering control to stabilize and reduce concentrations in the biologically active zone (Figure 5-1).

The potential impact from dredging is considered a short-term effect and, provided residuals are minimized and managed, negligible with respect to long-term expected outcomes.

5.3.2 *Capping*

Capping isolates contaminated sediment from surface exposure. Cap placement is expected to create turbidity in the water column during placement activities. However, this turbidity will be transient and associated with the clean cap material, so these impacts do not impact the physical CSM for contaminated sediment movement. Cap materials will have lower concentrations than the incoming upstream sediment. Therefore, following construction, surface sediment concentrations in capping areas are expected to increase toward surrounding surface concentrations over time.

5.3.3 *Enhanced Natural Recovery*

ENR consists of a thin layer of material placement, which may mix with underlying sediment and/or newly deposited sediment over time. ENR placement is expected to create turbidity in the water column during placement activities. However, this turbidity will be transient and associated with the clean ENR material, so it does not impact the physical CSM for contaminated sediment movement. ENR materials will have lower concentrations than the incoming upstream sediment. Therefore, following construction, sediment concentrations in ENR areas are expected to increase toward surrounding surface concentrations over time.

5.3.4 *Monitored Natural Recovery*

MNR is applied to areas with relatively low initial surface sediment concentrations and/or low scour potential. MNR areas may be impacted in the short term by releases from adjacent areas, either during dredging or placing clean material. Over the long term, MNR is driven by sediment deposition and transport processes described in Section 5.2.

5.4 **Anticipated Short-Term and Long-Term Post-Remediation Outcomes**

The expected conceptual outcomes to the middle reach of the remedial technologies described in Section 5.3 are described in this section. There is uncertainty associated with accurately predicting immediate post-remediation surface concentrations for the overall middle reach due to numerous variables (e.g., sequencing of work, contractor's equipment selection and construction means and methods, natural events such as high flows, and anthropogenic influences such as vessel propwash that occur during construction).

As previously observed on the LDW EAAs,¹⁵ and assuming middle reach sources are sufficiently controlled, the expected outcome of remediation in the overall middle reach is that surface sediment concentrations will equilibrate toward the surrounding sediment concentrations. In the long term, as more remediation and source control occur, the sediment concentrations will continue to decrease toward the incoming upstream sediment concentration. However, specific areas within the middle reach are anticipated to behave differently in the short term immediately following construction, depending upon the remedial technology implemented, as described in the following sections.

5.4.1 Enhanced Natural Recovery, Capping, and Backfill Placement Areas

Surface sediments are expected to be at or below cleanup levels immediately post-placement in ENR, capping, and backfill areas because the material used for those remedial technologies will be tested to verify it meets specified chemical concentration criteria prior to placement. For a short time after placement, the surface sediments in these areas will equilibrate to reflect a combination of placed material and depositional sediments composed of surrounding sediments and upstream and localized lateral inputs. In the long term, the surface sediment concentrations are anticipated to equilibrate to upstream sediment concentrations as incoming upstream sediment is deposited in the area through natural sedimentation processes.

5.4.2 Dredged Areas

After required dredging has been completed to design depths that account for ROD requirements, confirmation samples will be collected in dredge areas to assess whether remaining sediments exceed surface RALs. Results from the confirmatory sampling program, which will be developed as part of the CQAP, will be used to determine whether required backfilling or capping, additional dredging (“re-dredging”), or other contingency action (e.g., placing RMC) is needed, as described in the next sections. Contingency actions and a decision process will be developed in the CQAP.

5.4.2.1 Dredged Areas with Surface Concentrations Below Remedial Action Levels

If the post-dredging confirmation samples indicate surface (0- to 10-cm [i.e., the compliance depth]) sediment concentrations are below the RALs and the benthic cleanup levels (benthic SCO), no further dredging is required by the ROD, and backfill material, if required for elevation

¹⁵ For example, *Duwamish Diagonal Sediment Remediation Project: 2011 and 2012 Monitoring Report* (King County 2016b) and *Post-Construction Surface Sediment Monitoring Report—Year 3 Duwamish Sediment Other Area and Southwest Bank Corrective Measure and Habitat Project Boeing Plant 2, Seattle/Tukwila, Washington* (Wood 2018).

reasons (e.g., habitat areas), can then be placed. These areas will be incorporated into long-term monitoring plans to assess progress toward compliance with cleanup levels.

5.4.2.2 Dredged Areas with Surface Concentrations Above Remedial Action Levels

If the post-dredging confirmation samples indicate surface sediment concentrations above RALs, benthic cleanup levels, or both, contingency action will be required. For dredging areas requiring a cap or backfill, Section 5.4.1 describes the anticipated short-term and long-term post-remediation outcomes.

5.4.3 Areas Adjacent to Dredging

Dredge-generated residuals from nearby dredging activities may be transported outside of the dredging area and then settle on the adjacent surface, causing the surface sediment concentrations in these areas to be higher than pre-dredge conditions. Surface confirmation samples will be collected in adjacent areas to assess the need for contingency actions for generated residuals management.

6 Remedial Design Deliverables

This section describes the deliverables to be prepared for the RD in accordance with the AOC5 SOW (EPA 2021), which are summarized in Table 6-1.

6.1 Pre-Remedial Design Deliverables

6.1.1 *Pre-Design Investigation Quality Assurance Project Plans*

The PDI QAPPs address sample collection, analysis, and data handling. The QAPPs will include a field sampling plan, maps with sampling locations, sampling location placement rationale, and an explanation of DQOs, QA and quality control (QC), and chain-of-custody procedures for any treatment studies, design, compliance, and monitoring samples. The QAPPs will address disposal of Investigation Derived Waste in accordance with *Guide to Management of Investigation-Derived Wastes* (EPA 1992b).

A QAPP or QAPP addenda will be submitted to EPA for each field sampling effort in accordance with *EPA Requirements for Quality Assurance Project Plans* (EPA 2006), *Guidance for Quality Assurance Project Plans* (EPA 2002), and *Uniform Federal Policy for Quality Assurance Project Plans* (EPA 2005). The PDI QAPP addendum for Phase II PDI will be developed and submitted with the draft Phase I Data Evaluation Report per AOC5. If an addendum is needed for Phase III, it will be submitted after comments are received on 30% design.

6.1.2 *Pre-Design Investigation Health and Safety Plan*

The PDI Health and Safety Plan (HASP) will describe all activities to be performed to protect on-site personnel and others transiting the area or living or working nearby from physical, chemical, and all other hazards posed by the work. A Dive HASP will also be prepared to describe diving activities anticipated to be performed and appropriate safety protocols. HASPs will be developed in accordance with EPA's Emergency Responder Health and Safety and Occupational Safety and Health Administration (OSHA) requirements under 29 C.F.R. §§ 1910 and 1926. EPA will not approve the HASP but will review it to ensure that all necessary elements are included and that the plan provides for the protection of human health and the environment.

6.1.3 *Pre-Design Investigation Data*

Data collected during the PDI will be submitted to EPA in accordance with the schedule and requirements outlined in AOC5.

**Table 6-1
Remedial Design Elements**

Document	Element	Description	Preliminary (30%) Remedial Design	Intermediate (60%) Remedial Design	Pre-Final (90%) Remedial Design	Final (100%) Remedial Design
BODR Text and/or Appendices	Basis of Design for Remedial Technologies (dredging, capping, ENR, MNR>SCO)	Development of design criteria for technology areas, including the development dredging prisms, capping thicknesses, material grain sizes, material transport and transload, and other criteria.	Draft	Revised Draft	Draft Final	Final
	Transload Facility Criteria	Identification of candidate transloading location.	Draft	Revised Draft	Draft Final	Final
	Green and Sustainable Remediation Evaluation and Implementation Approach	Green and sustainable remediation calculations and implementation approach.	Draft	Revised Draft	Draft Final	Final
	Engineer's Construction Project Schedule	Engineer's project schedule for remedial action construction.			Draft Schedule	Final Schedule
	Engineer's Capital and Operation and Maintenance Cost Estimate	Cost estimate for post-construction operations, maintenance, and monitoring.			Draft Cost Estimate	Final Cost Estimate
	ARAR Compliance Evaluation	Descriptions of how compliance with ARARs will be achieved and documented.	Draft Evaluation	Final Evaluation		
	Habitat Area Identification	Identification of sensitive species and their habitat areas within the middle reach to facilitate the Biological Assessment and comply with the Endangered Species Act and Section 404 of the Clean Water Act.			Draft Identification	Final Identification
Drawings	Drawings	RD drawing package.	30% Drawings plus a list of all drawings for subsequent submittals	60% Drawings plus a list of all drawings for subsequent submittals	90% Drawings	100% Drawings
Specifications	Specifications	RD specification package.	Outline	Revised Outline	90% Specification Package	100% Specification Package
	Emergency Response Plan Specification	Procedures to be followed in the event of an accident or emergency during remedial construction. Requirements will be defined in the Specifications; the Emergency Response Plan itself will be a component of the contractor's RAWP.	Outline	Revised Outline	90% Specification	100% Specification
	Vessel Management Plan Requirements	Anticipated vessel operations necessary to complete the remedial action such as types of vessels, access points, and vessel frequency. The Vessel Management Plan itself will be an element of the contractor's RAWP.			90% Specification of Required Elements	100% Specification of Required Elements
LTMMMP Outline	LTMMMP Outline	Post-construction long-term operations, maintenance, and monitoring elements, including any expected measures for climate change adaptation.	Draft Outline and Description	Revised Outline and Description	Draft Annotated Outline and Description	Final Annotated Outline and Description
Sediment Remedy ICIAP Outline	Sediment Remedy ICIAP Outline	Evaluation of the most appropriate institutional, proprietary controls and location-specific use restrictions needed to ensure long-term effectiveness of the remedy.	Draft Outline and Description	Revised Outline and Description	Draft Annotated Outline and Description	Final Annotated Outline and Description

Document	Element	Description	Preliminary (30%) Remedial Design	Intermediate (60%) Remedial Design	Pre-Final (90%) Remedial Design	Final (100%) Remedial Design
CQAP	CQAP	Descriptions of activities that will be implemented to ensure the remedial action construction satisfies all plans, specifications, and related requirements, including quality objectives.	Summary Table	Revised Summary Table	Draft Plan	Final Plan
WQMP	WQMP	Plan for collecting and responding to water quality data during construction.			Draft Plan	Final Plan
QAPP and HASP	Addenda to QAPP and HASP. Provided as appendices to CQAP and WQMP.	QAPP and HASP for remedial action construction oversight and monitoring activities. The contractor will prepare a separate RAWP and contractor HASP per specifications.			Draft Plan	Final Plan
Monitoring and Inadvertent Discovery Plan ¹⁶	Monitoring and Inadvertent Discovery Plan	Documentation of districts, sites, buildings, structures, or objects included or eligible for inclusion in the National Register of Historic Places that are potentially impacted by remedy implementation. Specifications for an archaeological discovery plan to ensure protection of Native American artifacts and cultural or archaeological resources.			Draft Plan	Final Plan
Biological Assessment	Biological Assessment	Reasonable and prudent measures that will be taken to guide implementation of the selected remedy with respect to the protection of listed species.			Draft BA	Final BA
Clean Water Act Section 404 and Section 10 Rivers and Harbors Act of 1899 Memorandum	Clean Water Act Section 404 and Section 10 Rivers and Harbors Act of 1899 Memorandum	Documentation to evaluate compliance with Clean Water Act Section 404 requirements.			Draft Memo	Final Memo
Community Outreach and Communications Plan	Community Outreach and Communications Plan	Description of actions that will minimize the potential impacts, including safety issues, of remedy implementation on the community and a plan for communicating with and responding to the community.			Draft Plan	Final Plan
Compensatory Mitigation Plan	Compensatory Mitigation Plan	Plan for compensatory mitigation if necessary to comply with Clean Water Act Section 404 requirements.			Draft Plan	Final Plan
Permitting and Site Access Plan	Permitting and Site Access Plan	Plan for obtaining and complying with permits and obtaining site access needed for remedial action construction.			Draft Plan	Final Plan
Section 408 Compliance Documentation	Section 408 Compliance Documentation	Documentation to evaluate compliance with 33 U.S.C. Section 403 and Section 408.			Draft Memo	Final Memo

¹⁶ Referred to as Archeological Discovery Plan in AOC5. A Monitoring and Inadvertent Discovery Plan is also required for Pre-Design field investigations.

6.1.4 *Pre-Design Investigation Data Evaluation Report*

The PDI Data Evaluation Reports will include the following:

- Summary of the investigations performed
- Summary of investigation results
- Narrative interpretation of data and results, with supporting figures and tables, including updated graphics (similar to ROD Figure 18 [included in Appendix A of this report] or more detailed) of specific remedial technologies and details of how the decision trees in the ROD were applied (Figure 19 and corrected Figure 20 [included in Appendix A of this report])
- Results of statistical and modeling analyses, as needed
- Photographs documenting the work conducted¹⁷
- Conclusions and recommendations for RD, including design parameters and criteria, and identification of any remaining data gaps needed to support the design
- Summary information as required by the MIDP

6.2 Remedial Design Deliverables

Design deliverables will be prepared and submitted to EPA at the Preliminary (30%), Intermediate (60%), Pre-Final (90%), and Final (100%) RD stages. Table 6-1 illustrates the timing of the development of various design deliverables in relation to the overall design process. The following subsections present the information and documents that will be submitted as part of the design deliverables in accordance with the AOC5 SOW (EPA 2021).

6.2.1 *Preliminary (30%) Remedial Design*

The key deliverable of the Preliminary (30%) RD is the BODR. The draft BODR will document the design process outlined in Sections 3 and 4 of this document. The primary purpose of the BODR is to identify and establish design criteria for major elements of construction, present the technical requirements of the design elements, and document how they apply to the overall remedial action. The BODR will describe the analyses conducted to select the design approach, including a summary and detailed justification of design assumptions, restrictions, and objectives to be used in the design of the selected remedy, and supporting calculations.

¹⁷ Photographs are submitted as part of PDI data submittals.

The draft BODR will be submitted as part of the Preliminary (30%) RD and updated in subsequent RD submittals. The BODR will include the following elements. Table 6-1 notes which elements may occur at later stages of the BODR.

- Designation of remedial action areas based on interpolation of RAL exceedance area boundaries
- Designation of remedial action areas where location-specific conditions should be considered (e.g., structural considerations, geotechnical considerations, site use, habitat, etc.)
- Narrative basis of design for selection of remedial technologies (e.g., dredge, cap, ENR, and MNR), including supporting technical evaluations
- Permitting, site access, and easement requirements
- Preliminary construction sequence, scheduling, and cost estimate
- Anticipated long-term maintenance and monitoring approaches, including any expected measures for climate change adaptation
- Evaluation of institutional control requirements for caps
- Transportation and disposal approaches
- Scheduling and coordination of work under the AOC5 SOW with other in-water work or navigation or development projects on the bank and intertidal or subtidal areas, if they may substantively affect RD or construction in the middle reach
- Green and sustainable remediation evaluation and implementation approach, in accordance with *Principles for Greener Cleanups* (EPA 2009b)
- Approach to implementation and assurance of institutional controls,¹⁸ in accordance with *Recommended Evaluation of Institutional Controls: Supplement to the "Comprehensive Five-Year Review Guidance"* (EPA 2011); *Institutional Controls: A Guide to Planning, Implementing, Maintaining, and Enforcing Institutional Controls at Contaminated Sites* (EPA 2012a); and *Institutional Controls: A Guide to Preparing Institutional Controls Implementation and Assurance Plans at Contaminated Sites* (EPA 2012b)
- Geotechnical basis of design (e.g., stable construction slope angles)
- Sediment excavation prism design and verification
- Capping design criteria
- ENR design criteria
- Descriptions of the analyses conducted to select the design approach, including a summary and detailed justification of design assumptions, restrictions, and objectives that will be used in the design of the selected remedy

¹⁸ These do not include fish consumption advisory institutional controls, which are currently being developed under an agreement between EPA and Seattle-King County Public Health.

- Essential supporting calculations (at least one) for each significant or unique design calculation, such as cap thickness or propwash modeling
- General design elements for remedial technologies, such as:
 - Identification of candidate transloading locations, anticipated transport methods, and permitted upland off-site landfill facilities
 - Identification of potential import material sources
- Anticipated dredging and material placement equipment types
- Requirements during construction such as any needed controls and monitoring to comply with ARARs and minimize impacts (in accordance with Section 13.2.5 and Section 13.2.8 of the ROD)
- Contracting strategy to procure the remediation contractor

Other components of the Preliminary (30%) RD will include the following:

- Preliminary plans (i.e., drawings) including a list of all drawings to be included in the Intermediate (60%), Pre-Final (90%), and Final (100%) RD
- An outline of construction specifications prepared in Construction Specification Institute's (CSI) Master Format
- Identification of candidate transloading locations, transport methods, permitted upland off-site landfill facility, and import material sources
- A conceptual construction schedule and sequence, contracting strategy, contractor requirements, any needed controls and monitoring to comply with ARARs and minimize impacts (in accordance with Section 13.2.5 and Section 13.2.8 of the ROD), and plans to manage potential conflicts with other in-water work, treaty-protected uses, navigation, recreation and commerce, and upland developments and land use changes that may affect RD and construction in the middle reach
- Access and easement requirements
- Descriptions of how compliance with ARARs will be achieved and documented, specifying documentation requirements associated with ARARs (such as a Biological Assessment, Compensatory Mitigation Plan if needed, MIDP)
- An outline and description of LTMMP elements for the middle reach including any expected measures for climate change adaptation
- An outline of the Sediment Remedy ICIAP, including an evaluation of the most appropriate institutional, proprietary controls and location-specific use restrictions needed to ensure long-term effectiveness, consistent with ROD Section 13.2.4 (EPA 2014)
- An outline of an Emergency Response Plan

6.2.2 Intermediate (60%) Remedial Design

The Intermediate (60%) RD will be a continuation and expansion of the Preliminary (30%) RD. The Intermediate (60%) RD will address EPA's comments on the Preliminary (30%) RD and include the elements and deliverables required for the Preliminary (30%) RD at a 60% level of completion.

6.2.3 Pre-Final (90%) Remedial Design

The Pre-Final (90%) RD will be a continuation of the Intermediate (60%) RD. The Pre-Final (90%) RD will address EPA's comments on the Intermediate (60%) RD and include the elements and deliverables required for the Pre-Final (90%) RD at a 90% level of completion. The Pre-Final (90%) RD will also incorporate data collected during PDI Phase III (if data gaps following PDI Phase II are identified). In addition to the documents prepared as part of the Preliminary (30%) RD, the following will be included with the Pre-Final (90%) RD:

- A complete set of construction plans and technical specifications, following the CSI Master Format (or equivalent), and meeting other relevant standards for design of sediment cleanup
- Survey and engineering drawings showing existing features in the middle reach, such as property boundaries, easements, bathymetry, structures to be protected or removed, and other relevant conditions
- A specification for all necessary construction documentation, including but not limited to photographs and videos, bathymetric surveys, and GPS coordinates
- Draft CQAP
- Draft WQMP
- Draft QAPP/HASP for remedial action construction and monitoring activities
- Draft Permitting and Site Access Plan
- Outline of the Sediment Remedy ICIAP, including specific institutional control elements for each affected area, in accordance with *Recommended Evaluation of Institutional Controls: Supplement to the "Comprehensive Five-Year Review Guidance"* (EPA 2011); *Institutional Controls: A Guide to Planning, Implementing, Maintaining, and Enforcing Institutional Controls at Contaminated Sites* (EPA 2012a); and *Institutional Controls: A Guide to Preparing Institutional Controls Implementation and Assurance Plans at Contaminated Sites* (EPA 2012b)
- Required elements of a Vessel Management Plan (to be finalized by contractor)
- Annotated outline and conceptual description of LTMMP elements specific to the middle reach, discussing how the elements and schedule fit into a likely LTMMP approach for the LDW site as a whole

- Habitat Area Identification Memorandum, which will comply with the Endangered Species Act and Section 404 of the Clean Water Act; identify habitat areas and proposed elevations and substrate materials for caps, ENR, or placement of backfill materials in any identified habitat areas; and identify any areas where loss of aquatic habitat is unavoidable
- Draft Biological Assessment for use in consultation related to the Endangered Species Act
- Draft Clean Water Act Section 404 and Section 10 Rivers and Harbors Act of 1899 Memorandum
- Engineer's Capital and Operation and Maintenance Cost Estimate
- Engineer's Construction Project Schedule
- Community Outreach and Communications Plan
- Draft MIDP
- Compensatory Mitigation Plan if necessary to comply with Clean Water Act Section 404 requirements
- Section 408 Compliance Documentation to evaluate compliance with 33 U.S.C. Section 403 and Section 408
- Any additional plans identified in the RDWP

The Pre-Final (90%) RD will serve as the approved Final (100%) RD if EPA approves the Pre-Final (90%) RD without comments.

6.2.4 Final (100%) Remedial Design


The Final (100%) RD will address EPA's comments on the Pre-Final (90%) RD and include final versions of all pre-final RD elements and deliverables. The Sediment Remedy ICIAP and LTMMP will remain as annotated outlines in the Final (100%) RD. The Final (100%) RD will finalize the complete set of construction plans and technical specifications that will be stamped by a registered Professional Engineer, suitable for procurement.

7 Remedial Design Project Schedule

The middle reach RD project schedule is presented in the AOC5 SOW and in Table 7-1 and Figure 7-1. If schedule modifications are determined to be necessary, LDWG will submit a proposed revised project schedule to EPA for approval in accordance with the provisions of Paragraph 7.1 of the AOC5 SOW. The schedule presented in Figure 7-1 was developed based on assumed EPA review times and will be managed throughout the project. Any changes to this schedule are subject to EPA approval.

Table 7-1
LDW Middle Reach Remedial Design Project Schedule

Deliverable, Task	SOW or AOC Reference	Deadline
PDIWP PDI QAPP/HASP	6.4a 6.4b/c	135 days from issuance of Notice to Proceed to Contractor
Completion of PDI field work	6.4a	In accordance with the schedule in the approved PDIWP, unless otherwise approved by EPA
Phase 1 PDI Data Submittal	6.4d	10 days after Respondents' receipt of validated PDI sampling data from Tier 1, or from Tier 2 if there are two or more tiers of analysis
PDI Phase I Data Evaluation Report and Phase II QAPP Addendum	6.4b/e	80 days after Respondents' submittal of the PDI data for Phase I data collection to EPA
Phase II PDI Data Submittal	6.4e	10 days after Respondents' receipt of validated PDI sampling data from Tier 1, or from Tier 2 if there are two or more tiers of analysis
PDI Phase II Data Evaluation Report	6.4e	60 days after Respondents' submittal of PDI Phase II data to EPA
Preliminary (30%) RD Submittal	6.6	45 days from EPA approval of PDI Phase II Data Evaluation Report
Intermediate (60%) RD Submittal	6.7	120 days after EPA comments on Preliminary (30%) RD Submittal
Pre-Final (90%) RD Submittal	6.8	90 days after EPA comments on Intermediate (60%) RD Submittal
Final (100%) RD Submittal	6.9	60 days after EPA comments on Pre-Final (90%) RD Submittal
Periodic Monitoring QAPP Addendum for clam tissue	4	For clams: concurrent with plans for 2023 LDW-wide fish and crab sampling required under AOC4
Periodic Monitoring Data Evaluation Report	4	For clams, included with or concurrent with reporting of LDW-wide fish and crab sampling required under AOC4
Fish and Shellfish Background Compilation Report	5	15 months from AOC5 effective date

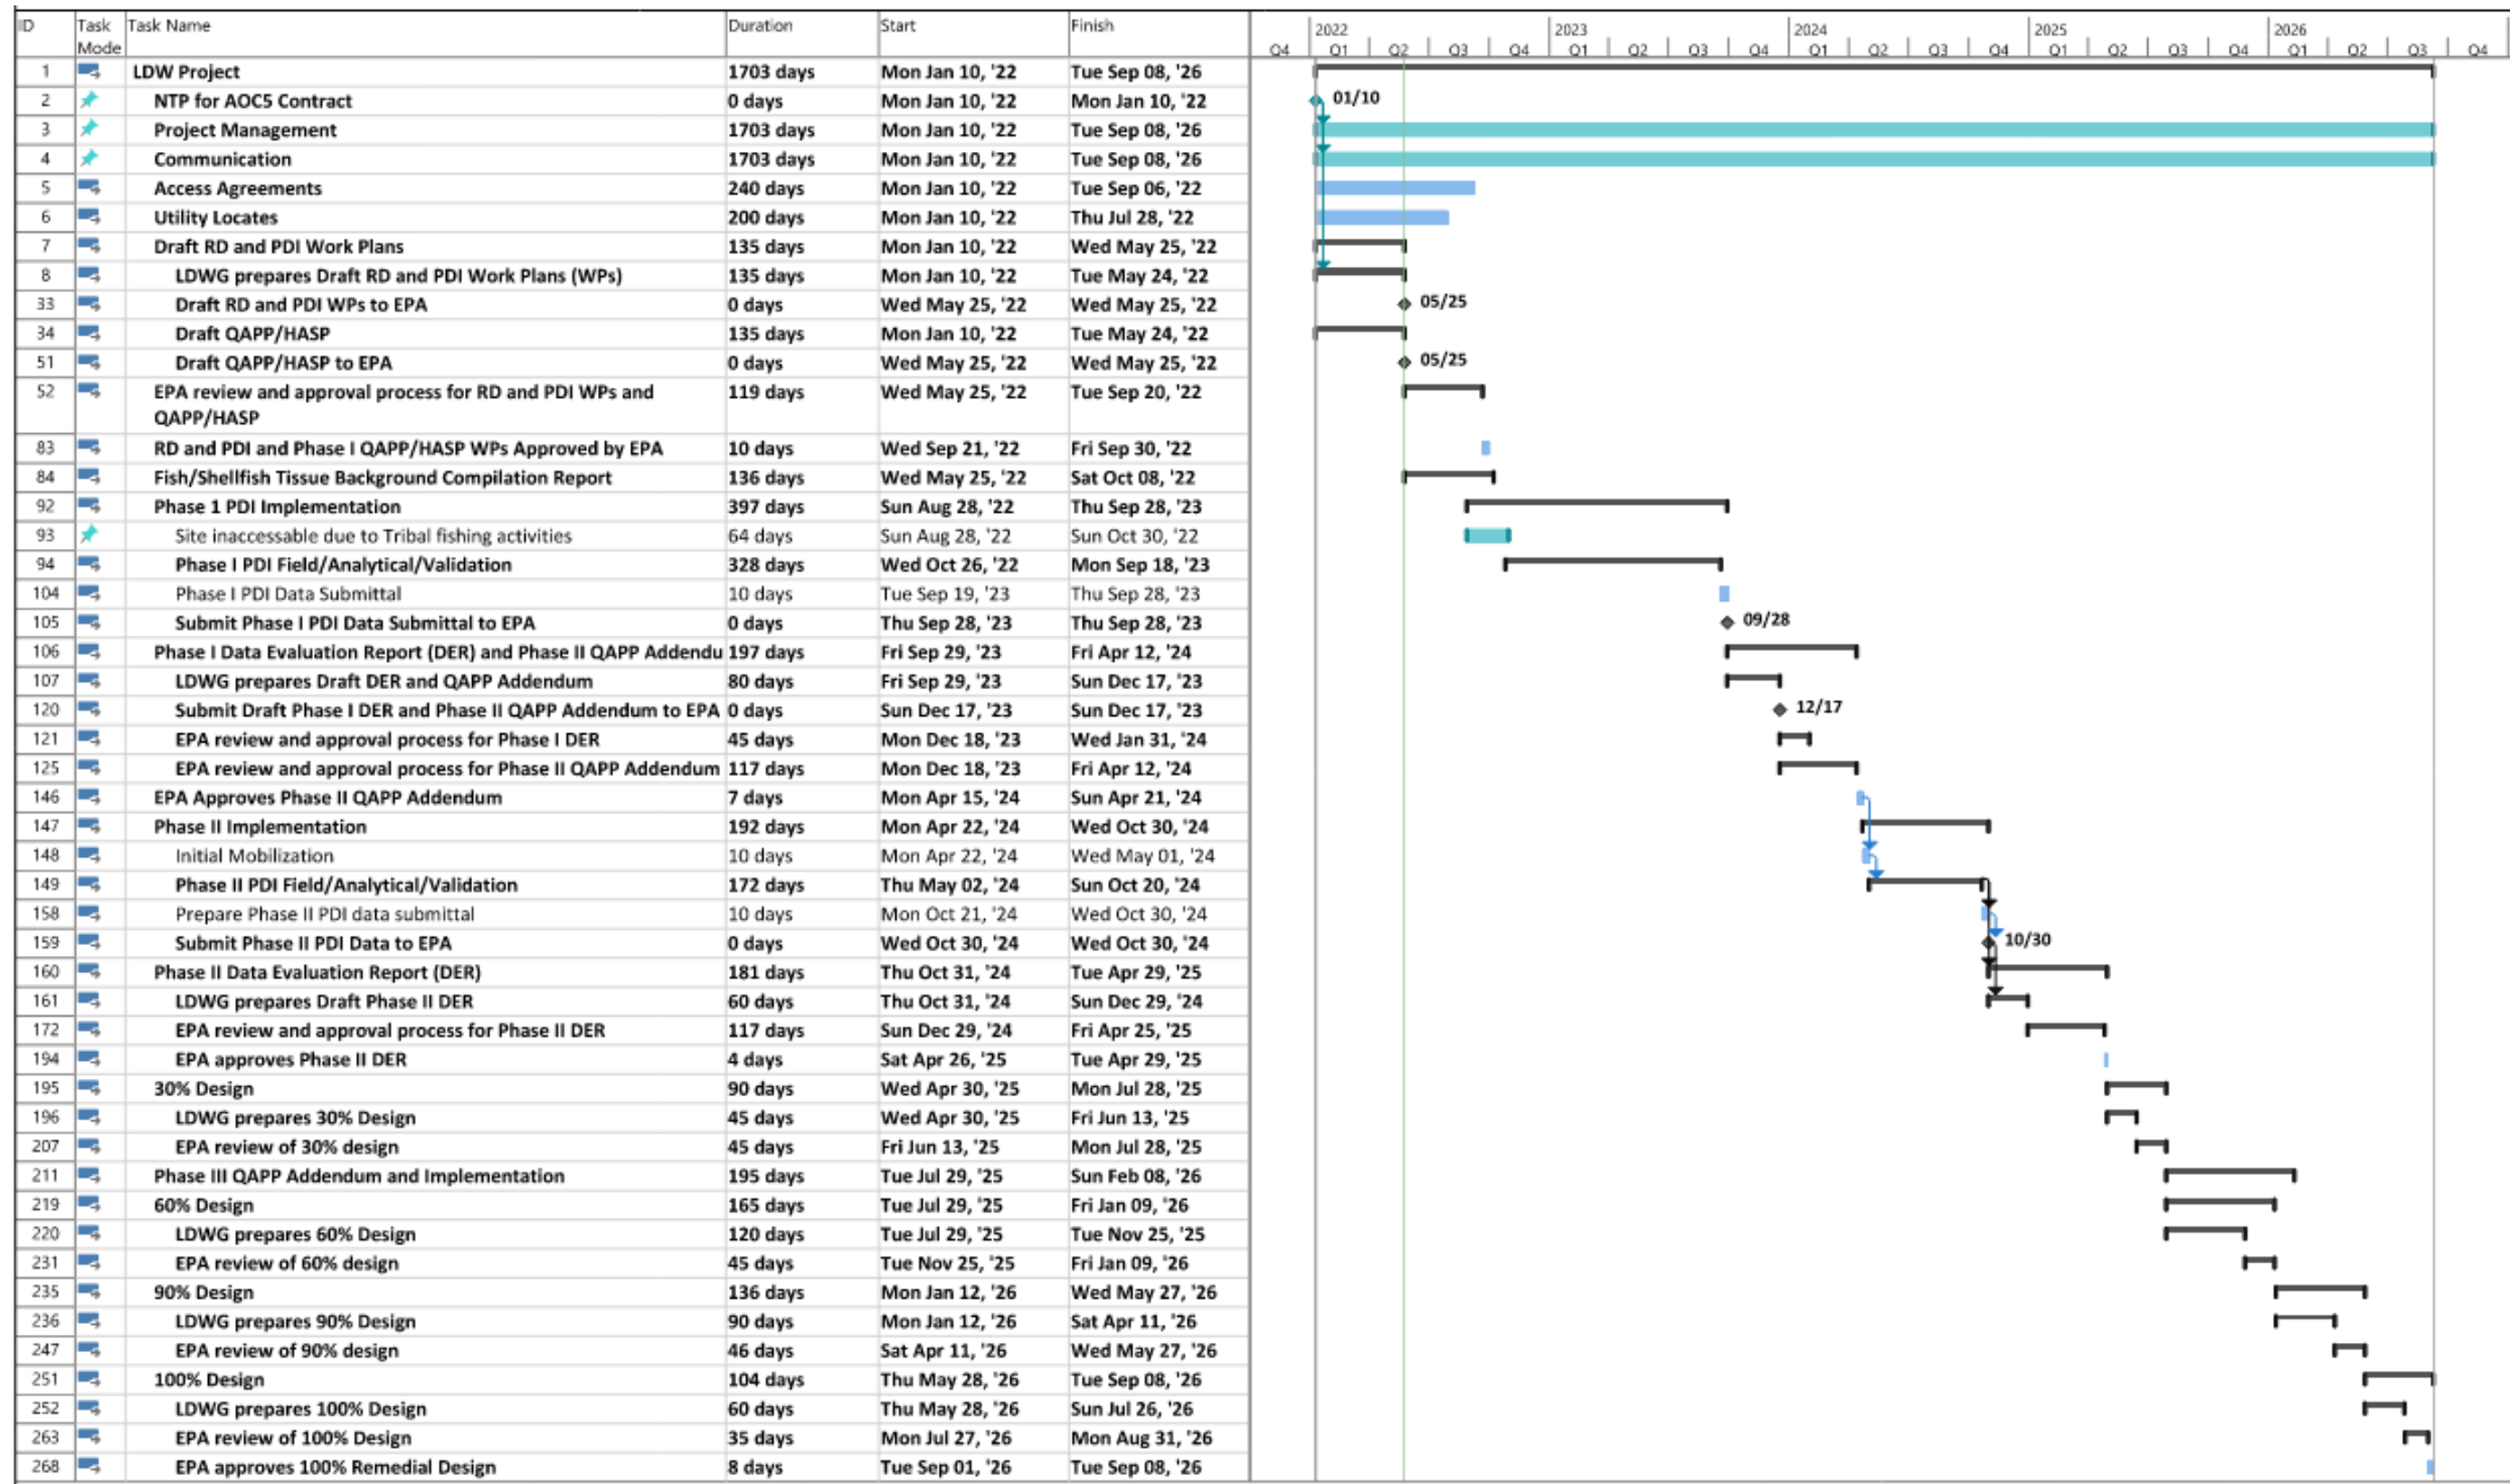

\\FUJI\Anchor\Projects\City of Seattle\LDW - Middle Reach\Deliverables\RDWP\Figures\source\Fig7-1_schedule.docx
5/2/2022

Figure 7-1. Project Schedule
REMEDIAL DESIGN WORK PLAN FOR LDW MIDDLE REACH

8 References

- AECOM, 2012. *Final Feasibility Study, Lower Duwamish Waterway (Seattle, Washington)*. Submitted to U.S. Environmental Protection Agency (Region 10) and Washington State Department of Ecology (Northwest Regional Office). October 31, 2012.
- Amec (Amec Foster Wheeler Environment & Infrastructure, Inc); Dalton, Olmsted & Fuglevand, Inc.; Ramboll; Floyd|Snider; and Geosyntec Consultants, 2018. *Construction Report - Enhanced Natural Recovery/Activated Carbon Pilot Study - Lower Duwamish Waterway - Final*. Prepared for U.S. Environmental Protection Agency (Region 10) and Washington State Department of Ecology (Northwest Regional Office). June 2018.
- Anchor QEA (Anchor QEA, LLC), 2016. *Removal Action Completion Report, Jorgensen Forge Early Action Area*. Prepared for Earle M. Jorgensen Company. May 2016.
- Anchor QEA, 2021. *Quality Assurance Project Plan: Pre-Design Surveys of the Lower Duwamish Waterway Middle Reach*. Prepared for Lower Duwamish Waterway Group.
- Anchor QEA and Windward. 2019. *Remedial design work plan for the Lower Duwamish Waterway upper reach*. Final. Submitted to EPA December 16, 2019. Anchor QEA, Inc. and Windward Environmental LLC, Seattle, WA.
- ASTM, 2016. E2893-16e1: *Standard Guide for Greener Cleanups*.
- Battelle (Battelle Pacific Northwest Laboratory), 2001. *Reconnaissance Assessment of the State of the Nearshore Ecosystem: Eastern Shore of Central Puget Sound, Including Vashon and Maury Islands (WRIAs 8 and 9)*. Prepared for King County Department of Natural Resources, Seattle, Washington. Prepared by Battelle Marine Sciences Laboratory.
- Blomberg, G., C. Simenstad, and P. Hickey, 1988. "Changes in Duwamish River Estuary Habitat over the Past 125 Years." *Proceedings of the First Annual Meeting on Puget Sound Research*. Volume II. Seattle, WA: Puget Sound Water Quality Authority; pp. 437-454.
- Booth D., and L. Herman, 1998. *Duwamish Industrial Area Hydrogeologic Pathways Project: Duwamish Basin Groundwater Pathways Conceptual Model Report*. Prepared for City of Seattle Office of Economic Development and King County Office of Budget and Strategic Planning. Produced by Hart Crowser, Inc., Seattle, WA. April 1998.

- Brettmann, K. 2017. *Green River Climate Change Impacts and Adaptation Pilot Study*. Presentation by USACE at EPA sponsored LDW Superfund Site: Climate Change Adaptation Workshop on March 28, 2017, Seattle, Washington.
- Conn, K.E., and R.W. Black, 2014. *Data Compilation for Assessing Sediment and Toxic Chemical Loads from the Green River to the Lower Duwamish Waterway, Washington*. Data Series 880. U.S. Geological Survey.
- Conn, K.E., R.W. Black, A.M. Vanderpool-Kimura, J.R. Foreman, N.T. Peterson, C.A. Senter, and S.K. Sissel, 2015. *Chemical Concentrations and Instantaneous Loads, Green River to the Lower Duwamish Waterway near Seattle, Washington, 2013-15*. Data Series 973. U.S. Geological Survey.
- Conn, K.E., R.W. Black, N.T. Peterson, C.A. Senter, and E.A. Chapman, 2018. *Chemical Concentrations in Water and Suspended Sediment, Green River to Lower Duwamish Waterway near Seattle, Washington, 2016-2017*. Data Series 1073. U.S. Geological Survey.
- CIG/UW (Climate Impacts Group-University of Washington), 2017. *Projected Changes in Climate and Hydrology for Puget Sound and Adaptation Strategies*. Lower Duwamish Waterway Superfund Site: Climate Change Adaptation Workshop (Seattle, Washington); March 2017.
- Ecology (Washington State Department of Ecology), 2009. *Contaminant Loading to the Lower Duwamish Waterway from Suspended Sediment in the Green River*. Washington State Department of Ecology, Olympia, Washington. November 2009.
- Ecology, 2016. *Lower Duwamish Waterway Source Control Strategy*. Waterbody ID No. 1224819475188. Facility Site # 42927743. Publication No. 16-09-339. Washington State Department of Ecology, Northwest Regional Office, Bellevue, Washington, and Leidos, Bothell, Washington. June 2016.
- Ecology, 2017. *Adaptation Strategies for Resilient Cleanup Remedies: A Guide for Cleanup Project Managers to Increase the Resilience of Toxic Cleanup Sites to the Impacts from Climate Change*. Publication No. 17-09-052. November 2017.
- Ecology and Leidos, 2018. *Lower Duwamish Waterway Source Control Status Report, January 2014 through December 2016*. Bellevue, Washington. June 2018.

- EPA (U.S. Environmental Protection Agency), 1992a. *Permits and Permit "Equivalency" Processes for CERCLA On-Site Response Actions*. Office of Solid Waste and Emergency Response. OSWER Directive 9355.7-03. February 19, 1992.
- EPA, 1992b. *Guide to Management of Investigation-Derived Wastes*. OSWER 9345.3-03FS. January 1992.
- EPA, 2002. *Guidance for Quality Assurance Project Plans*. QA/G-5, EPA/240/R-02/009. December 2002.
- EPA, 2005. *Uniform Federal Policy for Quality Assurance Project Plans*. Parts 1-3, EPA/505/B-04/900A through 900C. March 2005.
- EPA, 2006. *EPA Requirements for Quality Assurance Project Plans*. QA/R-5, EPA/240/B-01/003. March 2001, reissued May 2006.
- EPA, 2009a. *Clean and Green Policy*. Region 10 Superfund, RCRA, LUST, and Brownfields. August 13, 2009.
- EPA, 2009b. *EPA Principles for Greener Cleanups*. Accessed May 6, 2019. Available at: <https://www.epa.gov/greenercleanups/epa-principles-greener-cleanups>.
- EPA, 2010. *Superfund Green Remediation Strategy*. September 2010.
- EPA, 2011. *Recommended Evaluation of Institutional Controls: Supplement to the "Comprehensive Five-Year Review Guidance"*. OSWER 9355.7-18. September 2011.
- EPA, 2012a. *Institutional Controls: A Guide to Planning, Implementing, Maintaining, and Enforcing Institutional Controls at Contaminated Sites*. EPA/540/R-09/001; OSWER 9355.0-89. December 2012.
- EPA, 2012b. *Institutional Controls: A Guide to Preparing Institutional Controls Implementation and Assurance Plans at Contaminated Sites*. EPA/540/R-09/02; OSWER 9200.0-77. December 2012.
- EPA, 2014. *Record of Decision, Lower Duwamish Waterway*. Seattle, Washington. EPA ID: WA00002329803. U.S. Environmental Protection Agency Region 10, Seattle, Washington. November 2014.

- EPA, 2015a. Memorandum to: Lower Duwamish Waterway Site File. Regarding: Lower Duwamish Waterway Record of Decision Table and Figure Revisions. From Alison Hiltner (Office of Environmental Cleanup). August 26, 2015.
- EPA, 2015b. *Climate Change Adaptation Technical Fact Sheet: Contaminated Sediment Remedies*. Available at: https://www.epa.gov/sites/production/files/2018-08/documents/contaminated_sediments.pdf. April 2015.
- EPA, 2016. *Third Amendment of the Administrative Order on Consent for Remedial Investigation/Feasibility Study*. U.S. Environmental Protection Agency, Region 10, CERCLA Docket No. 10-2001-0055 and Ecology Docket No 00TCPNR-1895. Seattle, Washington. March 24, 2016.
- EPA, 2017. *Guidance for Management of Superfund Remedies in Post Construction*. EPA Office of Land and Emergency Management. OLEM 9200.3-105. February 2017.
- EPA, 2018. *Fourth Amendment of the Administrative Order on Consent for Remedial Investigation/Feasibility Study (AOC4)*. U.S. Environmental Protection Agency, Region 10, CERCLA Docket No. 10-2001-0055 and Ecology Docket No 00TCPNR-1895. Seattle, Washington. July 9, 2018.
- EPA, 2021. *Fifth Amendment of the Administrative Order on Consent for Remedial Investigation/Feasibility Study (AOC5)*. U.S. Environmental Protection Agency, Region 10, CERCLA Docket No. 10-2001-0055 and Ecology Docket No 00TCPNR-1895. Seattle, Washington. July 8, 2021.
- EPA. 2022. *Green Remediation Best Management Practices: Integrating Renewable Energy*. EPA Office of Land and Emergency Management. EPA 542-F-22-001. March 2022 Update.
- EPA and Ecology, 2014. Lower Duwamish Waterway Site Memorandum of Agreement between the United States Environmental Protection Agency and the Washington State Department of Ecology. November 2014.
- FEMA (Federal Emergency Management Agency), 2013. *Procedures for "No-Rise" Certification for Proposed Developments in the Regulatory Floodway*.
- Horner-Devine, A., N. Kumar, and M. McKeon, 2017. *Measurements and modeling of hydrodynamics and sediment transport in the Duwamish River estuary*. Environmental Fluid Mechanics, Civil and Environmental Engineering, University of Washington, Seattle.

- Integral (Integral Consulting Inc.), 2012. *Slip 4 Early Action Area Removal Action Completion Report*. July 26, 2012.
- Integral, Anchor QEA, and Windward Environmental LLC, 2019. *Recovery Category Recommendations Report – Final*. Prepared for: U.S. Environmental Protection Agency, Region 10. February 11, 2019.
- Integral, Moffatt & Nichol, and Windward Environmental LLC, 2018. *Waterway User Survey and Assessment of In-Water Structures – Data Report*. Prepared for U.S. Environmental Protection Agency, Region 10. July 2, 2018.
- Integral and Windward (Integral and Windward Environmental LLC), 2019. *Design Strategy Recommendations Report – Final*. Prepared for U.S. Environmental Protection Agency, Region 10. February 11, 2019.
- King County, 2016a. *Lower Duwamish Waterway Source Control: Green River Watershed Suspended Solids Data Report*. King County Department of Natural Resources and Parks, Water and Land Resources Division, Science and Technical Support Section, Seattle, WA. December 2016.
- King County, 2016b. *Duwamish Diagonal Sediment Remediation Project: 2011 and 2012 Monitoring Report*. Prepared by Jenée Colton, Water and Land Resources Division. Seattle, Washington.
- Palermo, M.R., S. Maynard, J. Miller, and D.D. Reible, 1998. *Assessment and Remediation of Contaminated Sediments (ARCS) Program: Guidance for In Situ Subaqueous Capping of Contaminated Sediments*. U.S. Environmental Protection Agency, Chicago, IL. EPA 905-B96-004. September 1998.
- Palermo M., P. Schroeder, T. Estes, and N. Francingues, 2008. *USACE Technical Guidelines for Environmental Dredging of Contaminated Sediments*. U.S. Army Corps of Engineers, Engineer Research and Development Center. ERDC/EL TR-08-29. September 2008.
- Public Health Seattle and King County, 2019. *US EPA’s Institutional Control Implementation and Assurance Plan (ICIAP) for Seafood Consumption at the Lower Duwamish Waterway (LDW) Superfund Site*. Final. August 2019.

QEA (Quantitative Environmental Analysis, LLC), 2008. *Lower Duwamish Waterway Sediment Transport Modeling Report*. Prepared for U.S. Environmental Protection Agency (Region 10) and Washington State Department of Ecology (Northwest Regional Office). October 2008.

Seaport Planning Group, 2009. *Duwamish Lower Duwamish River Habitat Restoration Plan: An Inventory of Port of Seattle Properties*. Adopted Plan July 7, 2009.

Senter, C.A., K.E. Conn, R.W. Black, N. Peterson, A.M. Vanderpool-Kimura, and J.R. Foreman, 2018. *Suspended-Sediment Transport from the Green-Duwamish River to the Lower Duwamish Waterway, Seattle, Washington, 2013–17*. U.S. Geological Survey Open-File Report 2018-1029. Prepared in cooperation with the Washington State Department of Ecology.

USACE (U.S. Army Corps of Engineers), 2008a. *The Four R's of Environmental Dredging: Resuspension, Release, Residual, and Risk*. Technical Report ERDC/EL TR-08-4. Vicksburg, MS: U.S. Army Corps of Engineers Research and Development Center. Prepared by T.S. Bridges, S. Ells, D. Hayes, D. Mount, S. Nadeau, M.R. Palermo, C. Patmont, and P. Schroeder. February 2008.

USACE, 2008b. *Technical Guidelines for Environmental Dredging of Contaminated Sediments*. Technical Report ERDC/EL TR-08-29. Vicksburg, MS: U.S. Army Corps of Engineers Research and Development Center. Prepared by M.R. Palermo, P.R. Schroeder, T.J. Estes, and N.R. Francingues. September 2008.

USACE, 2009a. *Duwamish River Federal Navigation Channel Dredged Material Characterization (Seattle, WA), Data Report Final*. October 7, 2009.

USACE, 2009b. *Duwamish River Federal Navigation Channel Dredged Material Characterization (Seattle, WA), Data Report Addendum Final*. November 20, 2009.

USACE, 2013. Letter to: Allison Hiltner, EPA. Regarding: USACE Comments on Lower Duwamish Waterway Proposed Plan. June 13, 2013.

USACE, 2014. *Howard Hanson Dam, Green River, Washington, Climate Change Impacts and Adaptation Study*. U.S. Army Corps of Engineers, Seattle District, April 2014.

Webb, R., and D. Schuchardt, 2017. *Cleanup and Climate Change*. Lower Duwamish Waterway Superfund Site: Climate Change Adaptation Workshop (Seattle, Washington); March 2017.

Windward (Windward Environmental, LLC), 2005. *Quality Assurance Project Plan: Porewater Sampling of Lower Duwamish Waterway*. Final. Prepared for Lower Duwamish Waterway Group for submittal to U.S. Environmental Protection Agency, Seattle, Washington, and Washington State Department of Ecology, Bellevue, Washington. May 2005.

Windward, 2010. *Lower Duwamish Waterway Remedial Investigation Report – Final*. Prepared for Lower Duwamish Waterway Group for submittal to U.S. Environmental Protection Agency, Seattle, Washington, and Washington State Department of Ecology, Bellevue, Washington. July 2010.

Windward, 2018a. *Lower Duwamish Waterway Baseline Seep Data Report*. Prepared for Lower Duwamish Waterway Group. For submittal to U.S. Environmental Protection Agency. December 7, 2018.

Windward, 2018b. *Lower Duwamish Waterway Fish and Crab Data Report*. Prepared for Lower Duwamish Waterway Group. For submittal to U.S. Environmental Protection Agency. May 22, 2018.

Windward, 2018c. *Lower Duwamish Waterway Data Evaluation Report (Task 6)*. Draft. Prepared for Lower Duwamish Waterway Group. For submittal to U.S. Environmental Protection Agency. December 17, 2018.

Windward, 2019a. *Lower Duwamish Waterway Surface Sediment Data Report*. Prepared for Lower Duwamish Waterway Group. For submittal to U.S. Environmental Protection Agency. February 8, 2019.

Windward, 2019b. *Baseline Surface Water Collection and Chemical Analysis Data Report*. Prepared for Lower Duwamish Waterway Group. For submittal to U.S. Environmental Protection Agency. April 2, 2019.

Windward, 2019c. *Lower Duwamish Waterway Clam Data Report*. Prepared for Lower Duwamish Waterway Group. For submittal to U.S. Environmental Protection Agency. February 28, 2019.

Windward, 2020. *Lower Duwamish Waterway Pre-Design Studies Data Evaluation Report (Task 6)*. Prepared for Lower Duwamish Waterway Group. For submittal to U.S. Environmental Protection Agency. June 26, 2020.

Windward and Anchor QEA, 2019. *Pre-design investigation work plan for the Lower Duwamish Waterway upper reach*. Final. Submitted to EPA December 16, 2019. Windward Environmental LLC and Anchor QEA, Seattle, WA

Windward and Integral, 2018. *Technical Memorandum: Compilation of Existing Data, Final*. Prepared for Lower Duwamish Waterway Group. For submittal to U.S. Environmental Protection Agency. November 19, 2018.


Windward and QEA, 2008. *Lower Duwamish Waterway Sediment Transport Analysis Report – Final*. Submitted to U.S. Environmental Protection Agency (Region 10) and Washington State Department of Ecology (Northwest Regional Office). January 24, 2008.

Wood (Wood Environment & Infrastructure Solutions, Inc.), 2018. *Post-Construction Surface Sediment Monitoring Report—Year 3 Duwamish Sediment Other Area and Southwest Bank Corrective Measure and Habitat Project Boeing Plant 2, Seattle/Tukwila, Washington*. Prepared for The Boeing Company Seattle, Washington.

Wood; Ramboll; Floyd|Snider; Geosyntec Consultants; and Dalton, Olmsted & Fuglevand, Inc., 2019. *Year 1 Monitoring Report, Enhanced Natural Recovery/Activated Carbon Pilot Study, Lower Duwamish Waterway. Final*. Approved by EPA April 2019.

Wood; Ramboll; Floyd|Snider; Geosyntec Consultants; and Integral Consulting, 2021. *Year 3 Monitoring Report, Enhanced Natural Recovery/Activated Carbon Pilot Study, Lower Duwamish Waterway. Final*.

Maps

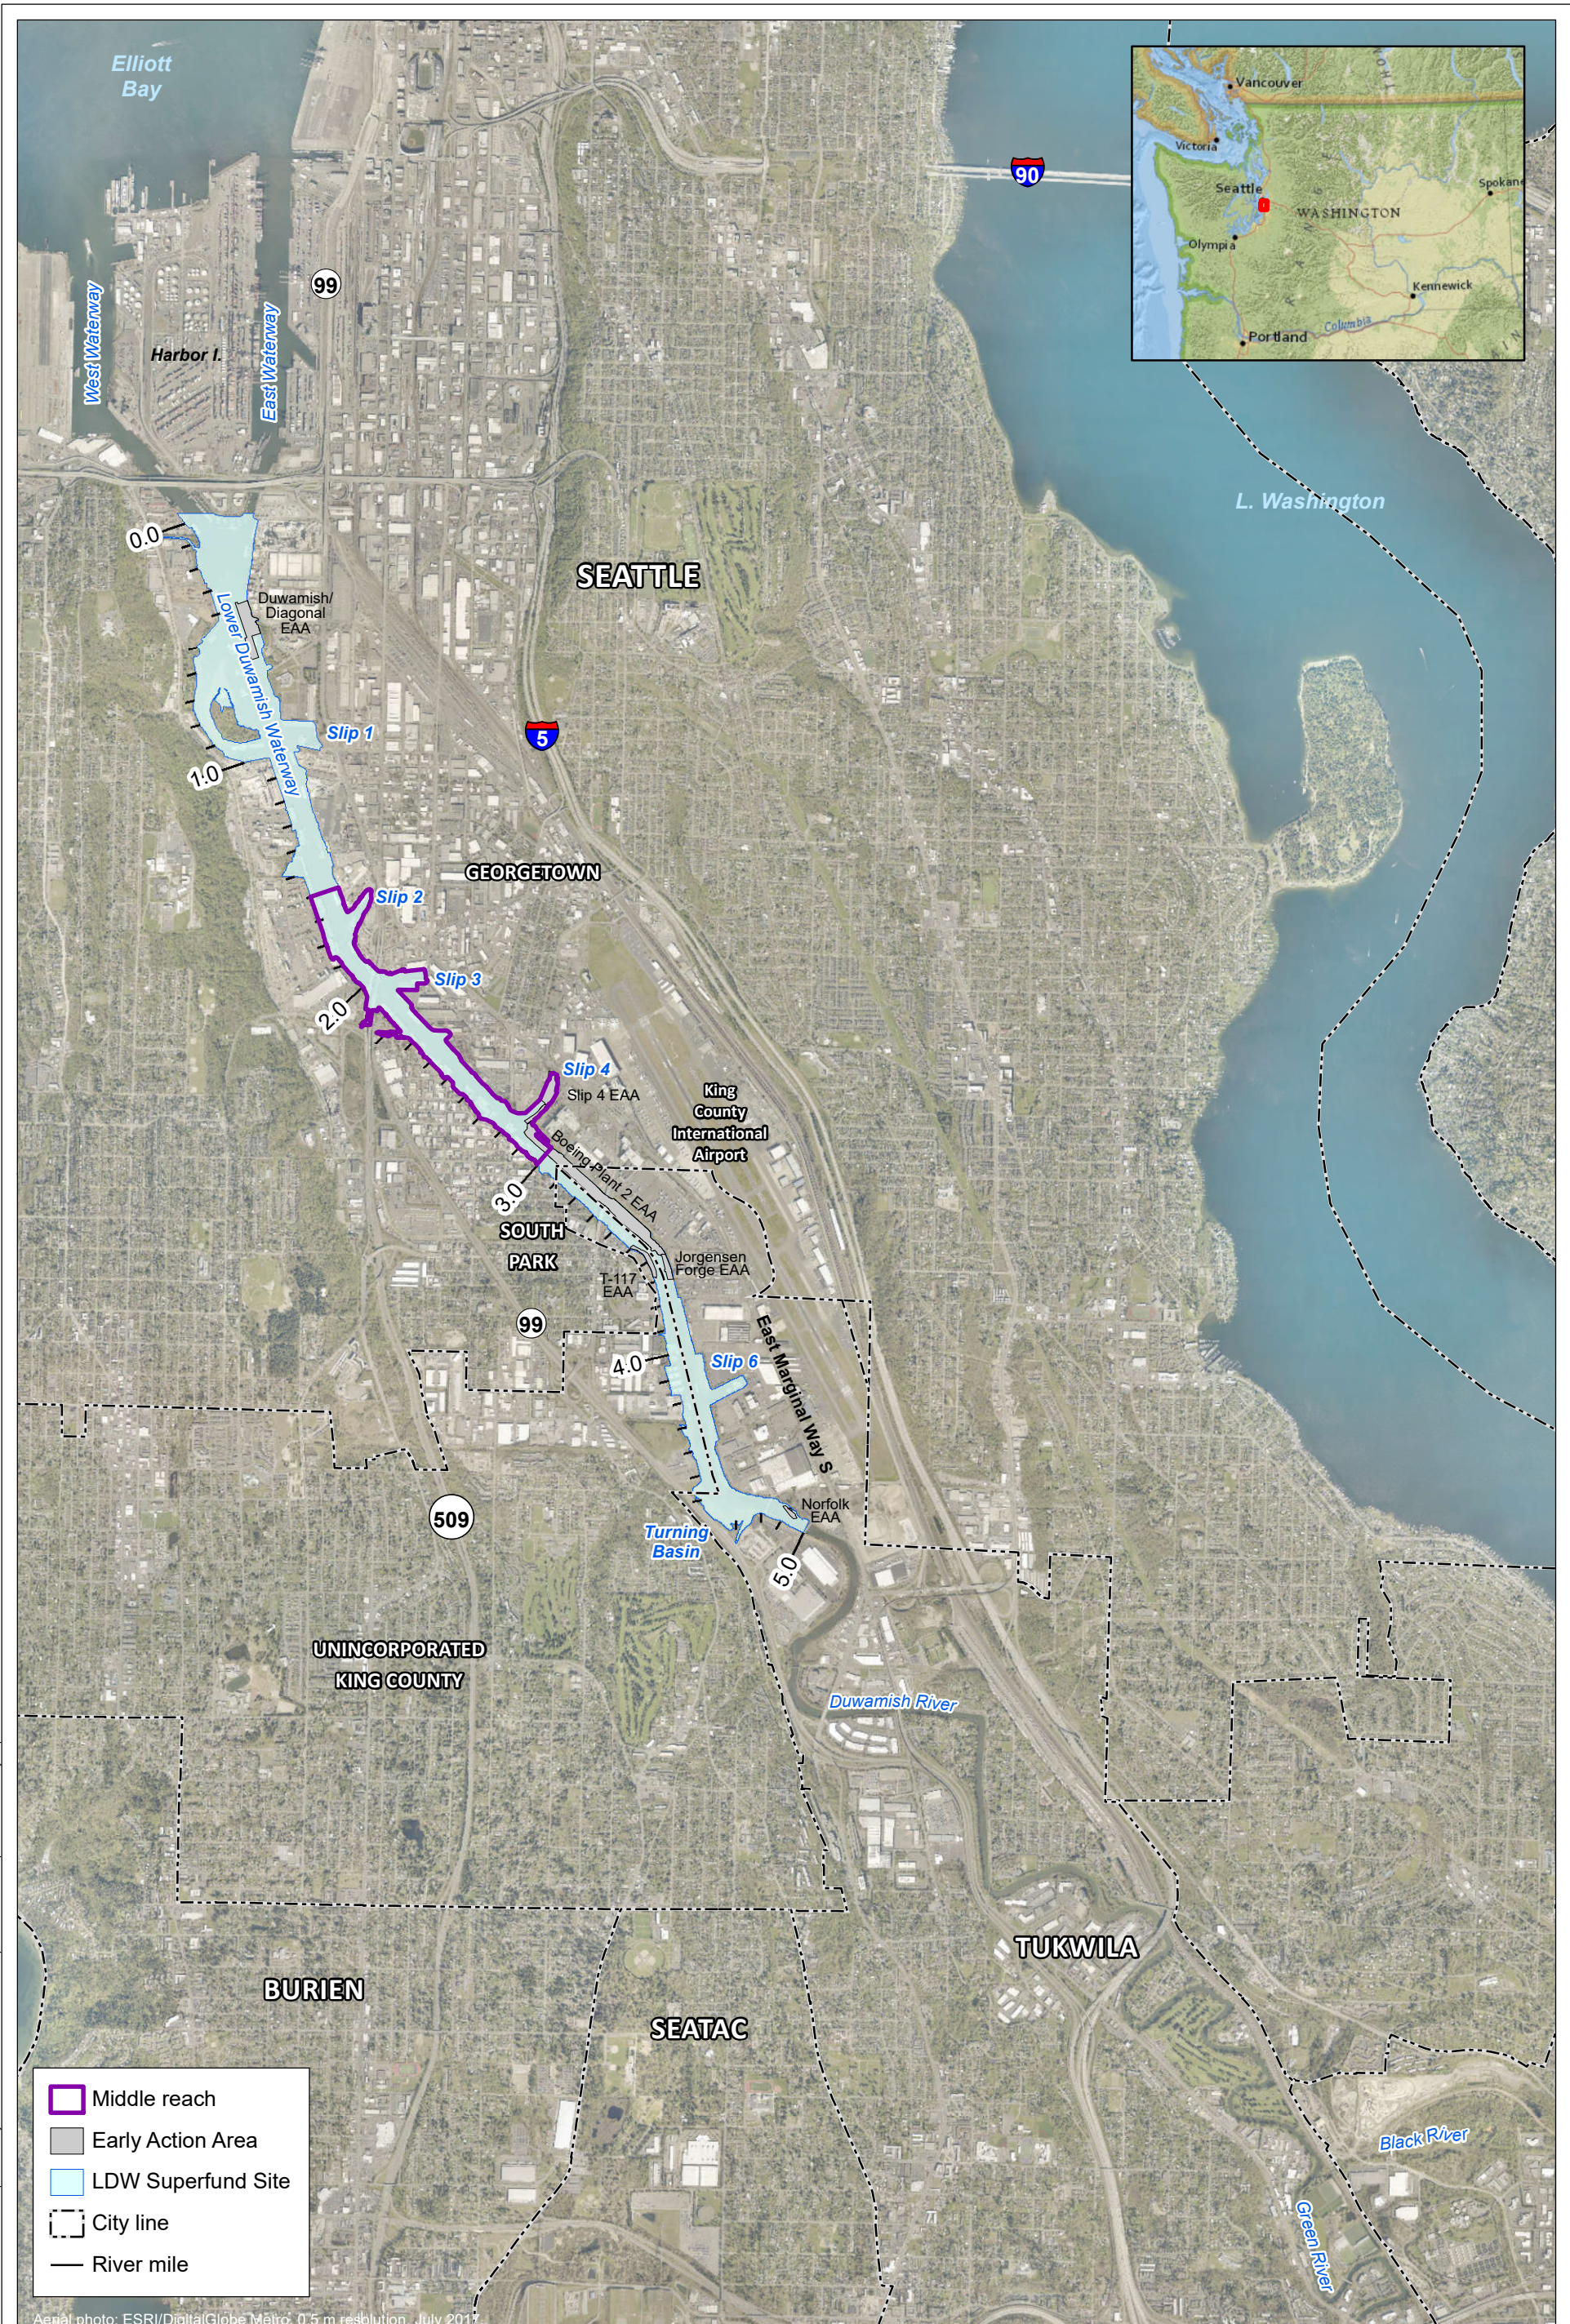

Middle reach
 Early Action Area
 LDW Superfund Site
 City line
 River mile

Aerial photo: ESRI/DigitalGlobe/Metro, 0.5 m resolution, July 2017





Lower Duwamish Waterway Group
 Port of Seattle / City of Seattle / King County / The Boeing Company


N
 0 0.5 1 Miles
 0 1 2 Kilometers

Map 1-1. LDW Superfund Site Vicinity Map
 REMEDIAL DESIGN WORK PLAN for LDW
 MIDDLE REACH DECEMBER 2, 2022

Prepared by craigh.11/30/22: W:\Projects\Duwamish AOC\GIS\Maps and Analyses\Phase 1\Work_Plan\RD_WP\Map 1-1 7-18 LDW Superfund Site Vicinity map.mxd

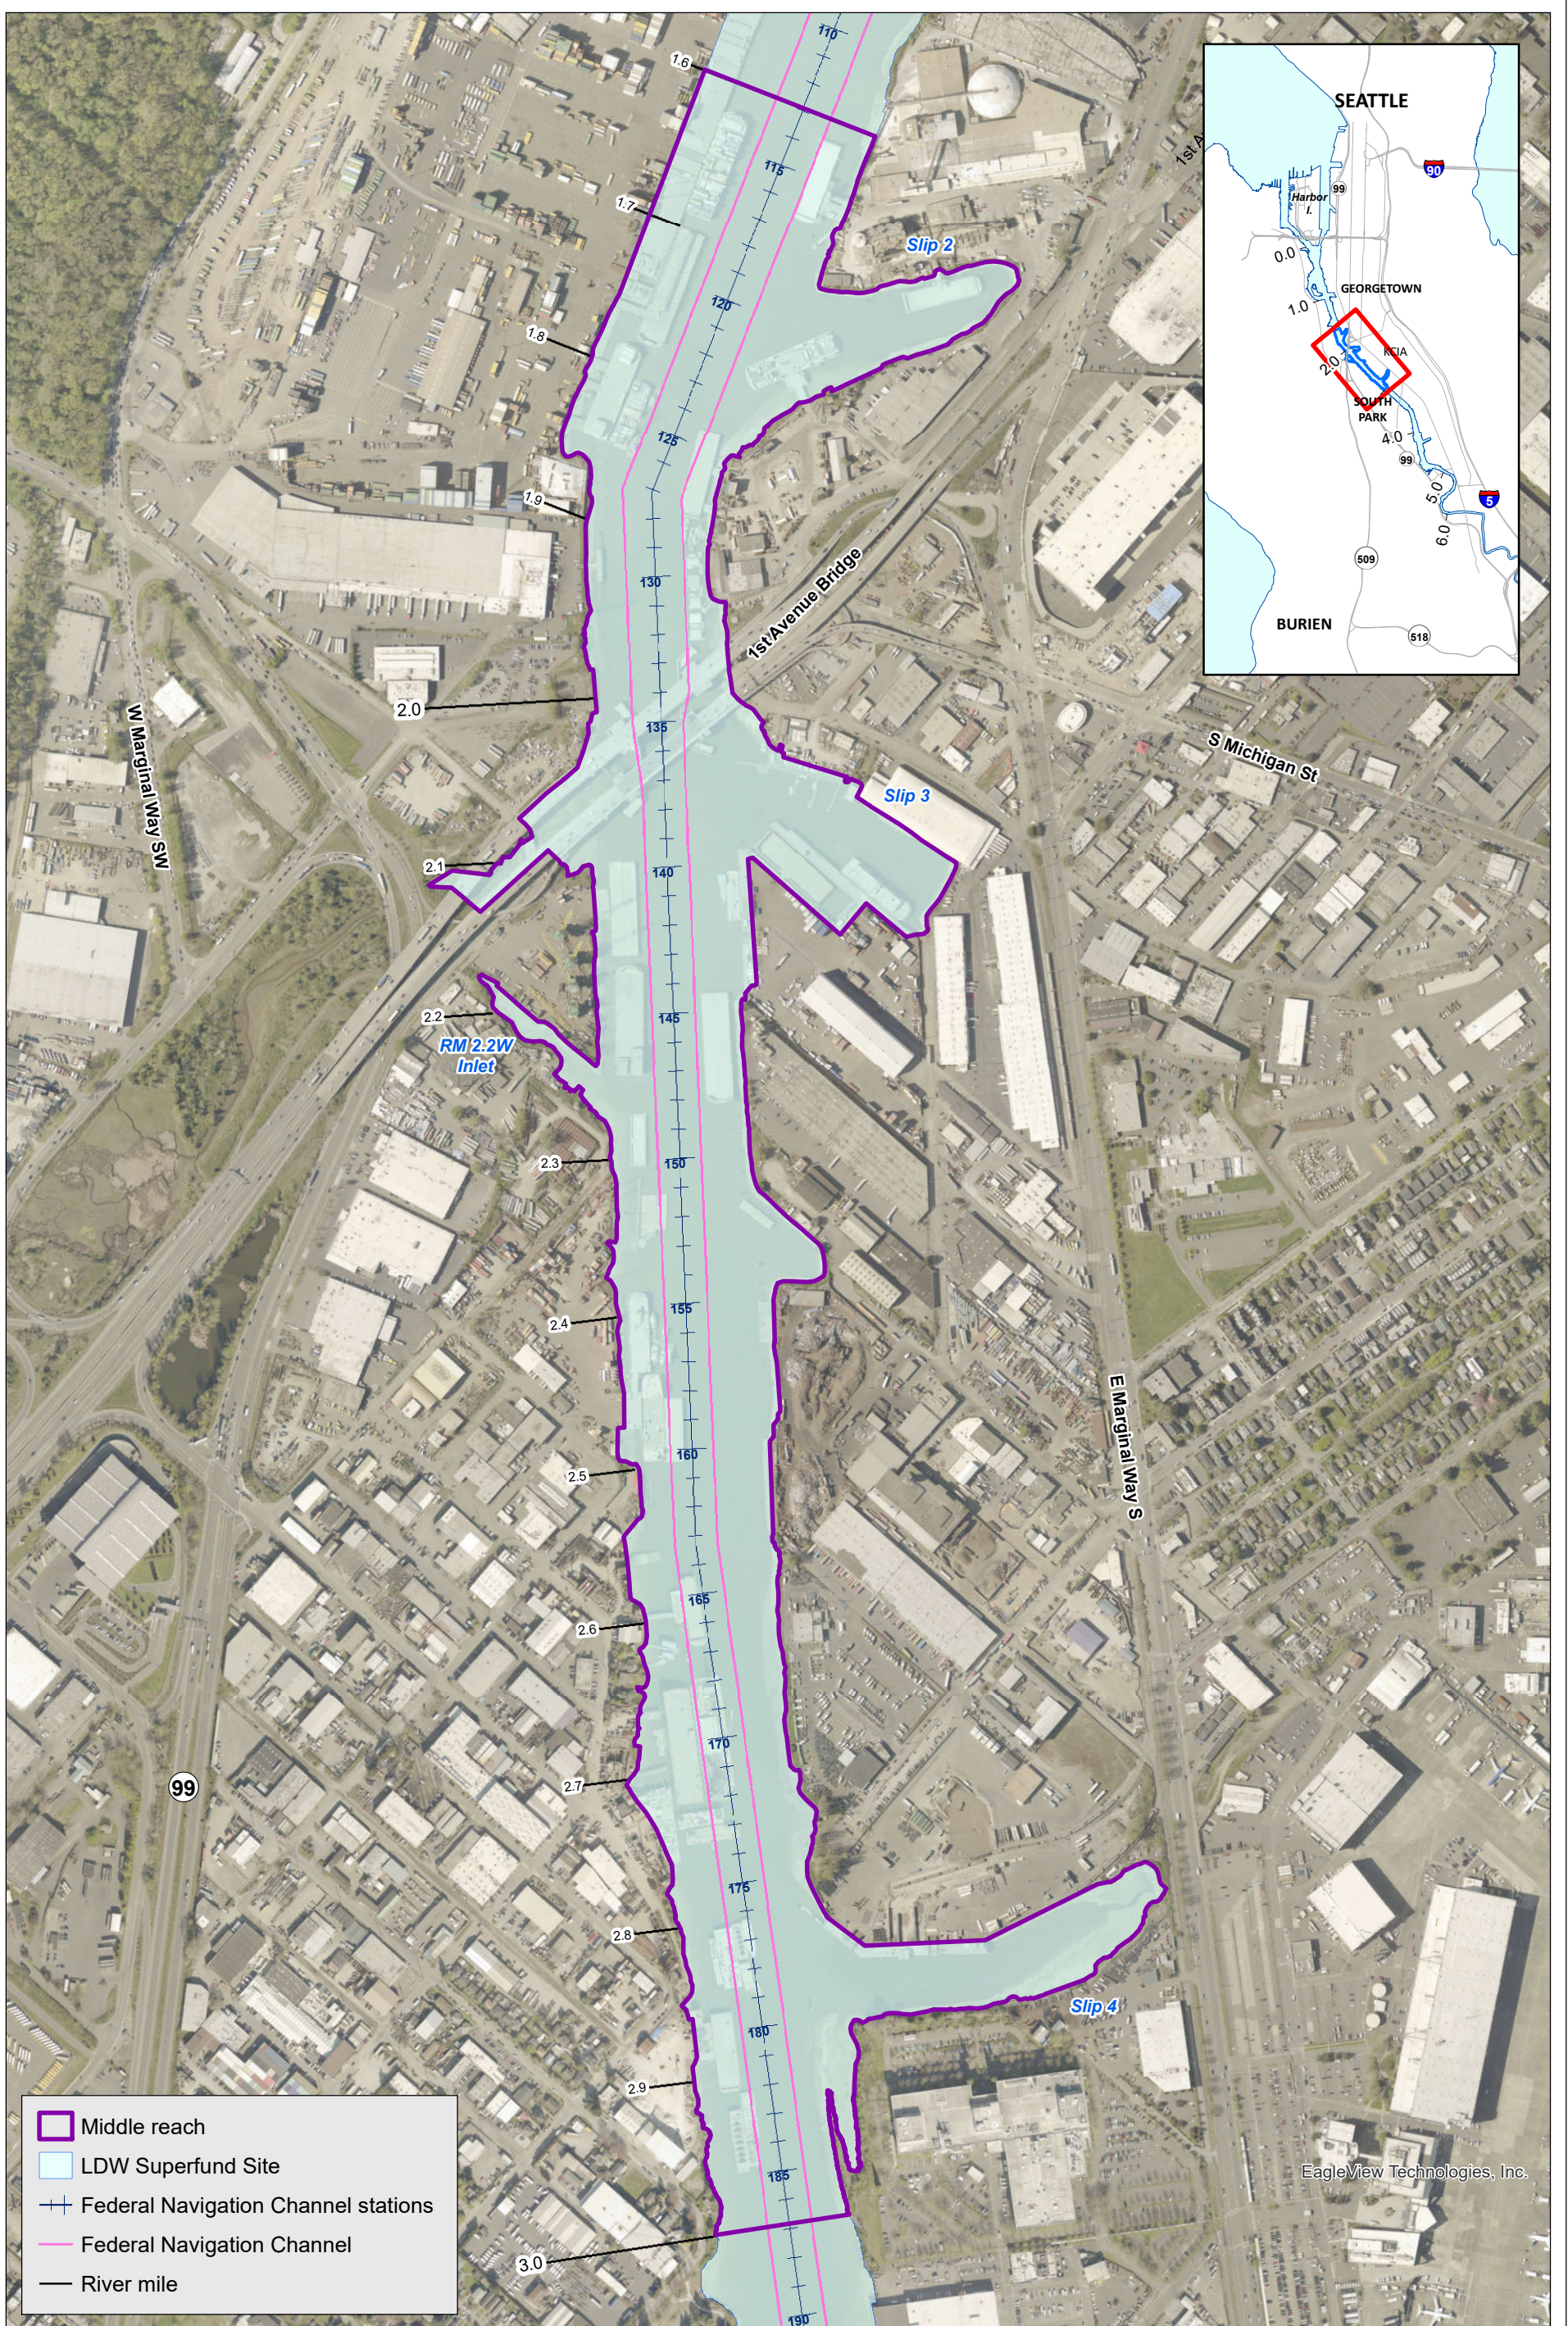


- Middle reach
- LDW Superfund Site
- + Federal Navigation Channel stations
- Federal Navigation Channel
- River mile





Prepared by craigh, 11/30/22: \\Projects\Duwamish AOC\GIS\Maps and Analysis\Phase 1\Work Plan\RD WPM\Map 1-2 7419 Middle Reach Vicinity Map.mxd

EagleView Technologies, Inc.

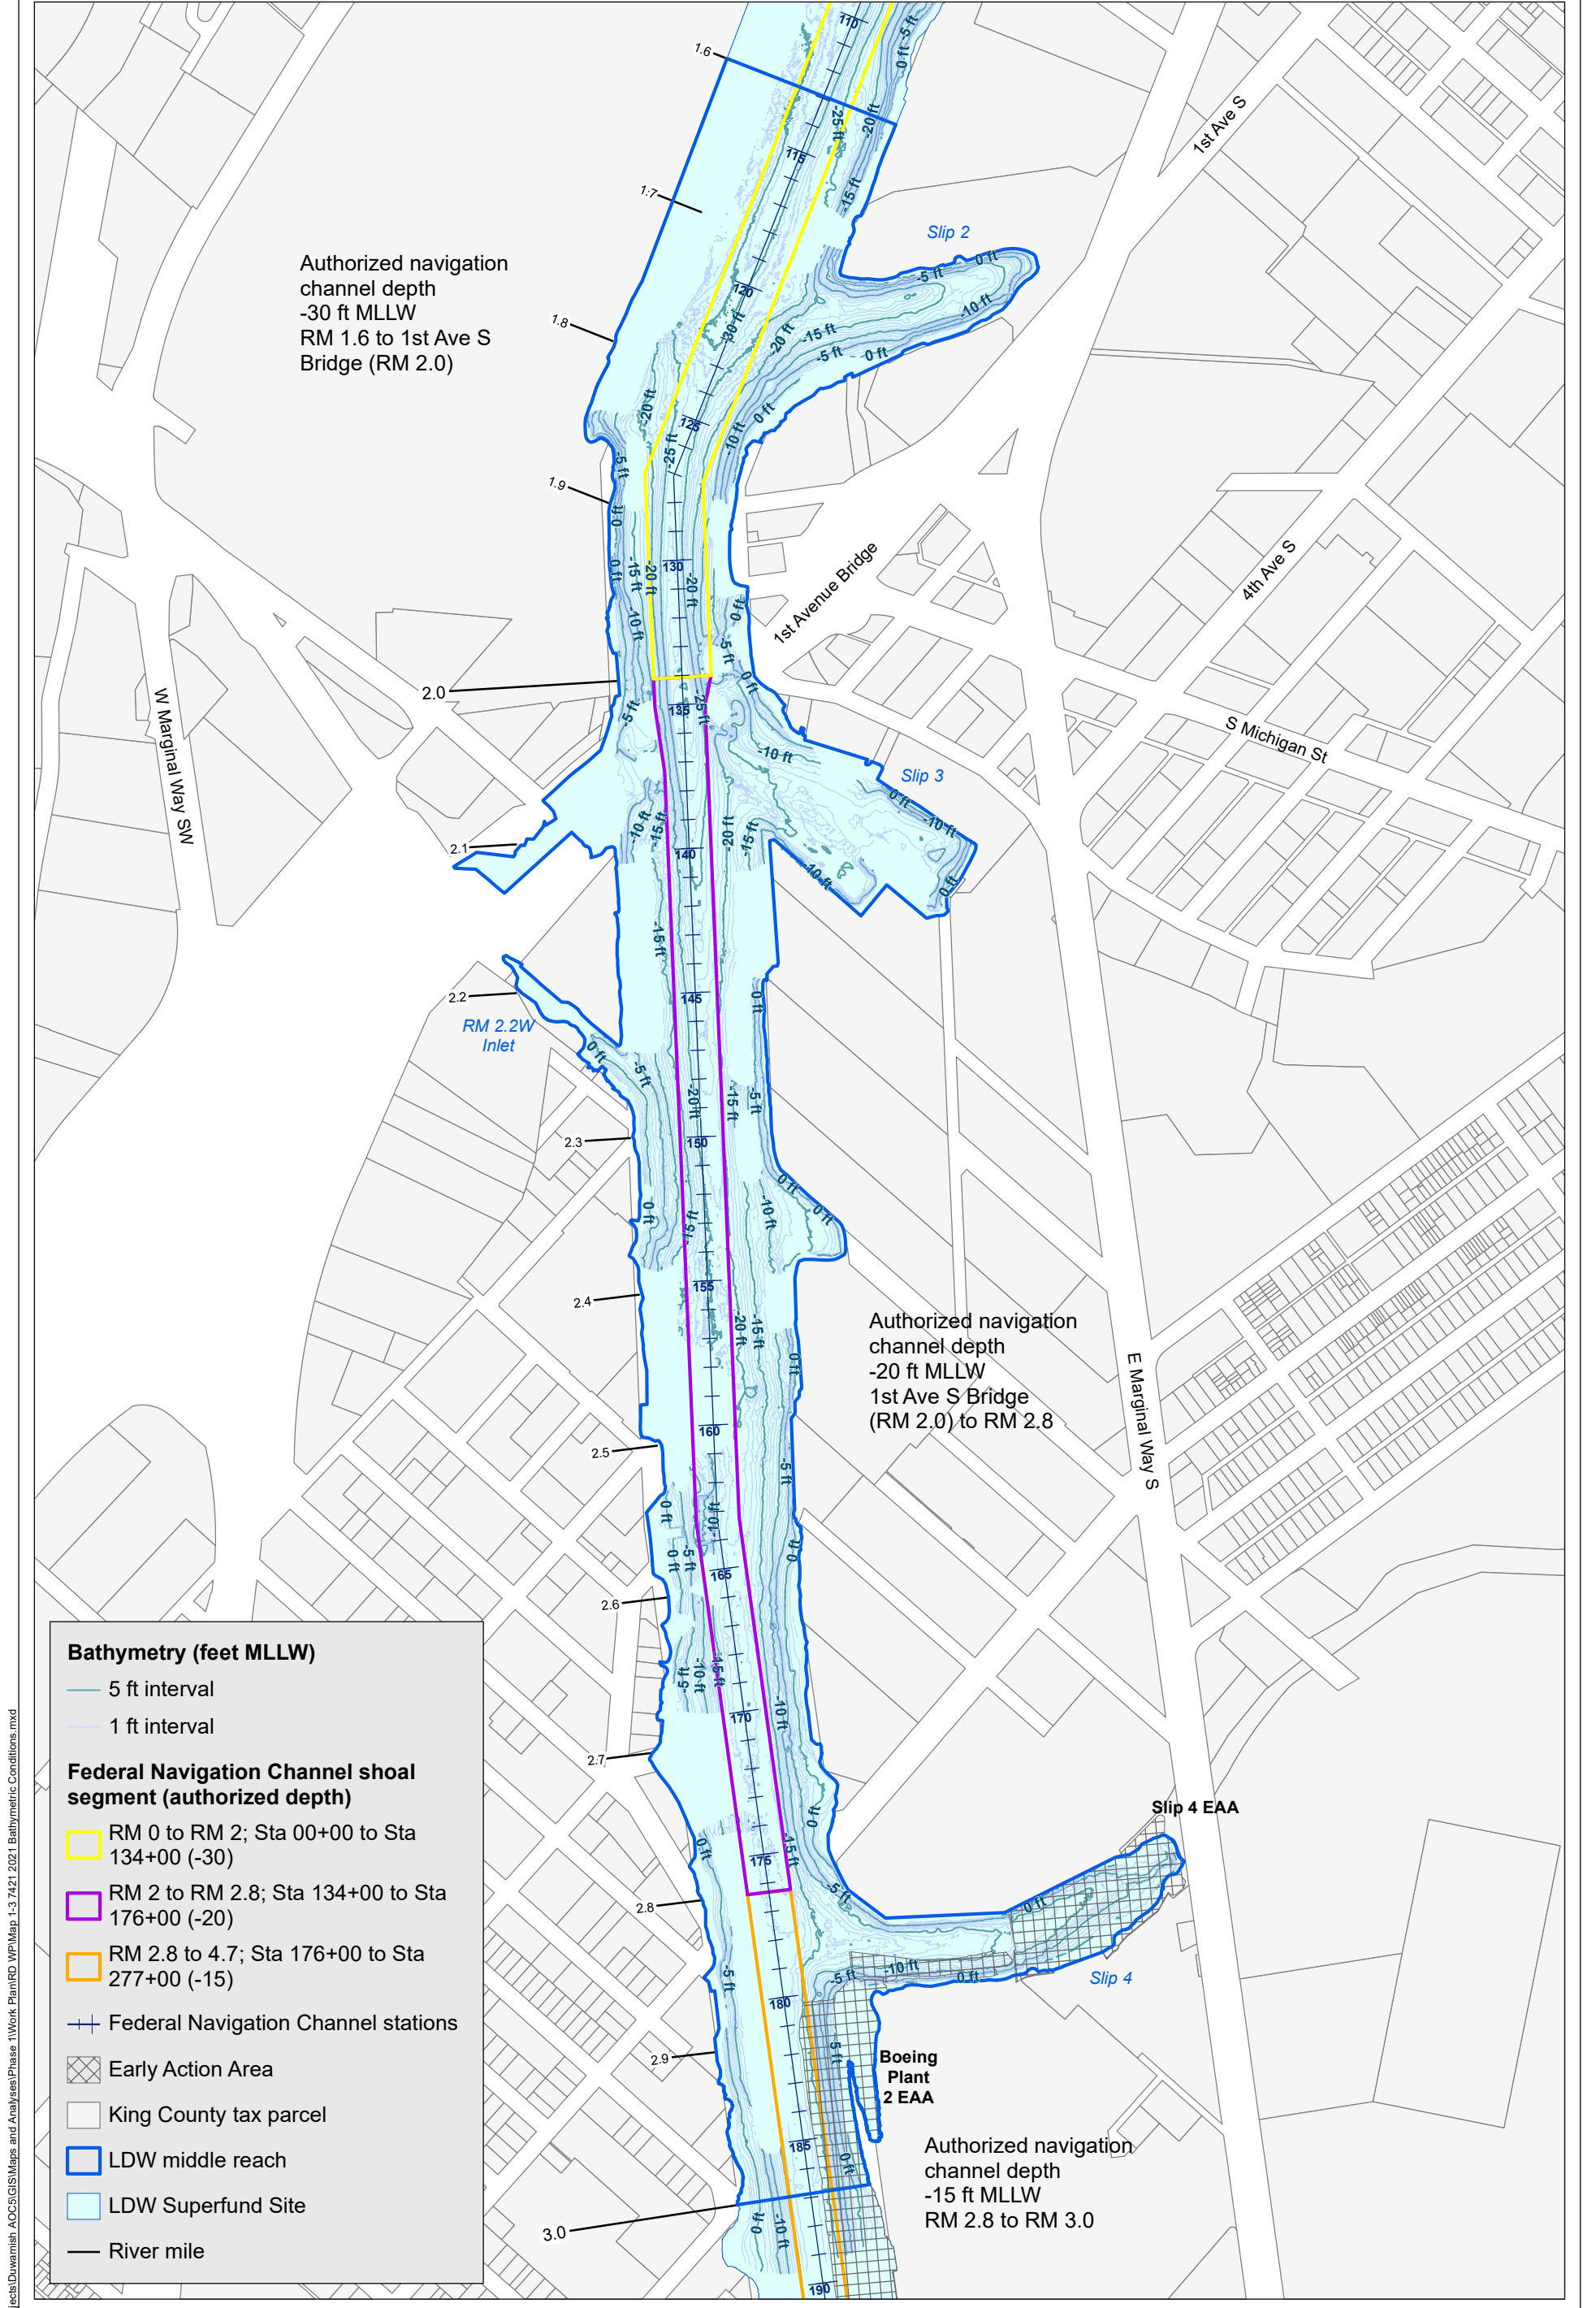

Prepared by craigh. 11/30/22. W:\Projects\Duwamish AOC\GIS\Maps and Analysis\Phase 1\Work_Plan\RD_WP\Map_1-3_7421_2021_Bathymetric_Conditions.mxd




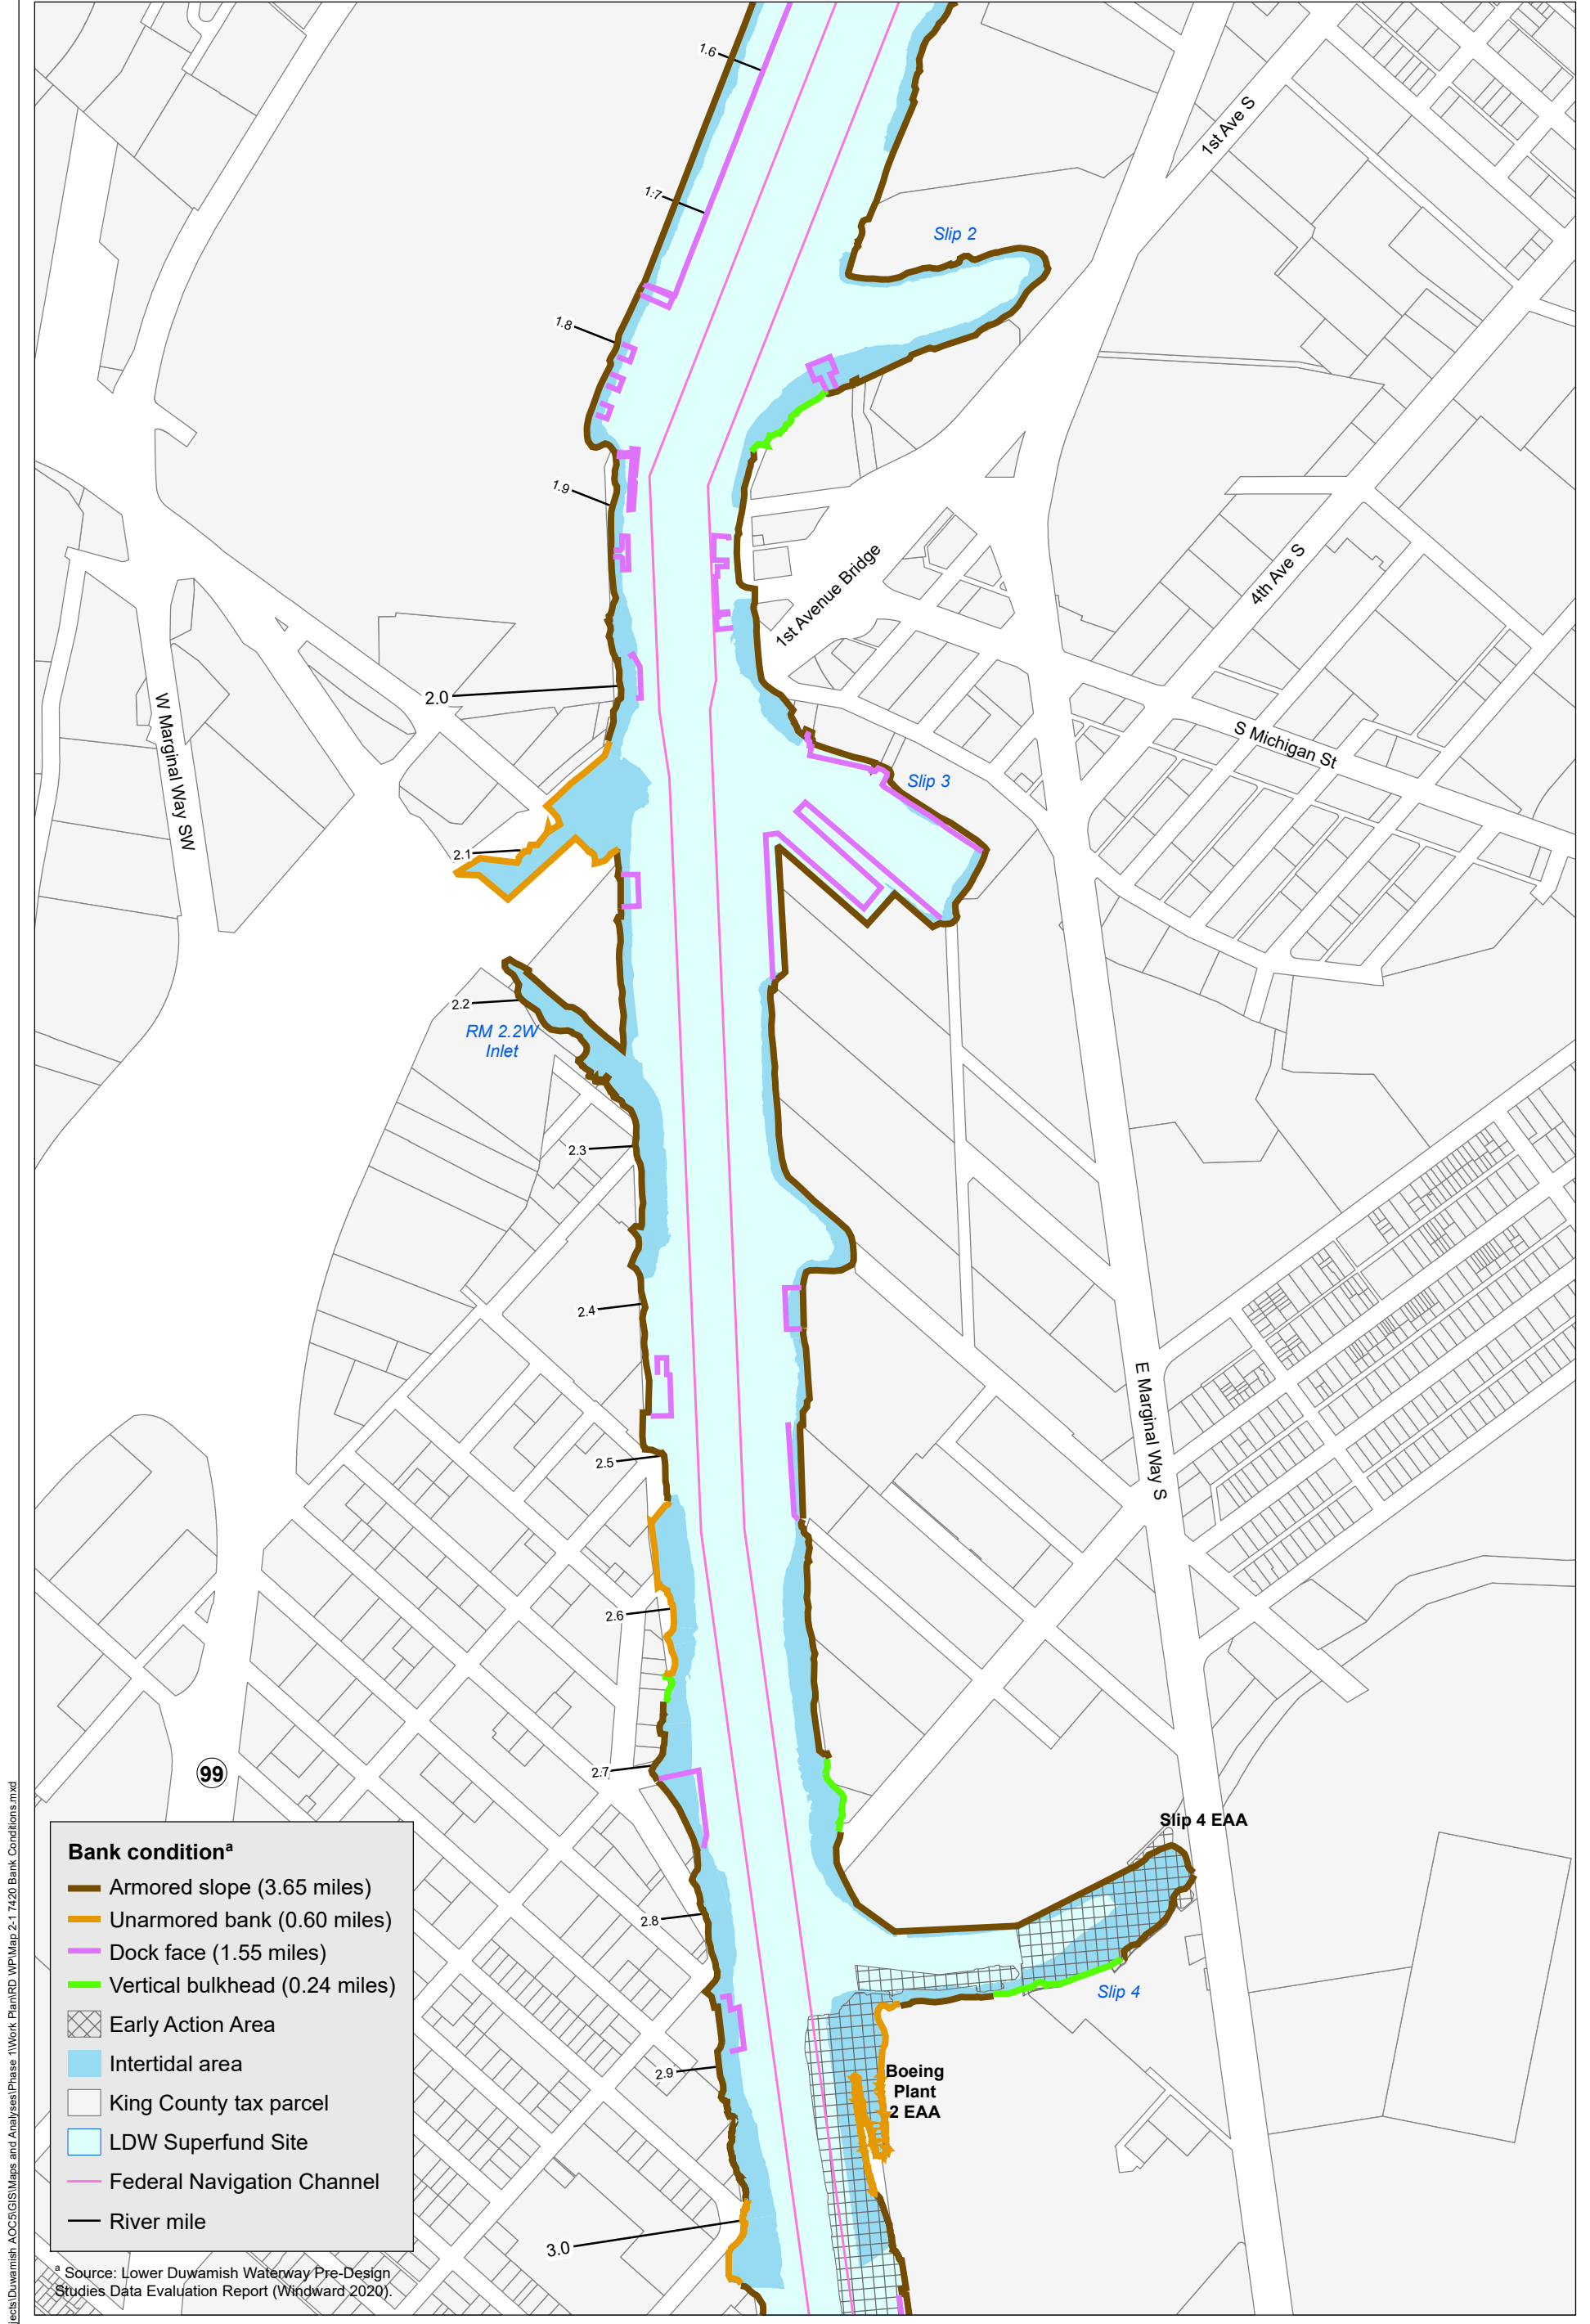

Prepared by craigh_11/30/22: W:\Projects\Duwamish AOC\GIS\Maps and Analyses\Phase 1\Work_Plan\RD_WP\Map 2-1 7420 Bank Conditions.mxd




Lower Duwamish Waterway Group
 Port of Seattle / City of Seattle / King County / The Boeing Company



Map 2-1. Bank Conditions


REMEDIAL DESIGN WORK PLAN for LDW
 MIDDLE REACH
 DECEMBER 2, 2022

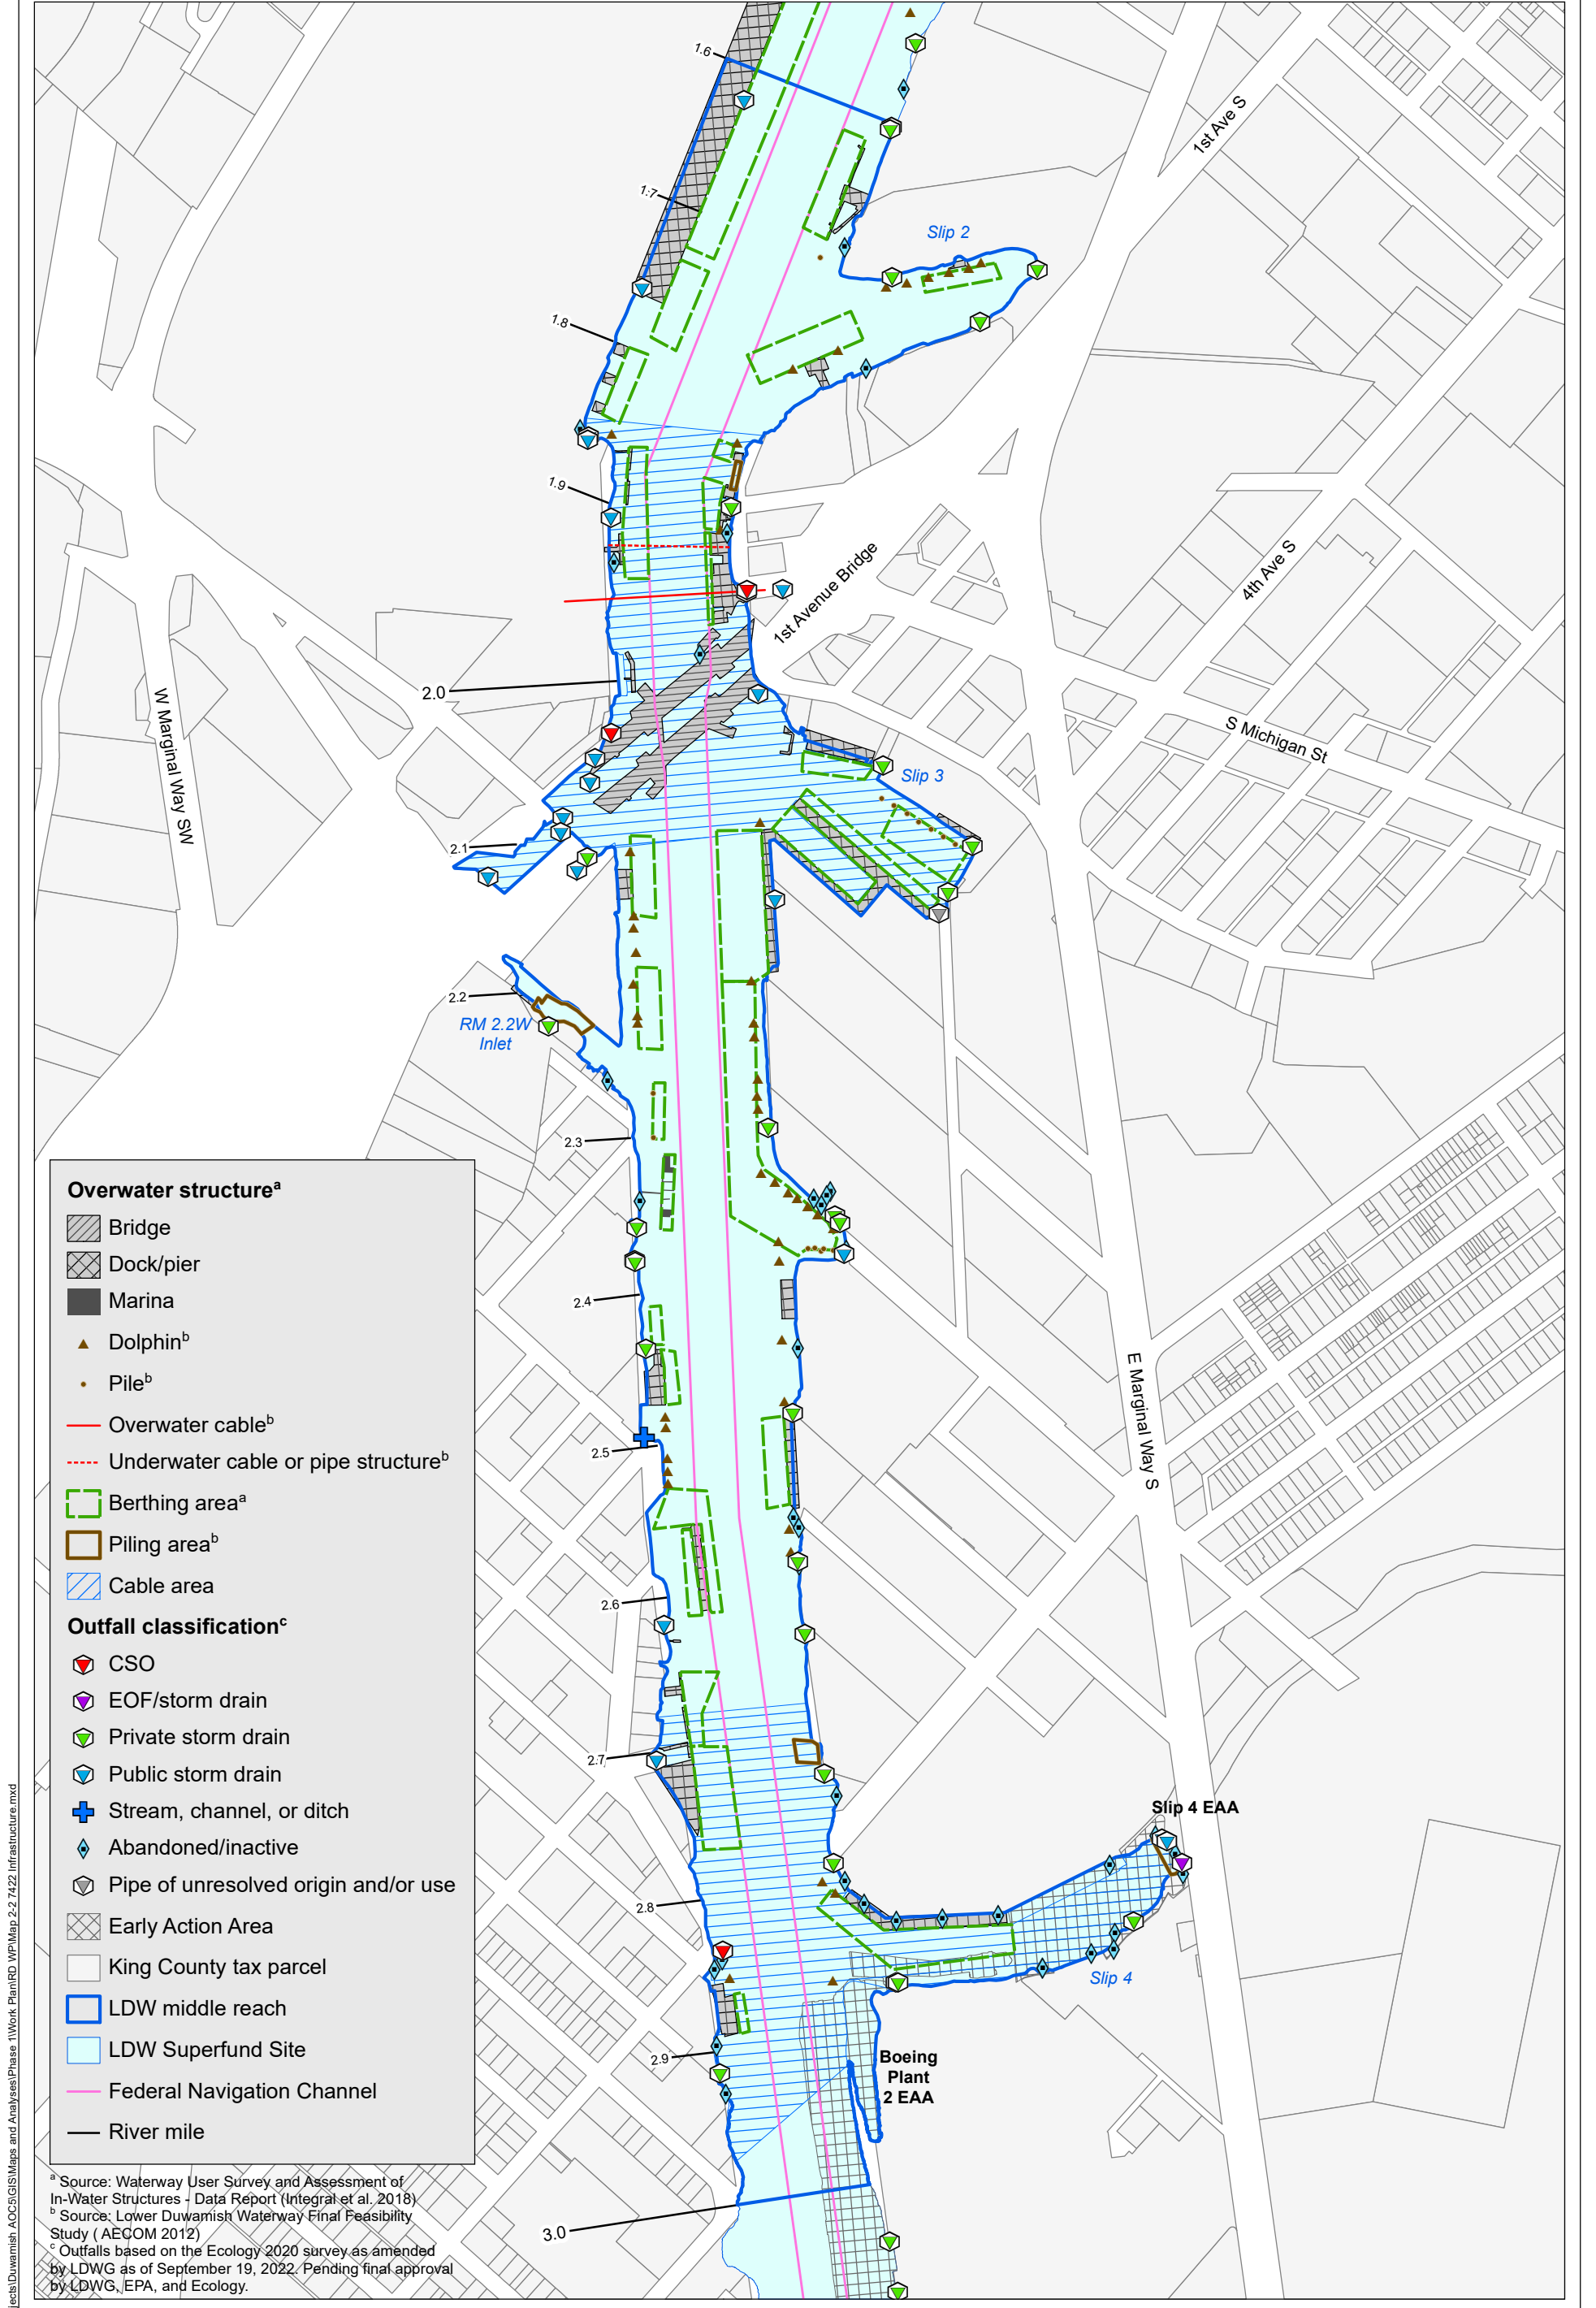


- Overwater structure^a**
- Bridge
 - Dock/pier
 - Marina
 - Dolphin^b
 - Pile^b
 - Overwater cable^b
 - Underwater cable or pipe structure^b
 - Berthing area^a
 - Piling area^b
 - Cable area
- Outfall classification^c**
- CSO
 - EOF/storm drain
 - Private storm drain
 - Public storm drain
 - Stream, channel, or ditch
 - Abandoned/inactive
 - Pipe of unresolved origin and/or use
 - Early Action Area
 - King County tax parcel
 - LDW middle reach
 - LDW Superfund Site
 - Federal Navigation Channel
 - River mile

^a Source: Waterway User Survey and Assessment of In-Water Structures - Data Report (Integral et al, 2018)
^b Source: Lower Duwamish Waterway Final Feasibility Study (AEGOM 2012)
^c Outfalls based on the Ecology 2020 survey as amended by LDWG as of September 19, 2022. Pending final approval by LDWG, EPA, and Ecology.

Prepared by craigh_11/30/22: W:\Projects\Duwamish AOC\GIS\Maps and Analyses\Phase 1\Work_Plan\RD_WP\Map 2-2 7422 Infrastructure.mxd




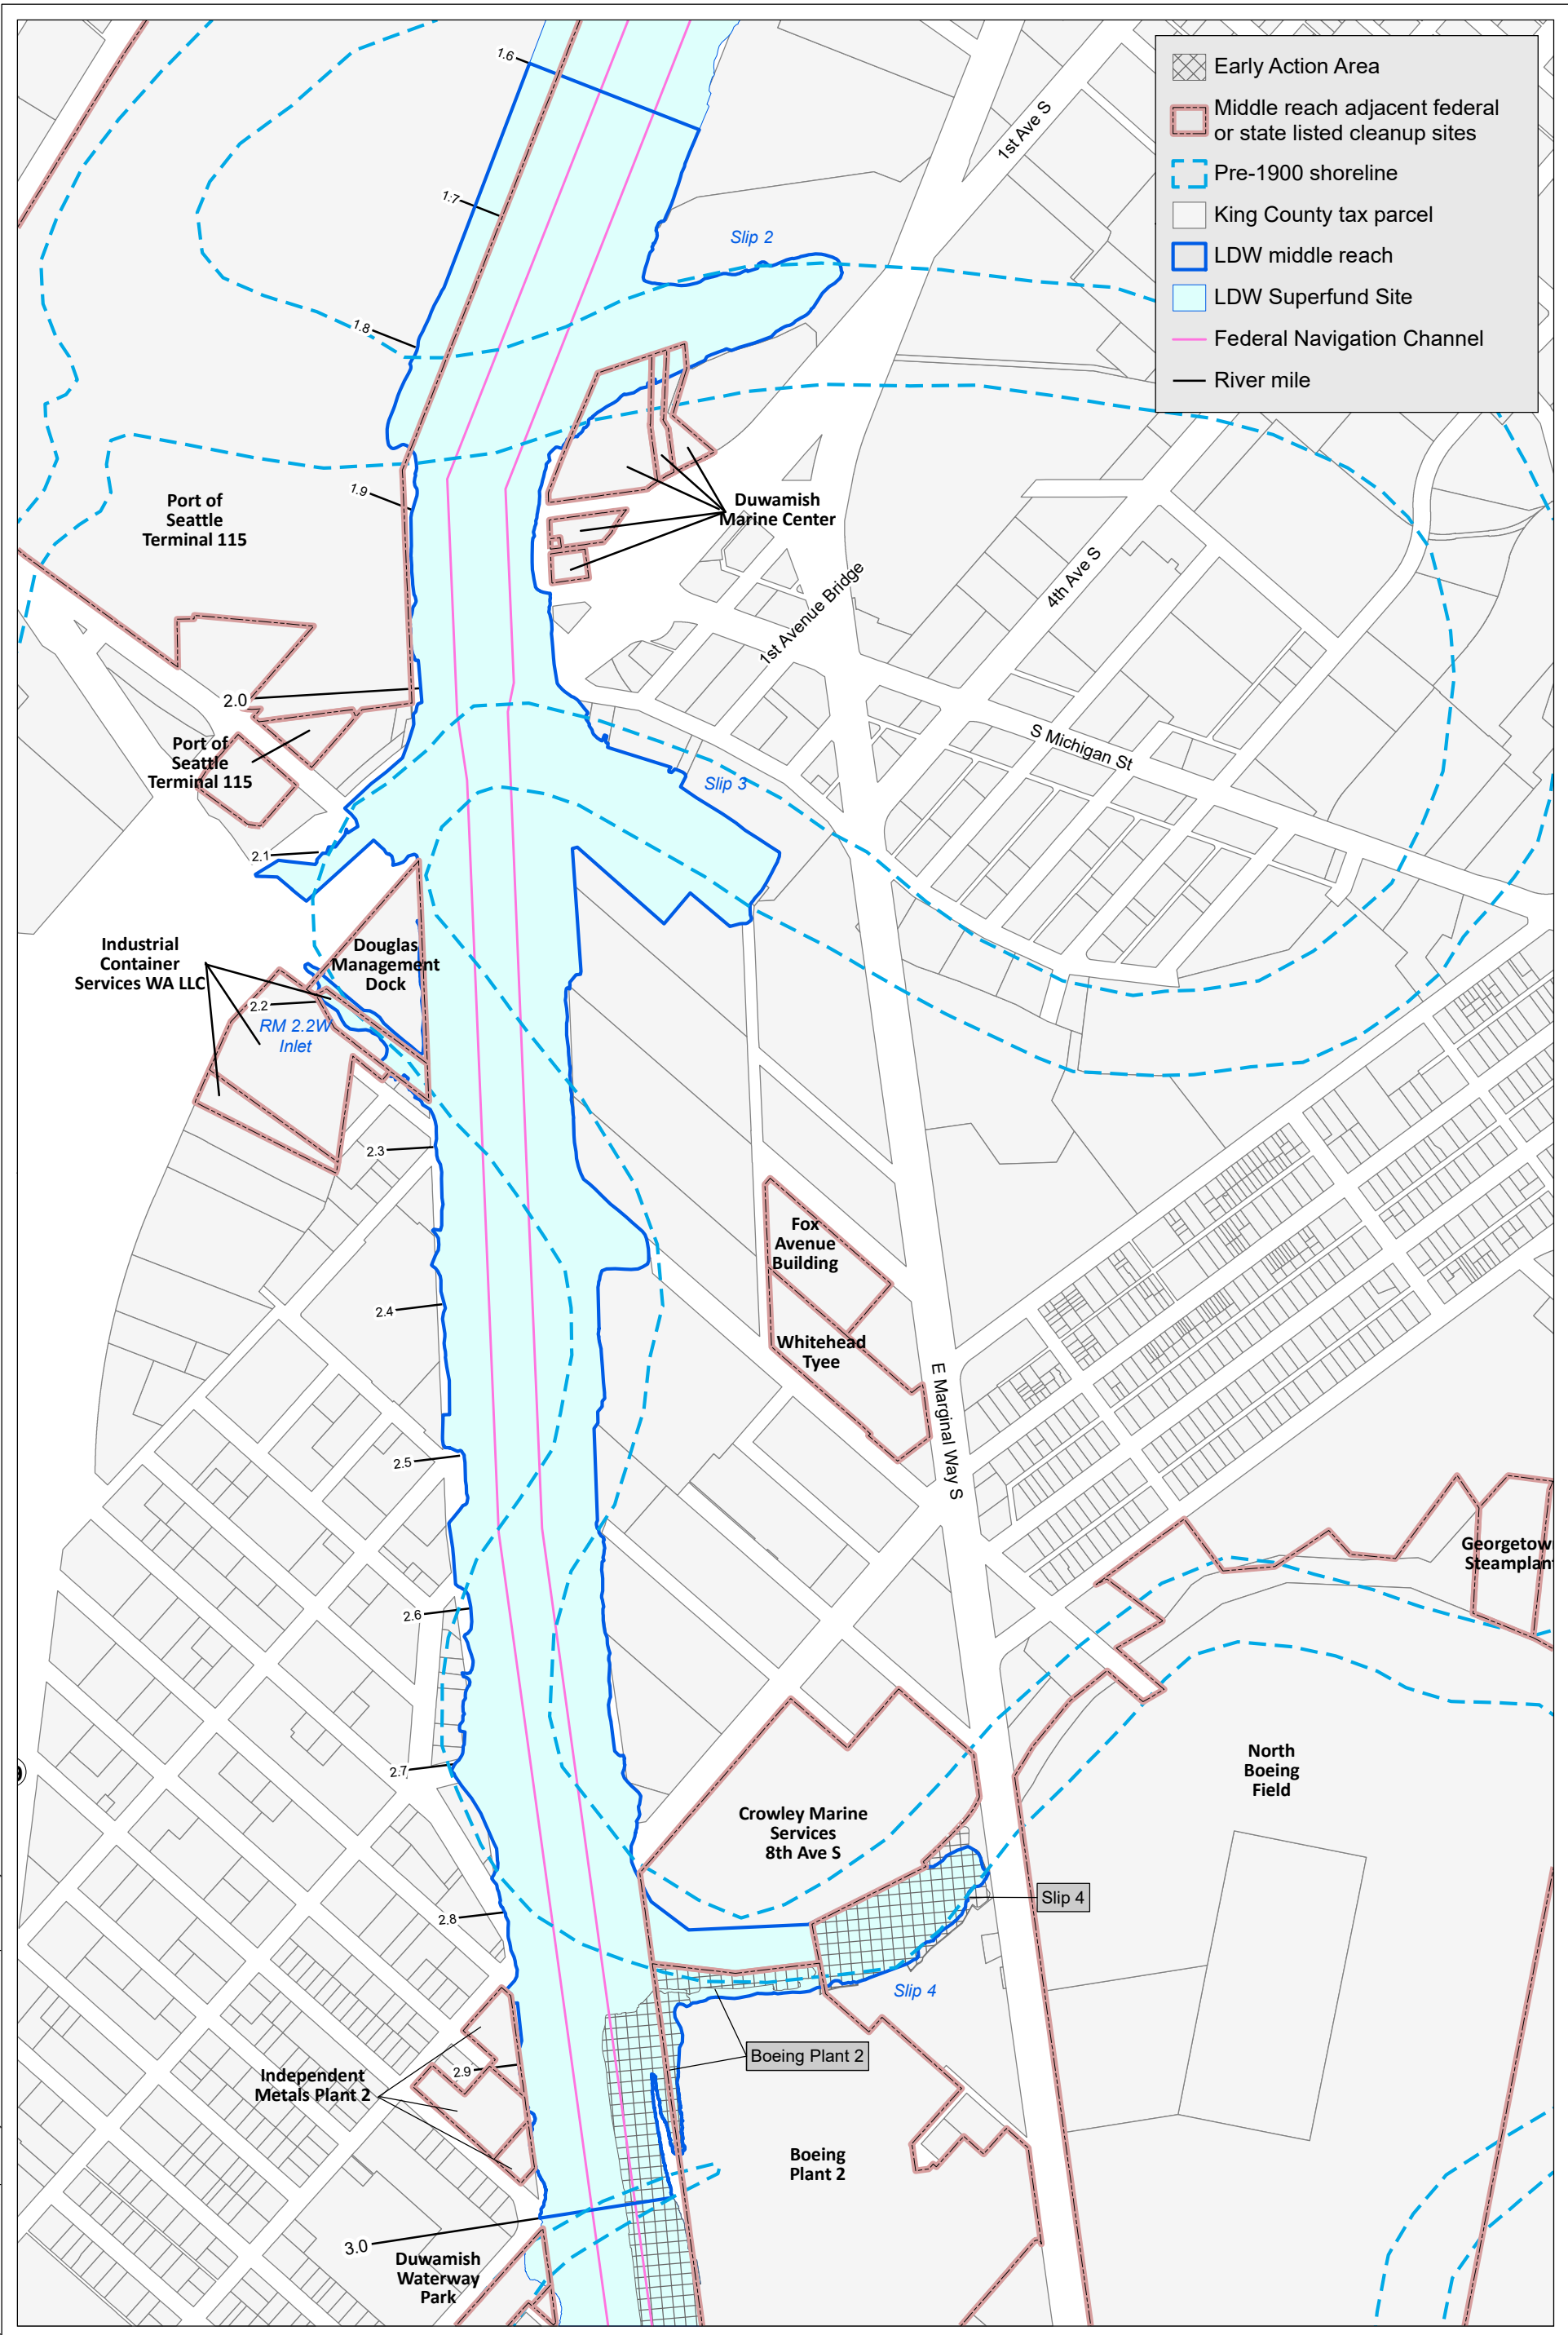

Prepared by craigh, 11/30/22: W:\Projects\Duwamish AOC\GIS\Maps and Analyses\Phase 1\Work_Plan\RD_WP\Map 2-3 7425 Early Action Areas and Other Listed Sites.mxd




Lower Duwamish Waterway Group
 Port of Seattle / City of Seattle / King County / The Boeing Company



Map 2-3. Early Action Areas and Upland Listed Cleanup Sites

REMEDIAL DESIGN WORK PLAN for LDW
 MIDDLE REACH
 DECEMBER 2, 2022

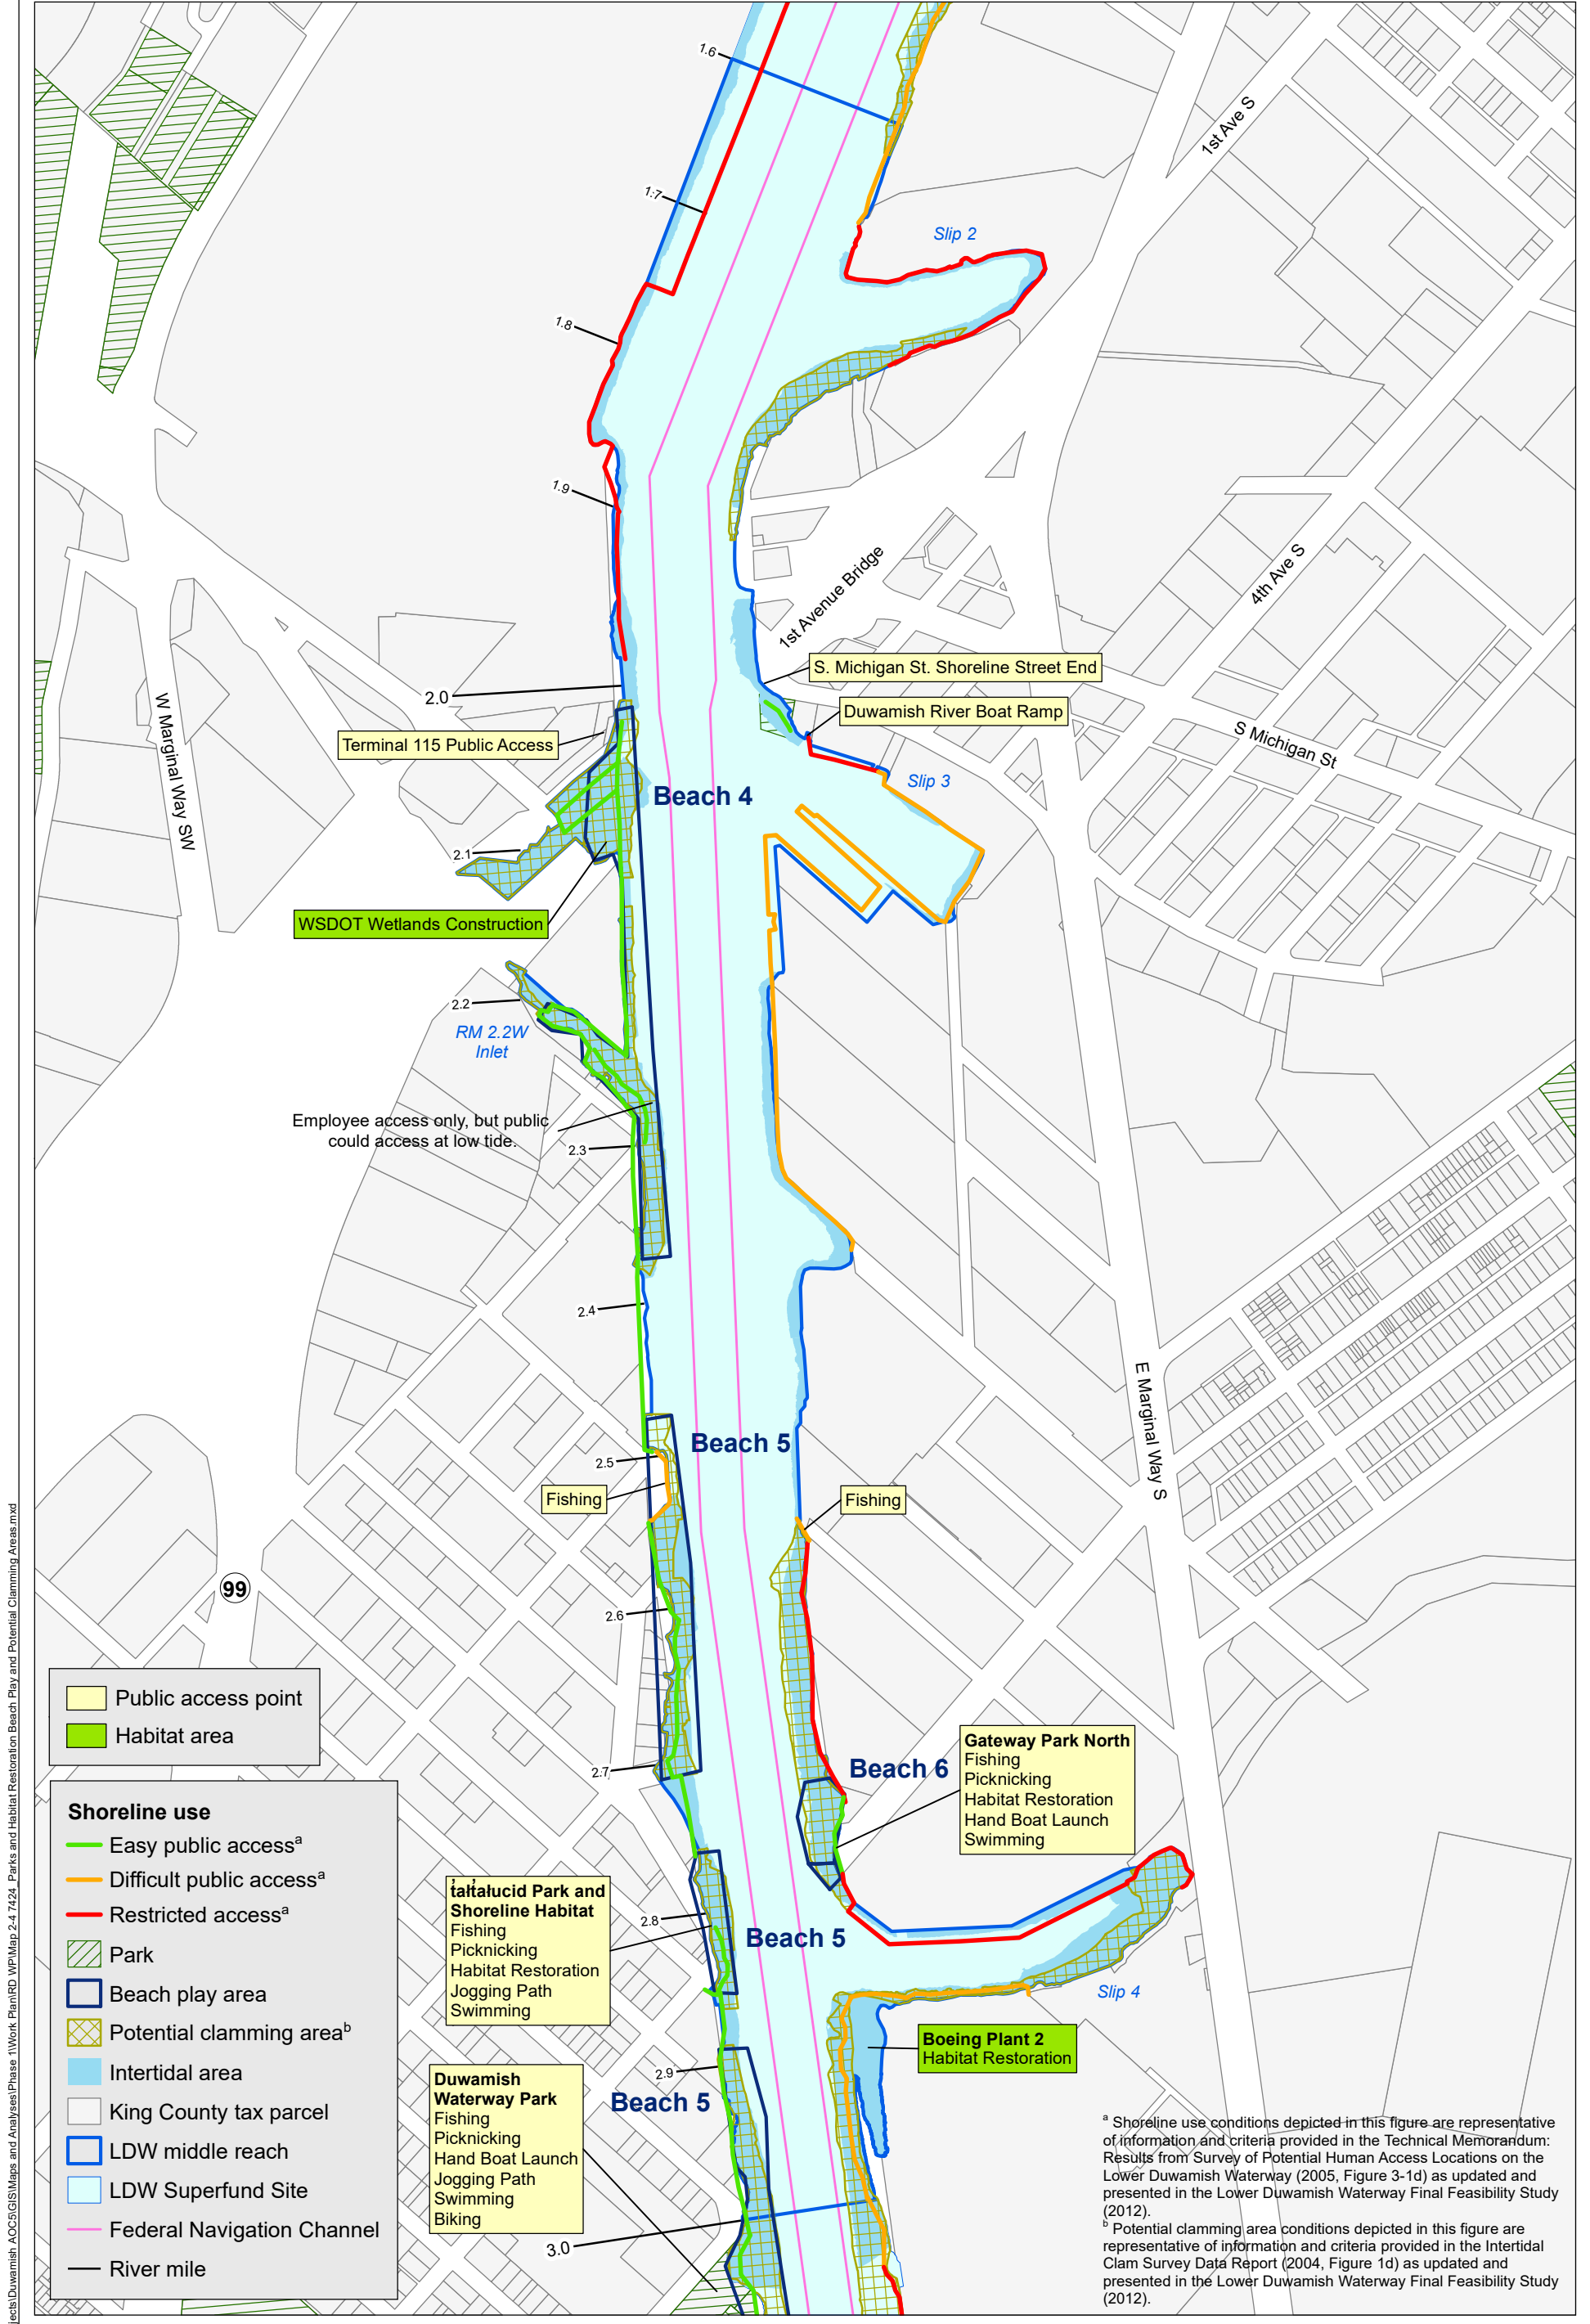

Prepared by craigh, 11/30/22, W:\Projects\Duwamish AOC\GIS\Maps and Analyses\Phase 1\Work Plans\RD WPM\Map 2-4 7424 Parks and Habitat Restoration Beach Play and Potential Clamming Areas.mxd

